



Status as of 31 May 20


- ◆ Milestone
- Planned Bar
- Critical Activity
- ◆ Progress Milestone
- Progress Bar
- ▶ Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu

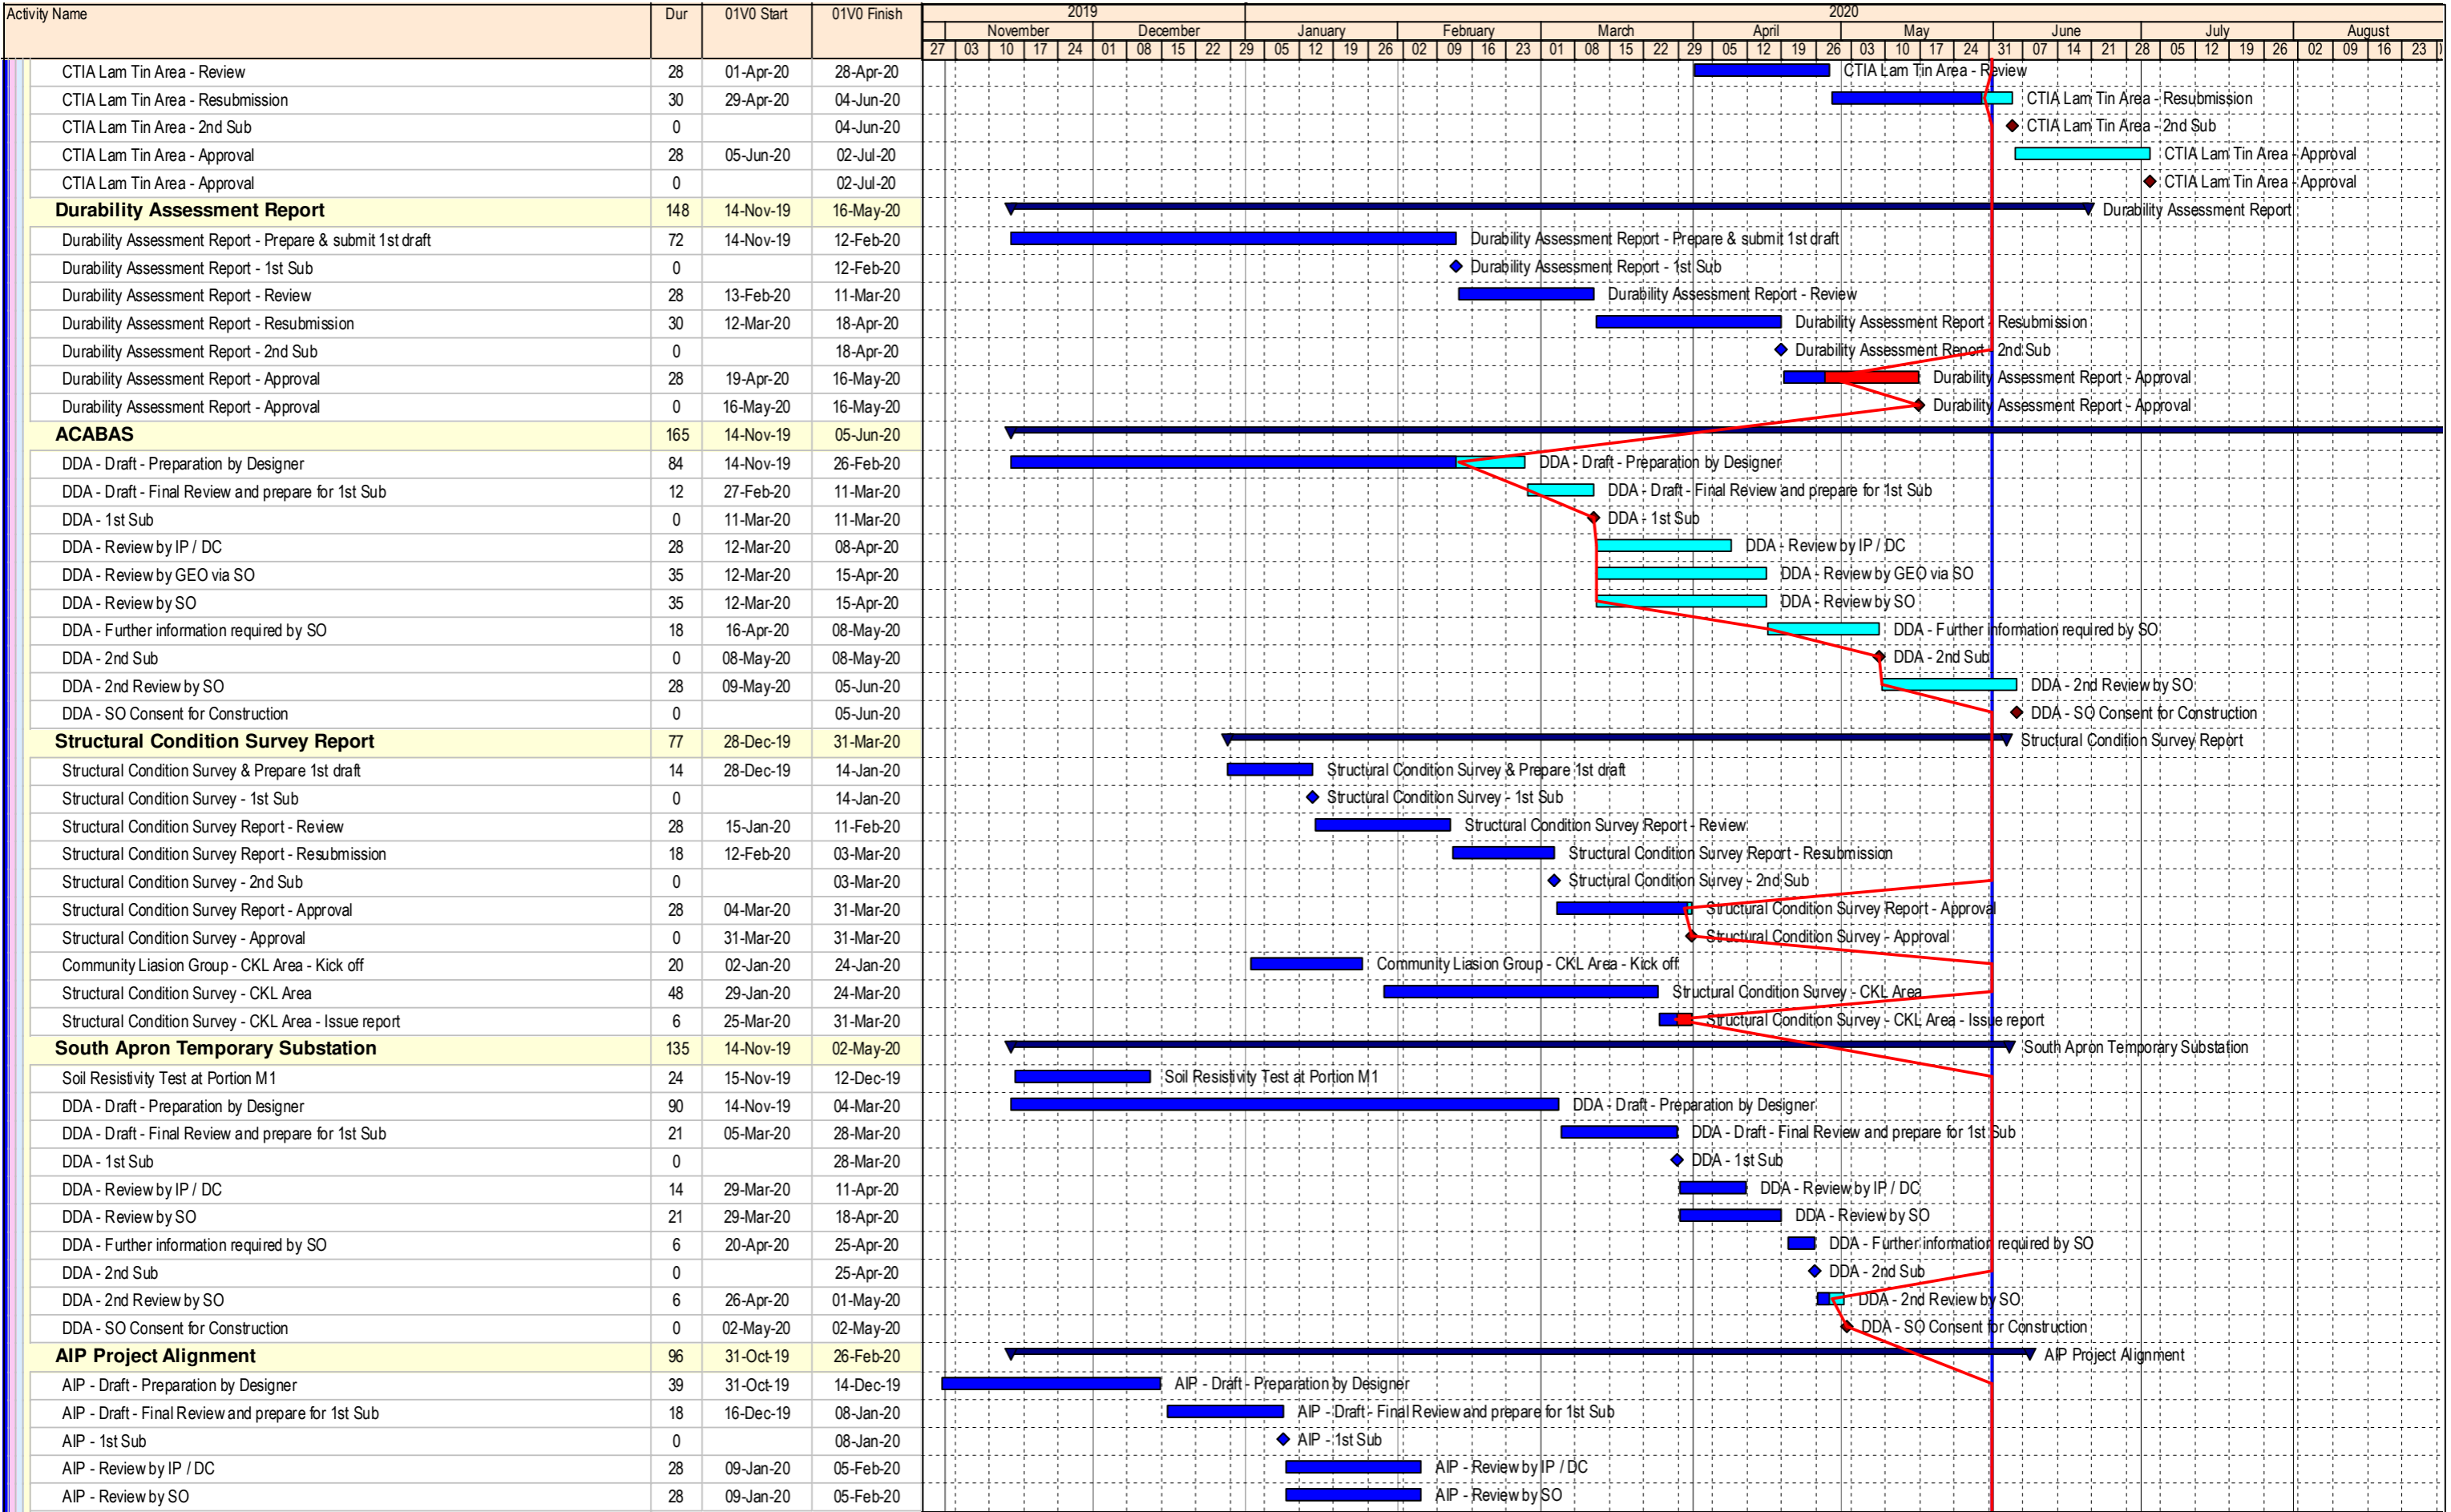

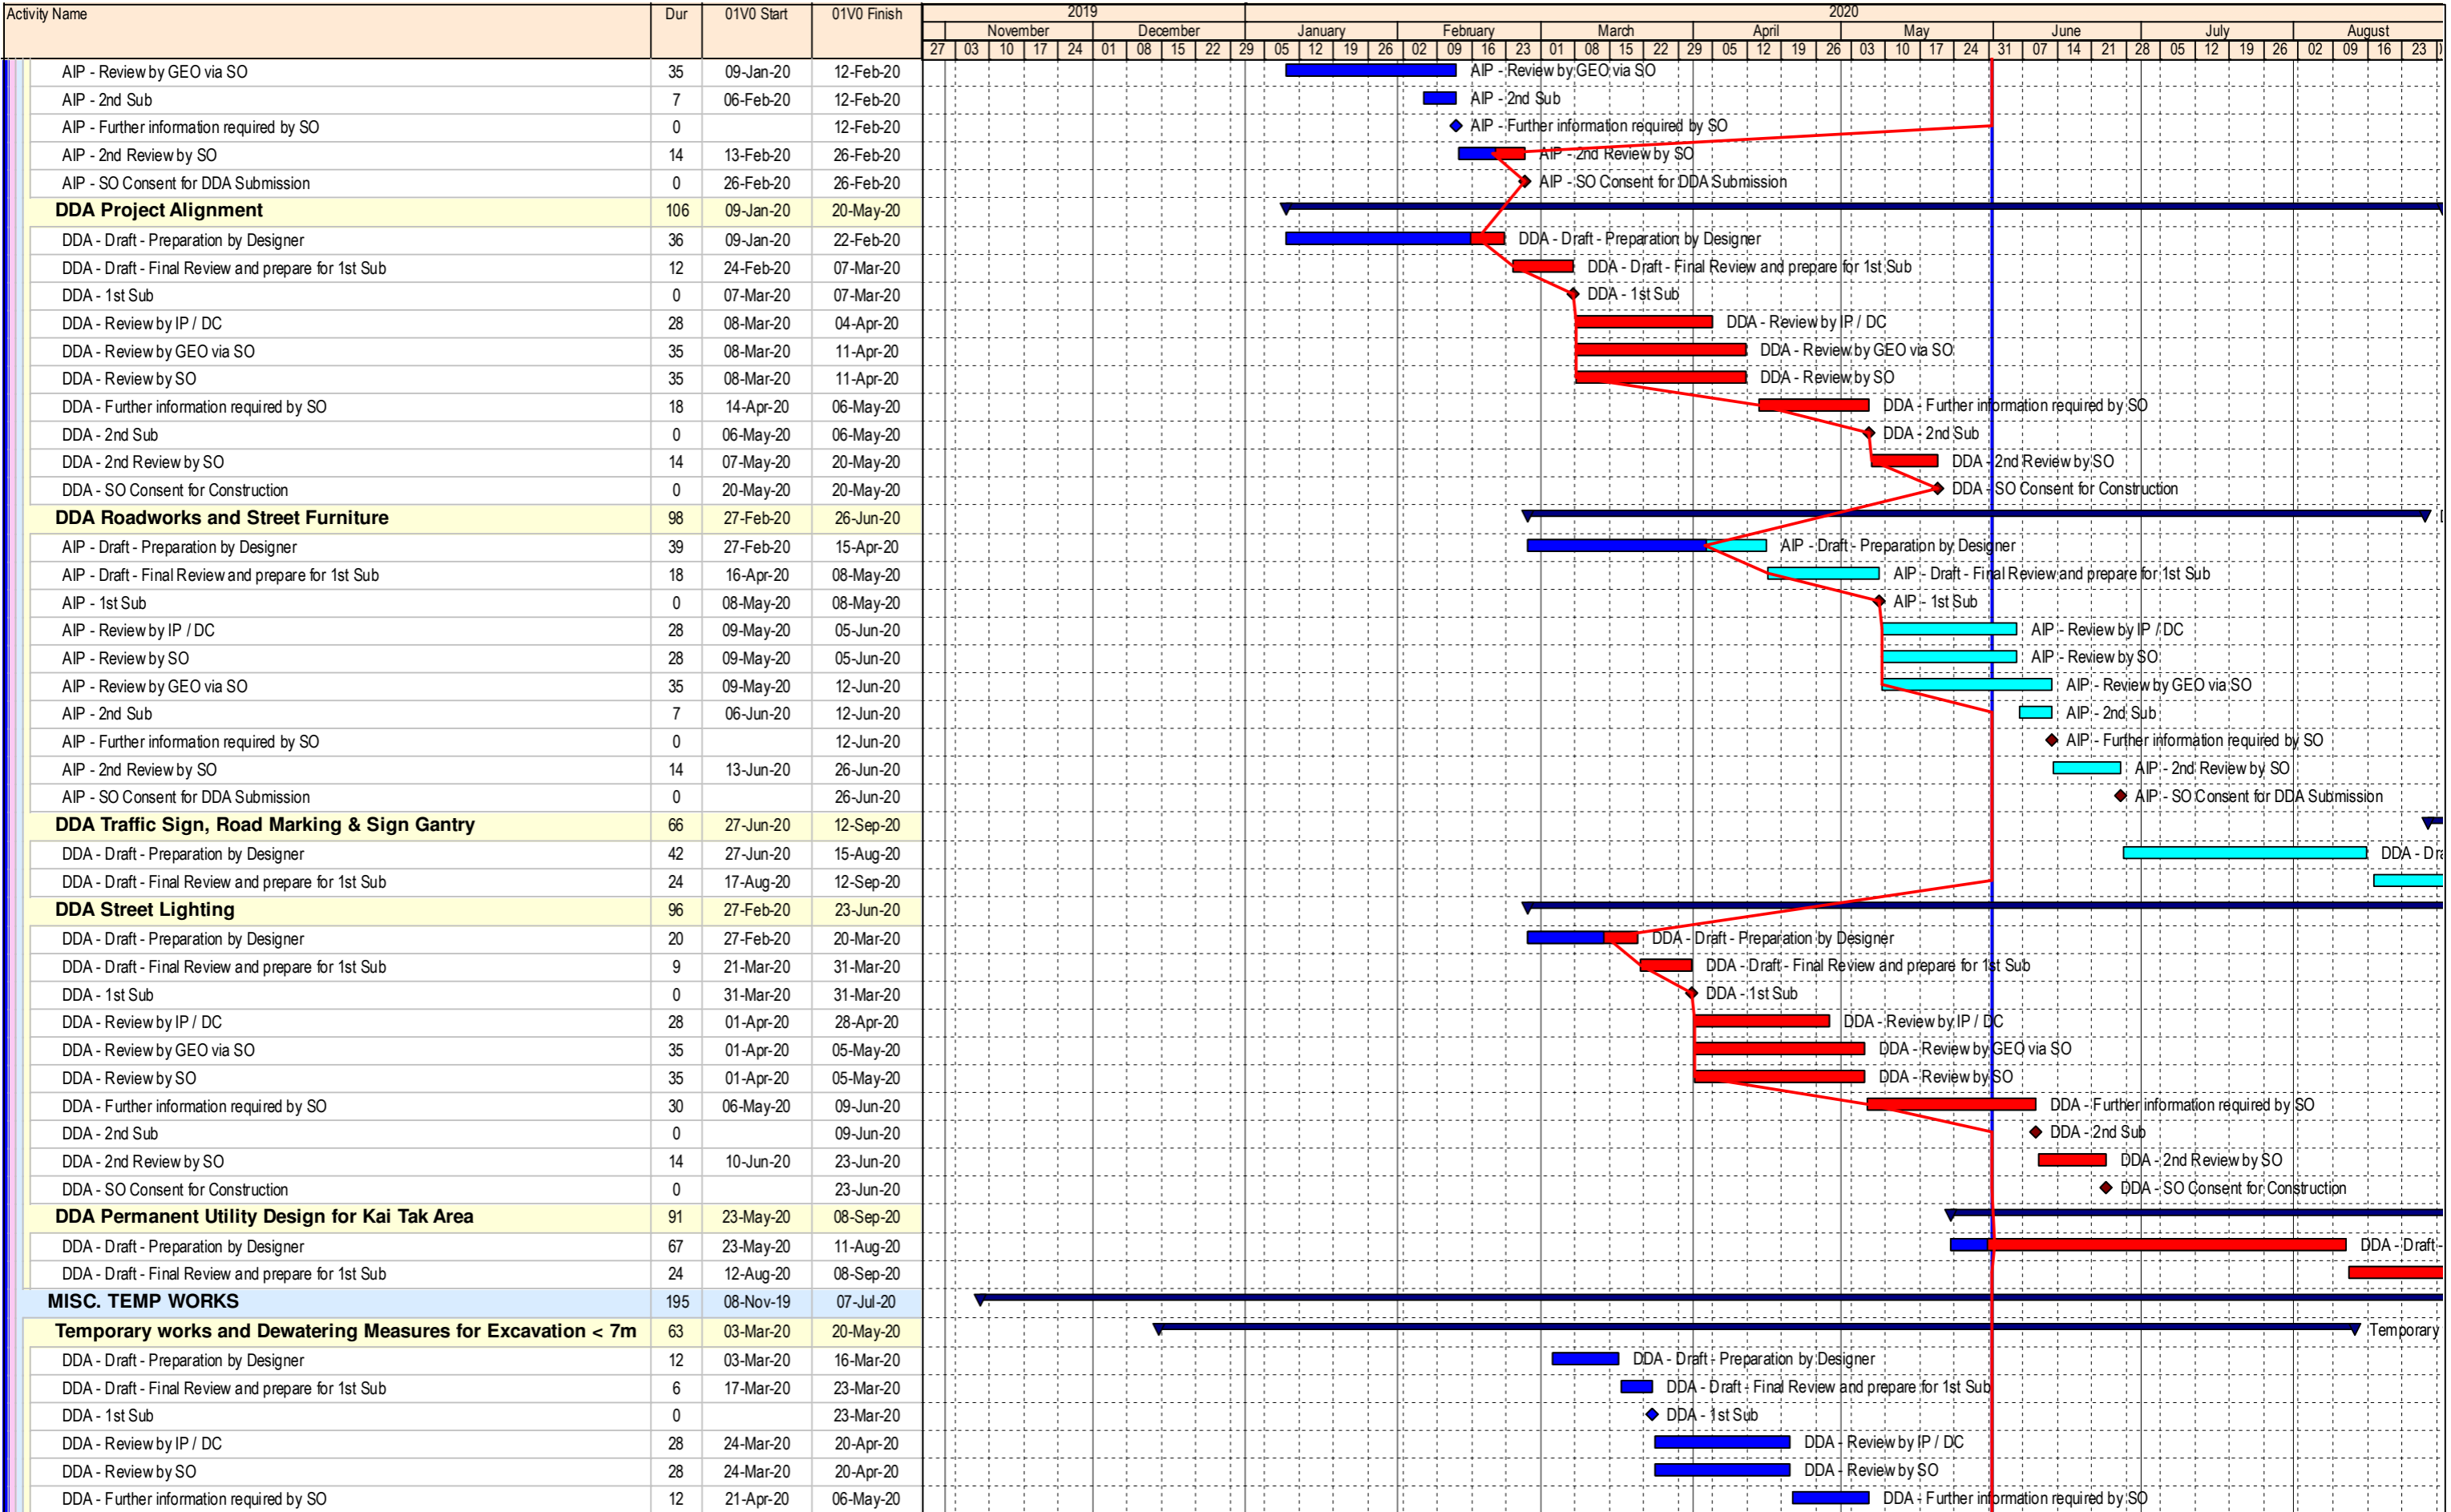



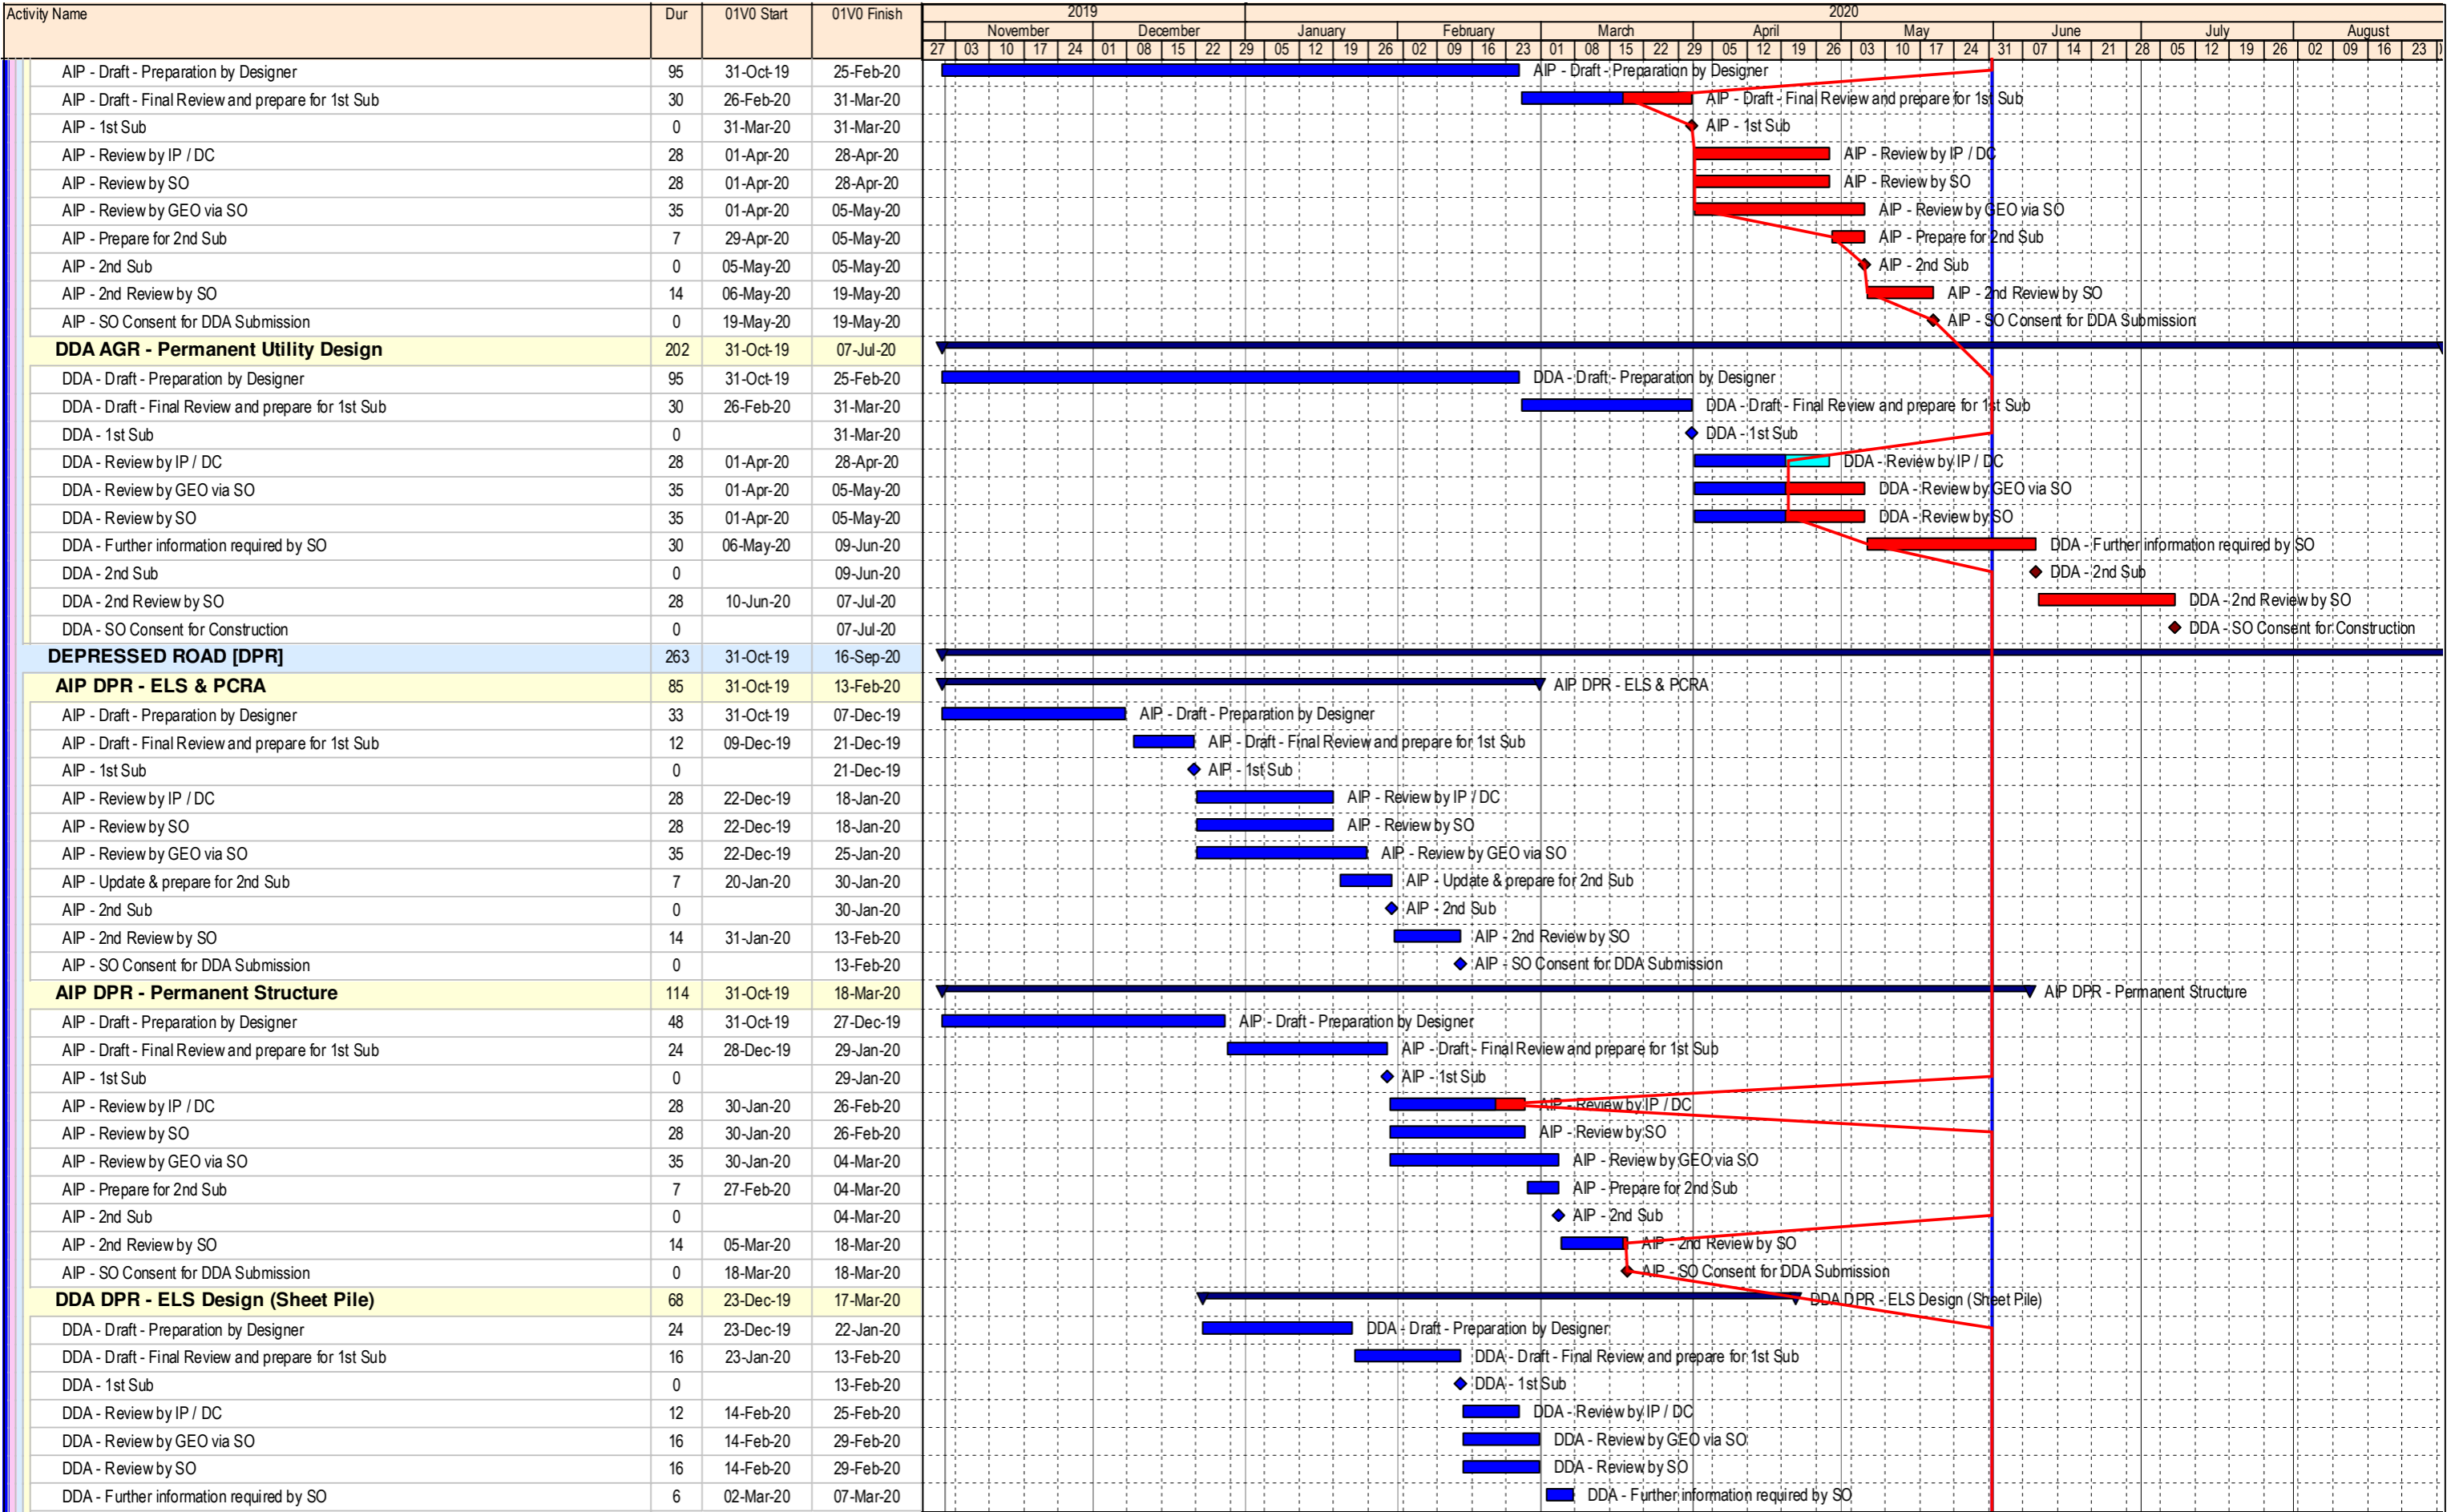

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Progress Milestone
- ▬ Progress Bar
- ▬ Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
















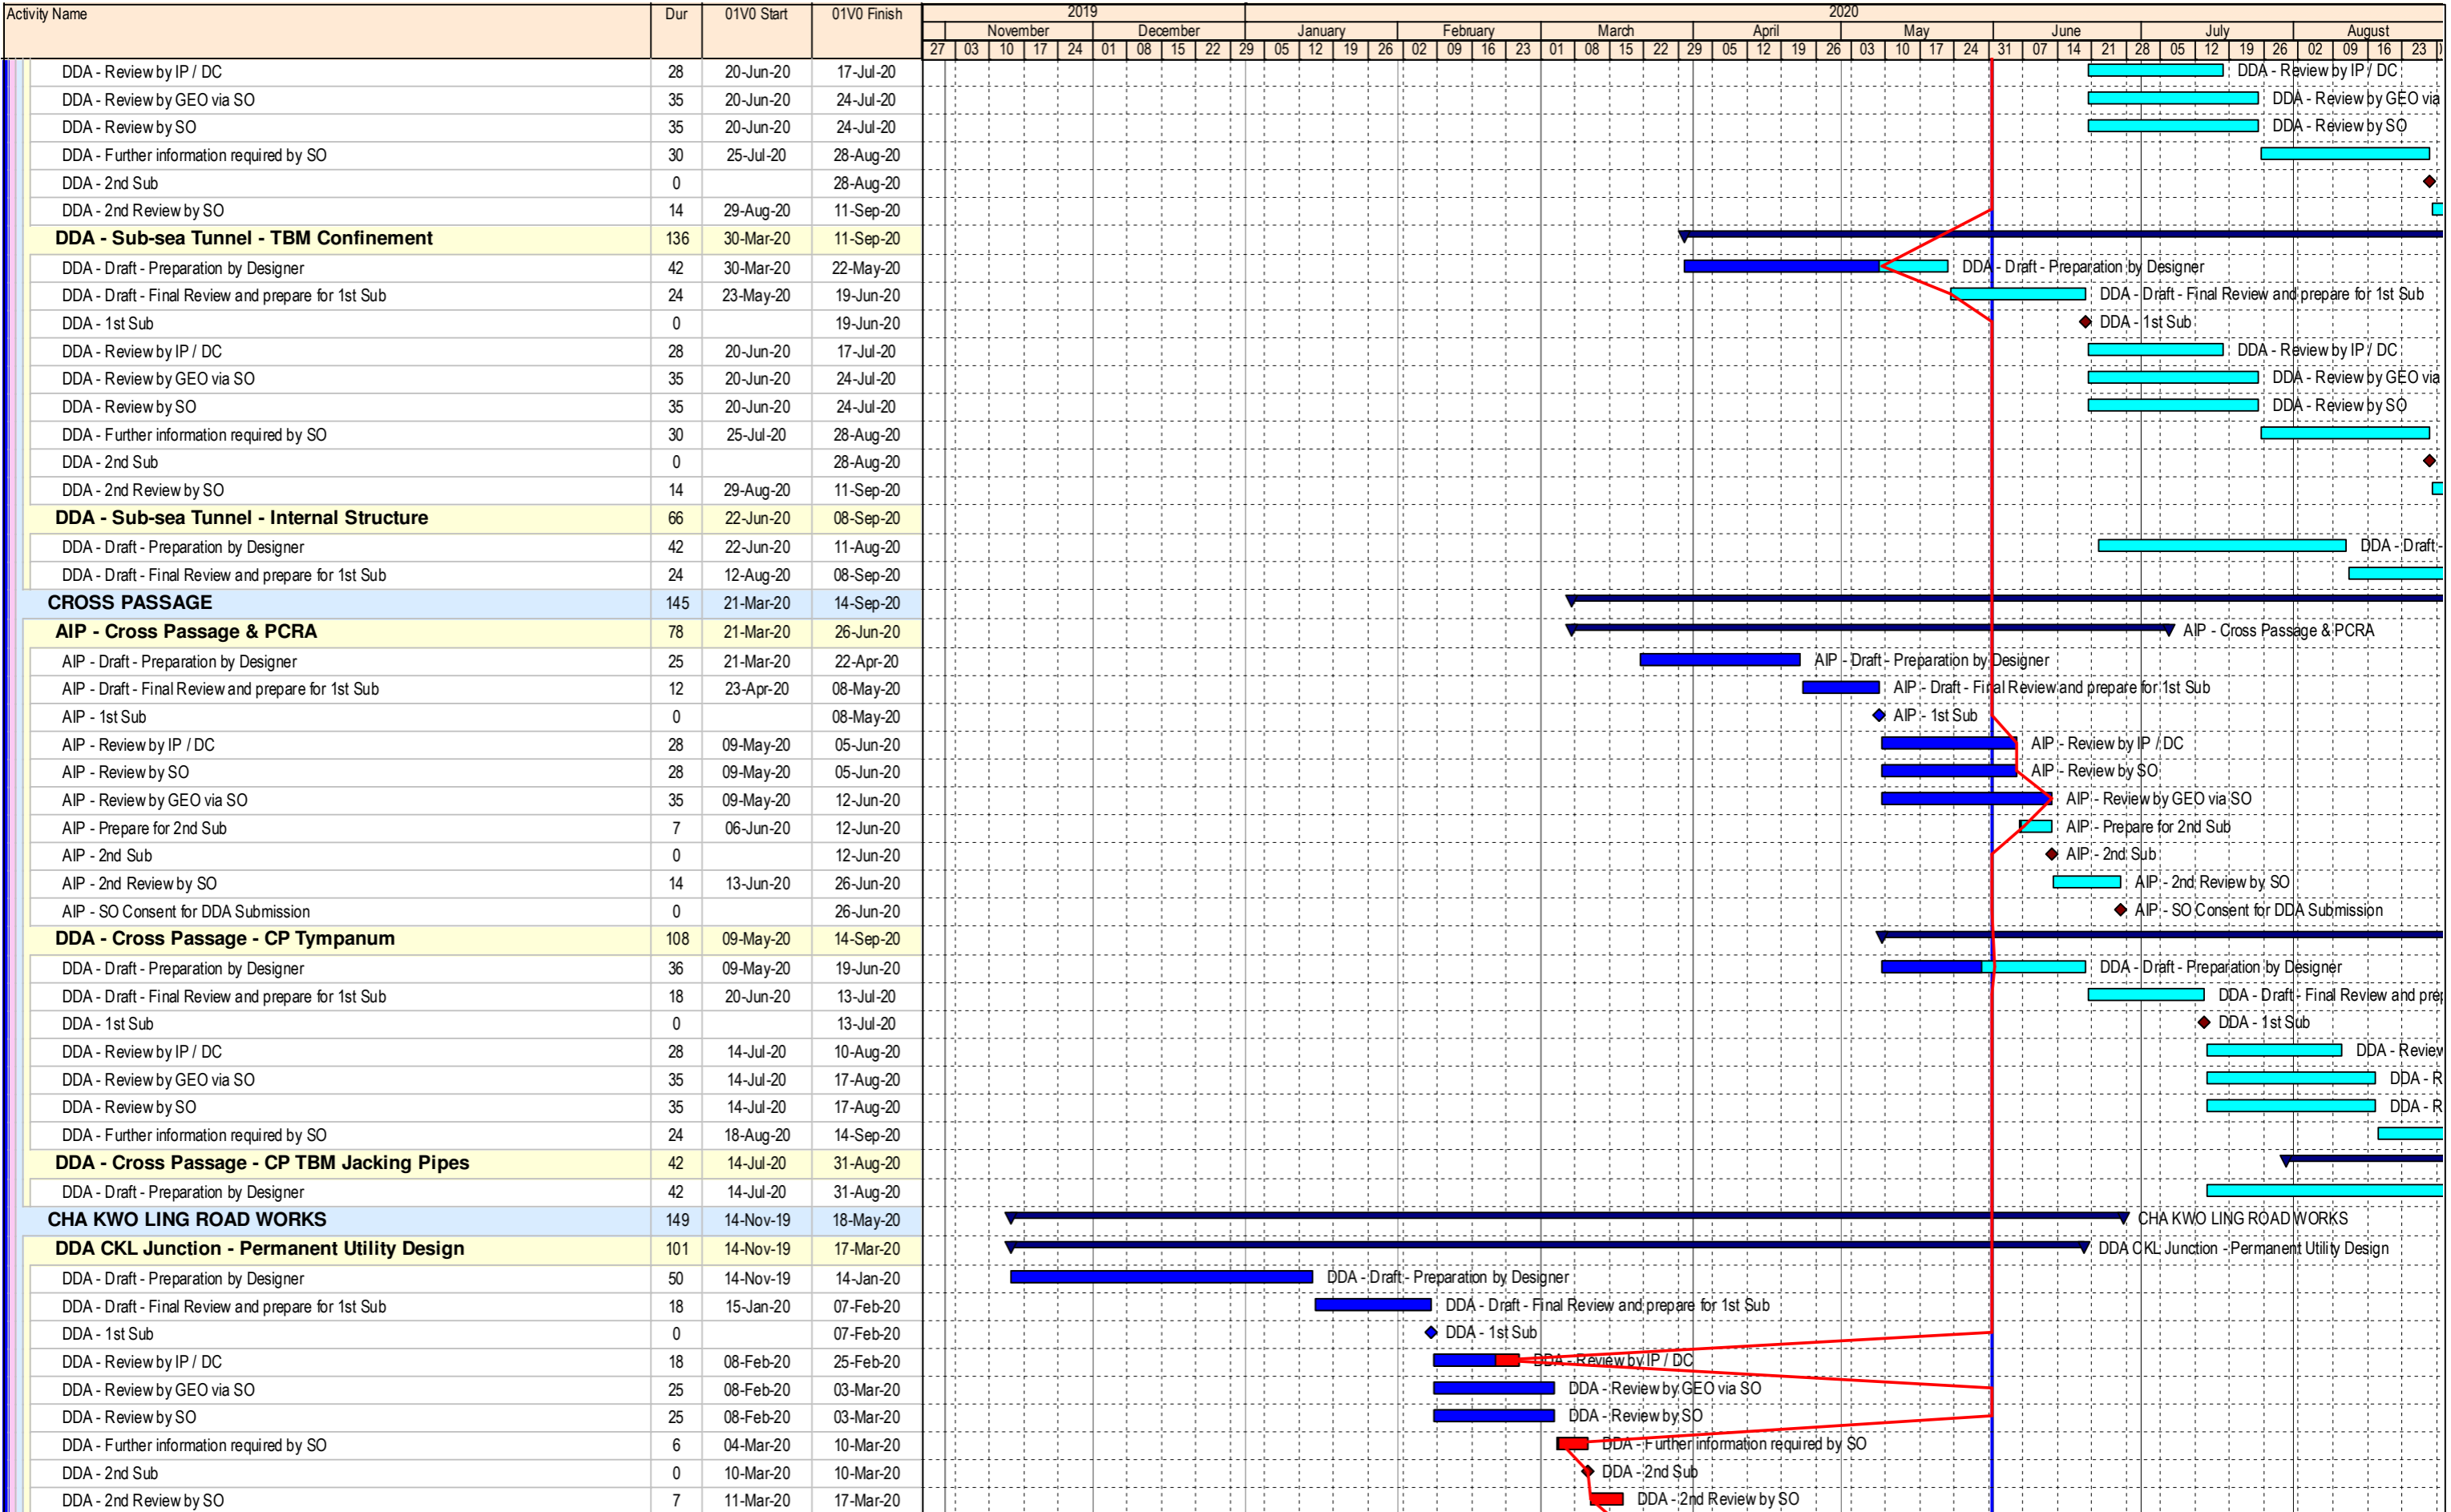

Page 12 of 18  
 Data Date: 31-May-20  
 Project ID: T210010-10

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Progress Milestone
- ▬ Progress Bar
- ▬ Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu













