



Page 1 of 30  
Data Date: 30-Aug-20

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

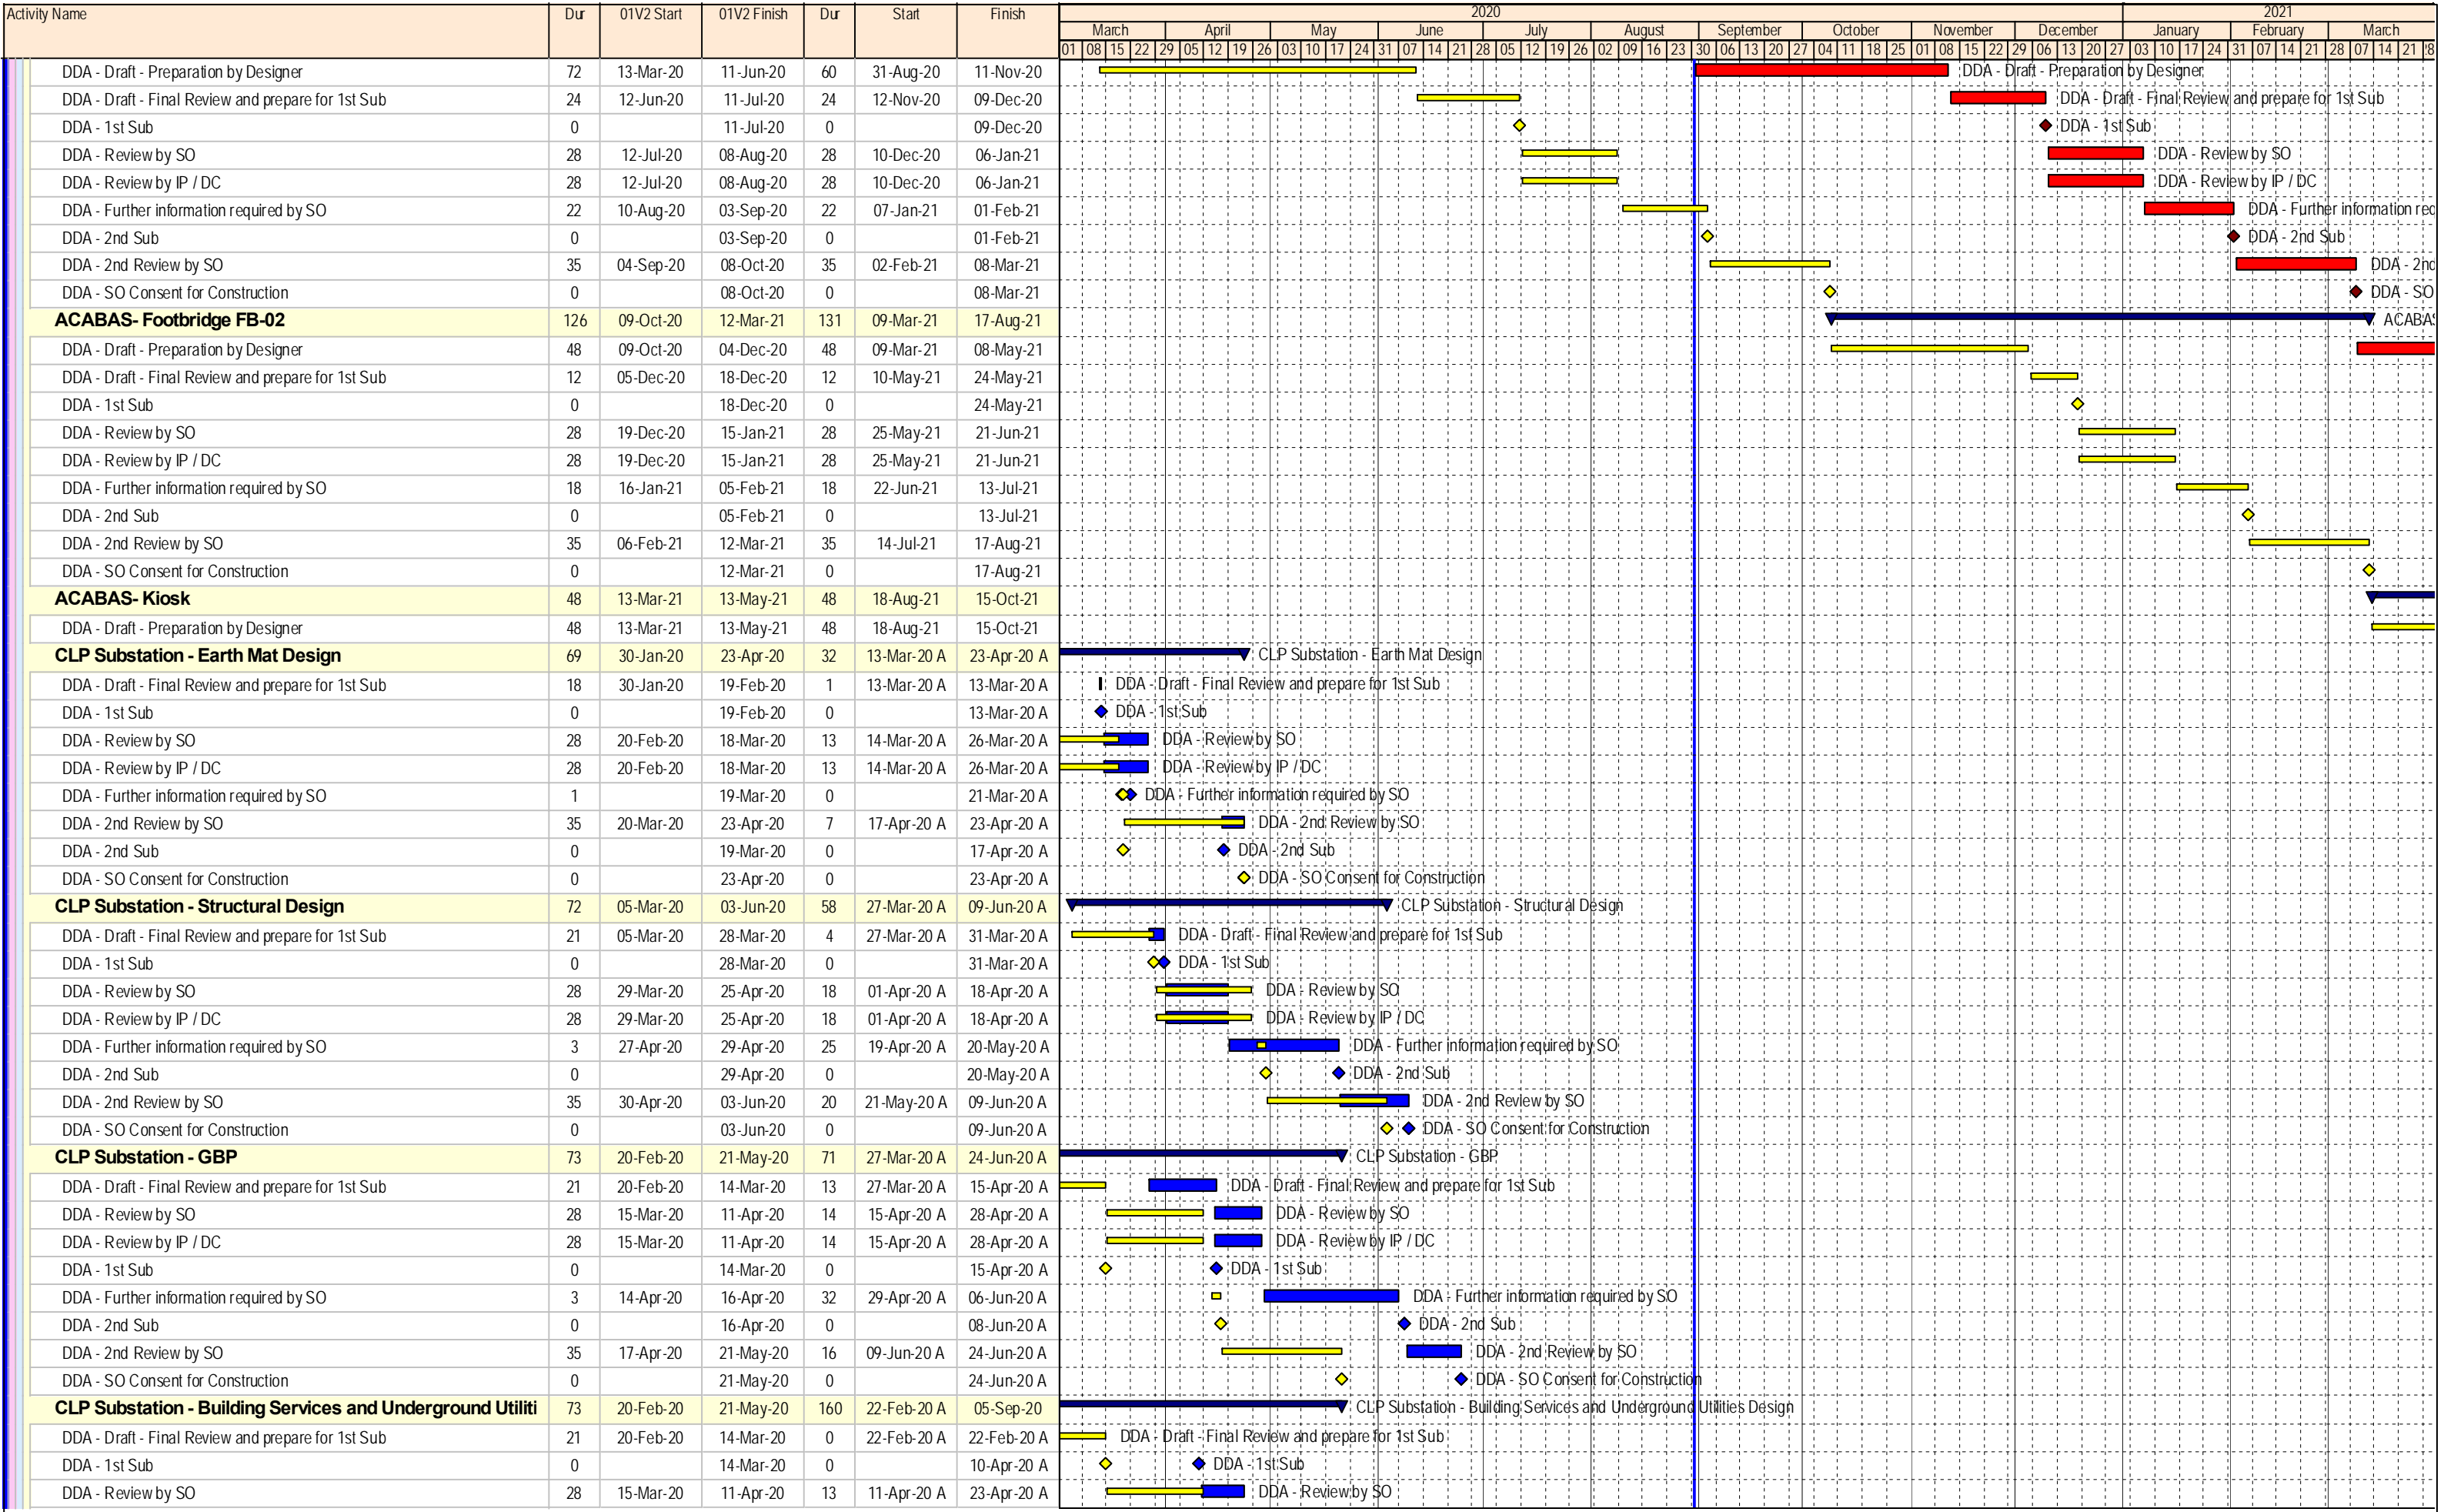


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

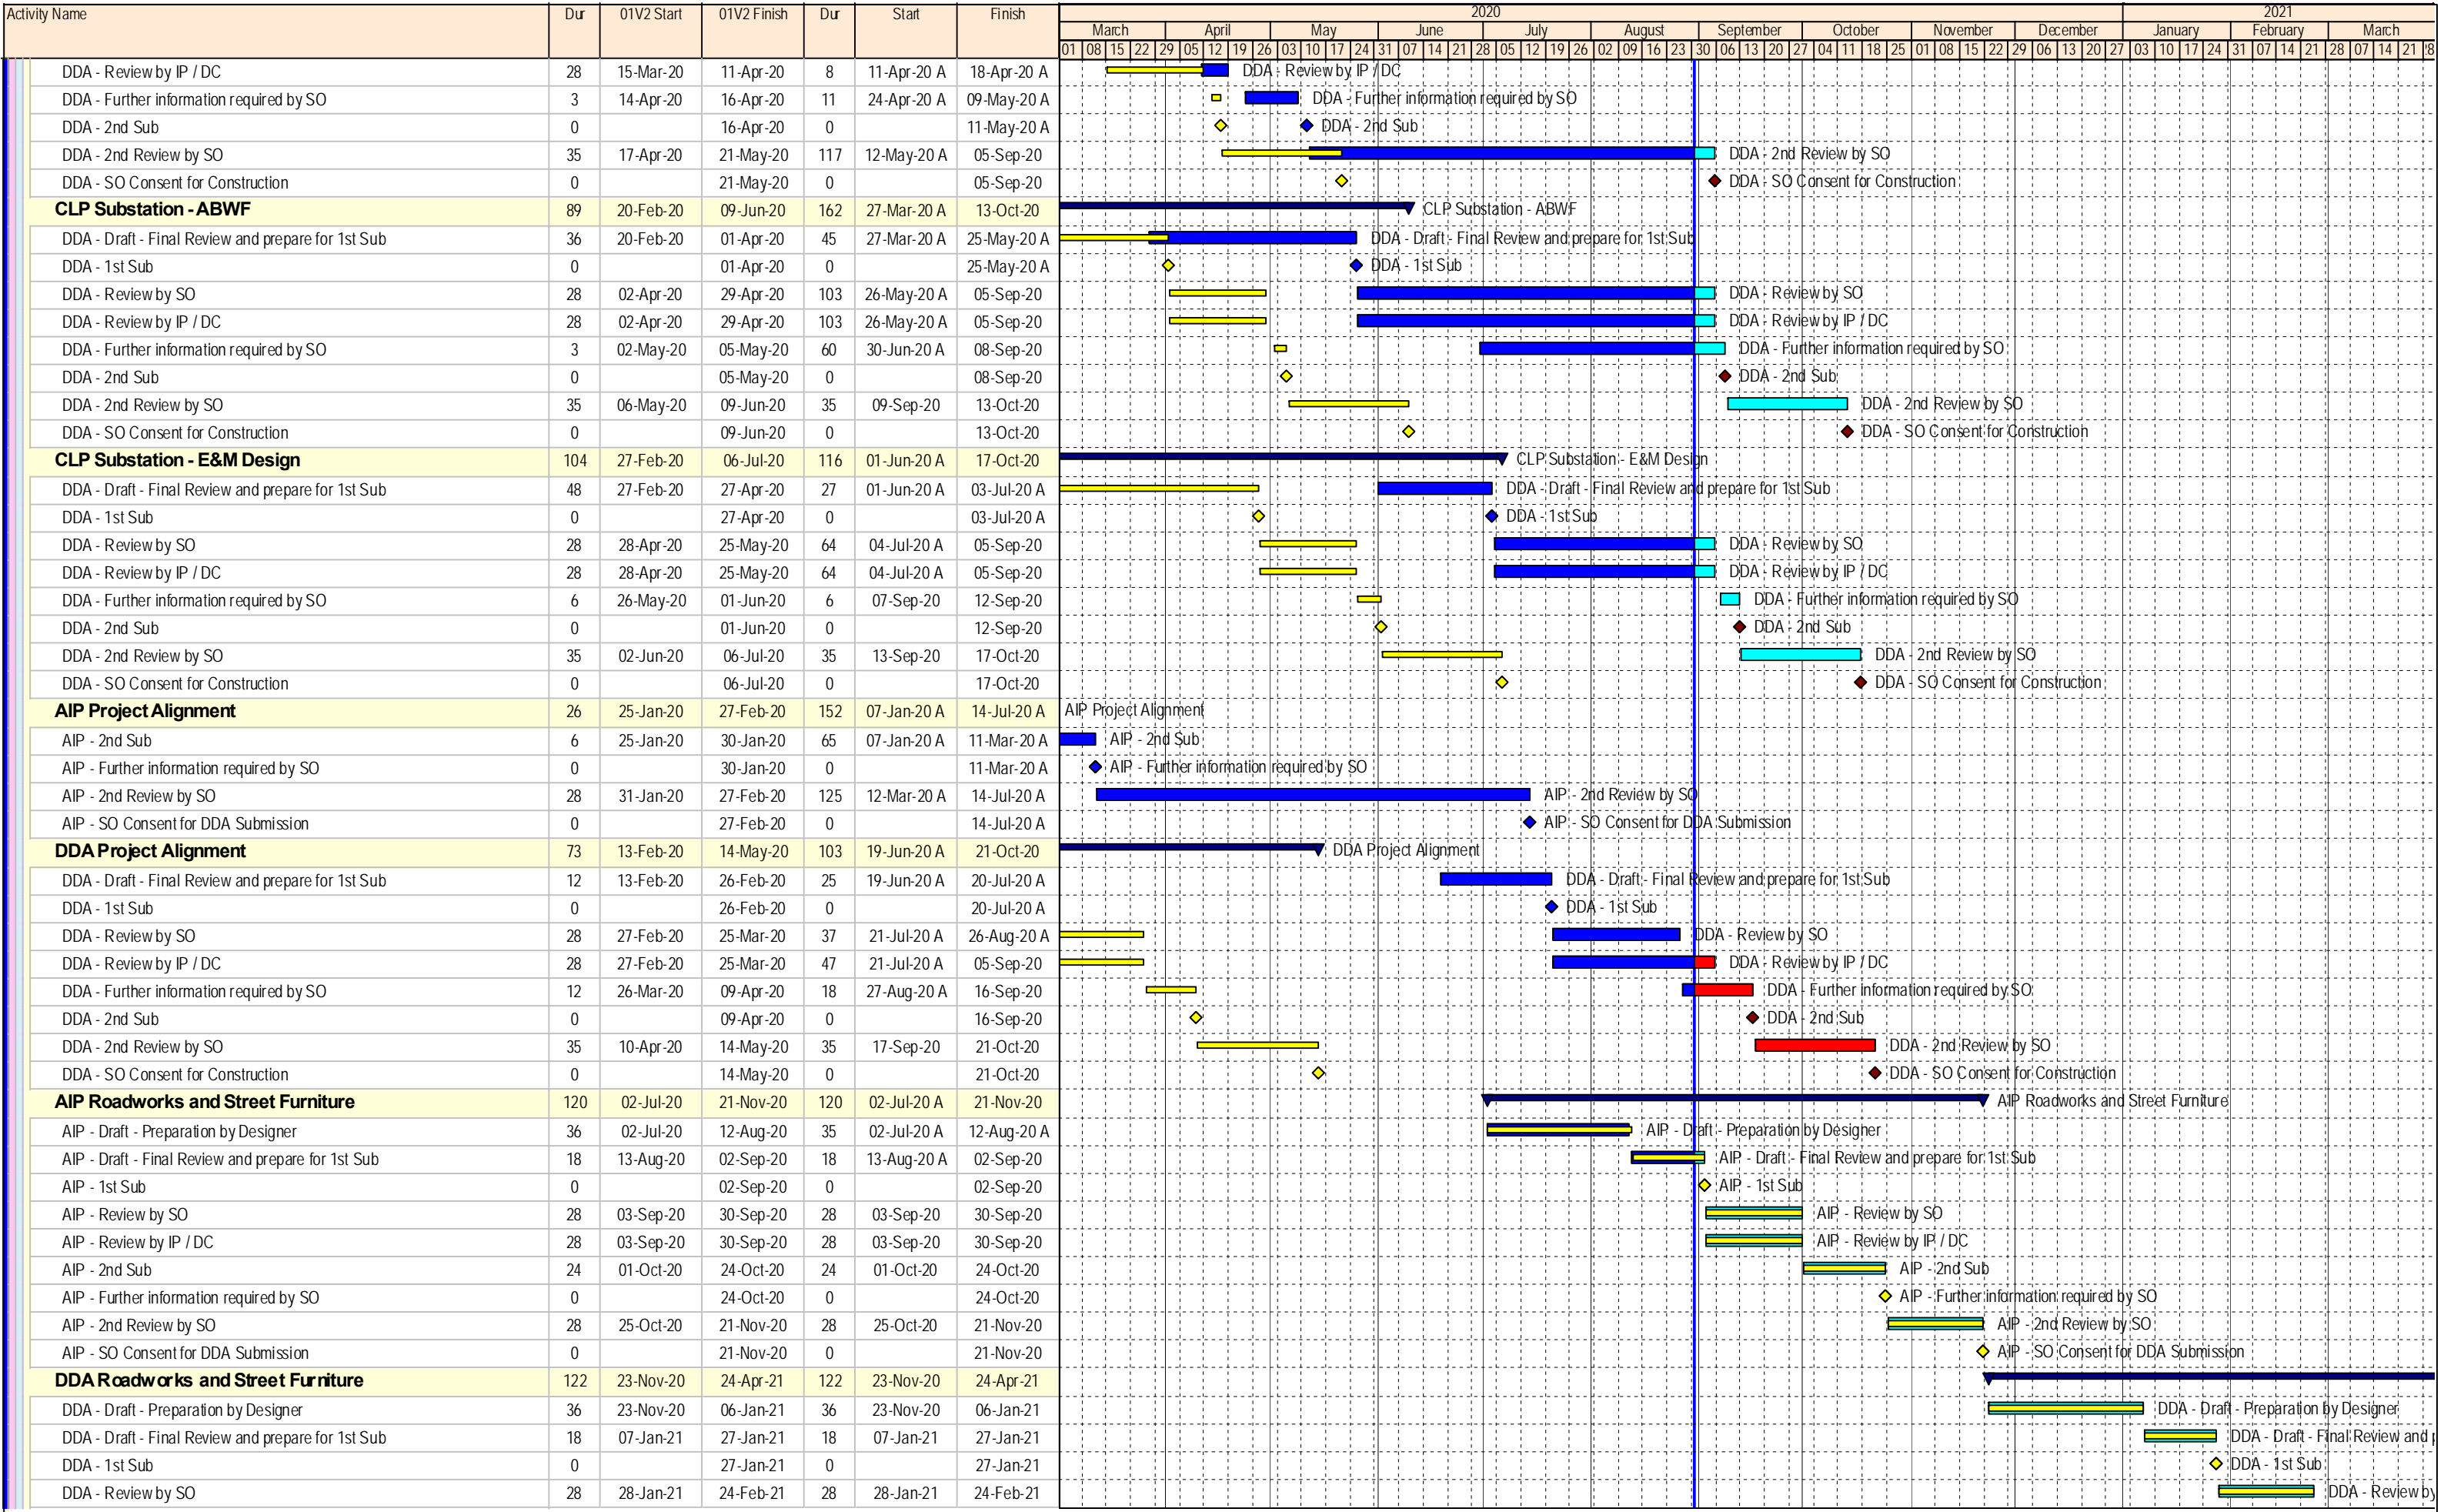

Page 3 of 30  
Data Date: 30-Aug-20

- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu






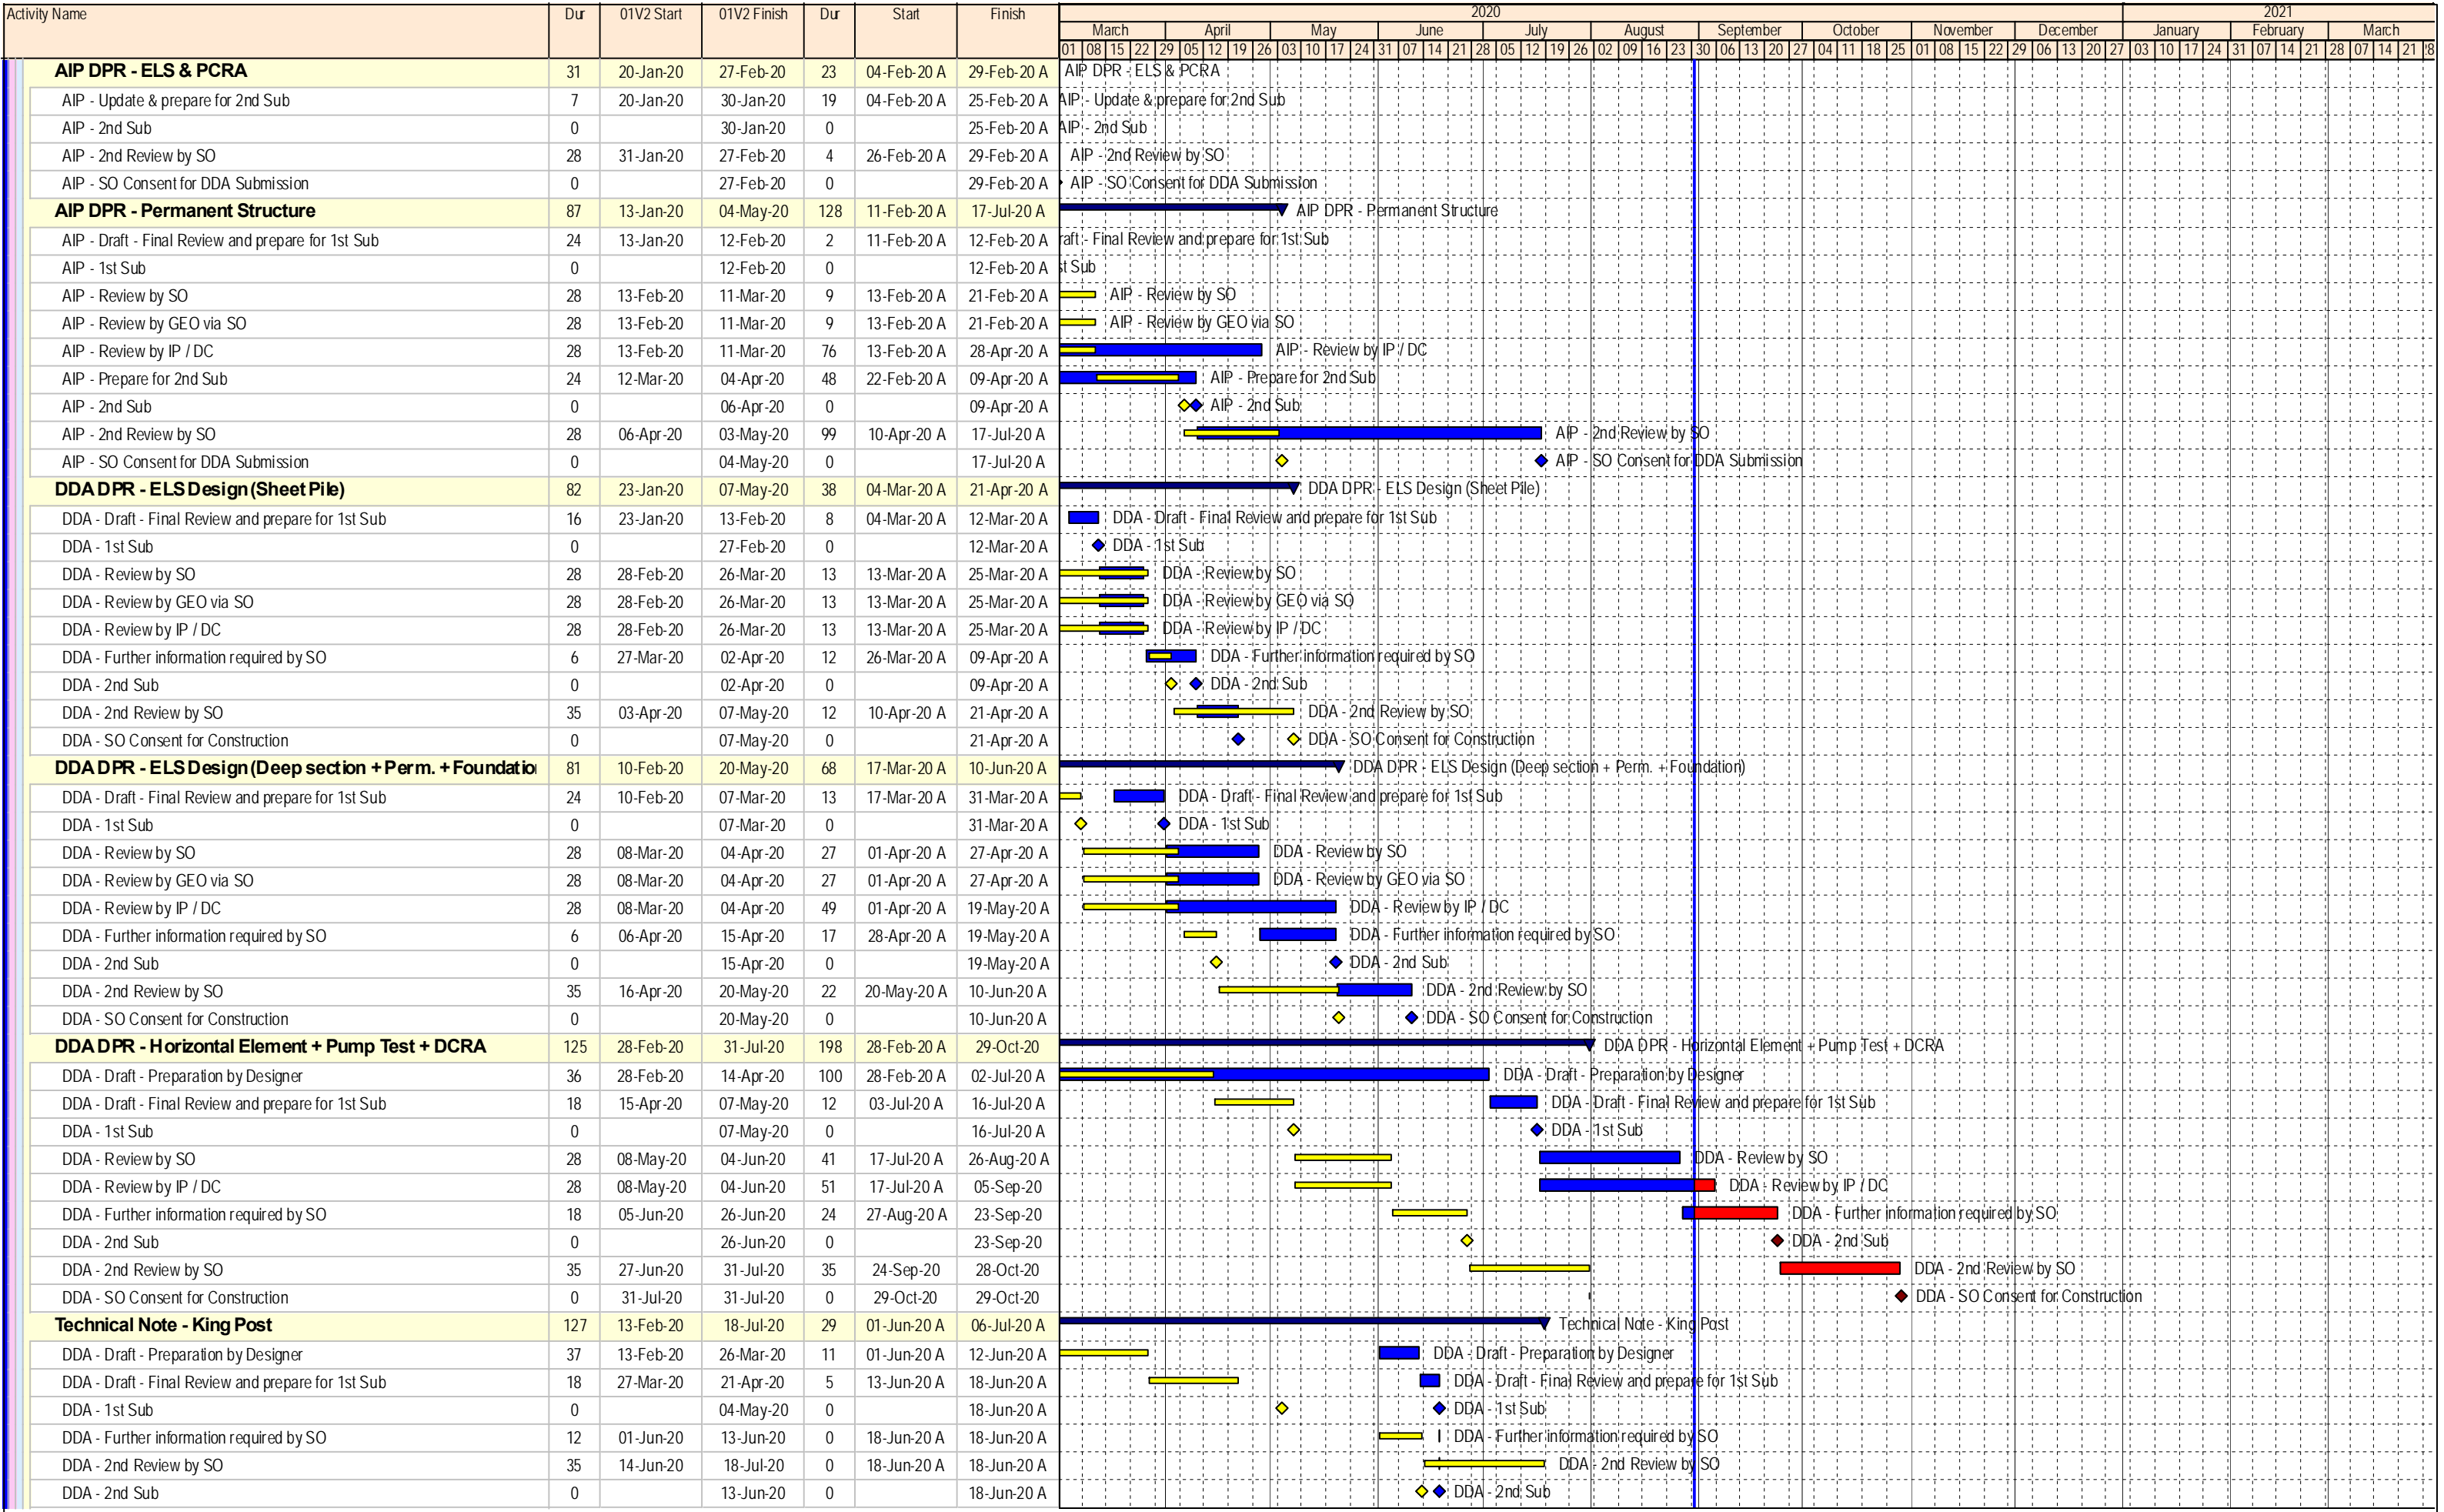

Page 6 of 30  
Data Date: 30-Aug-20


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu




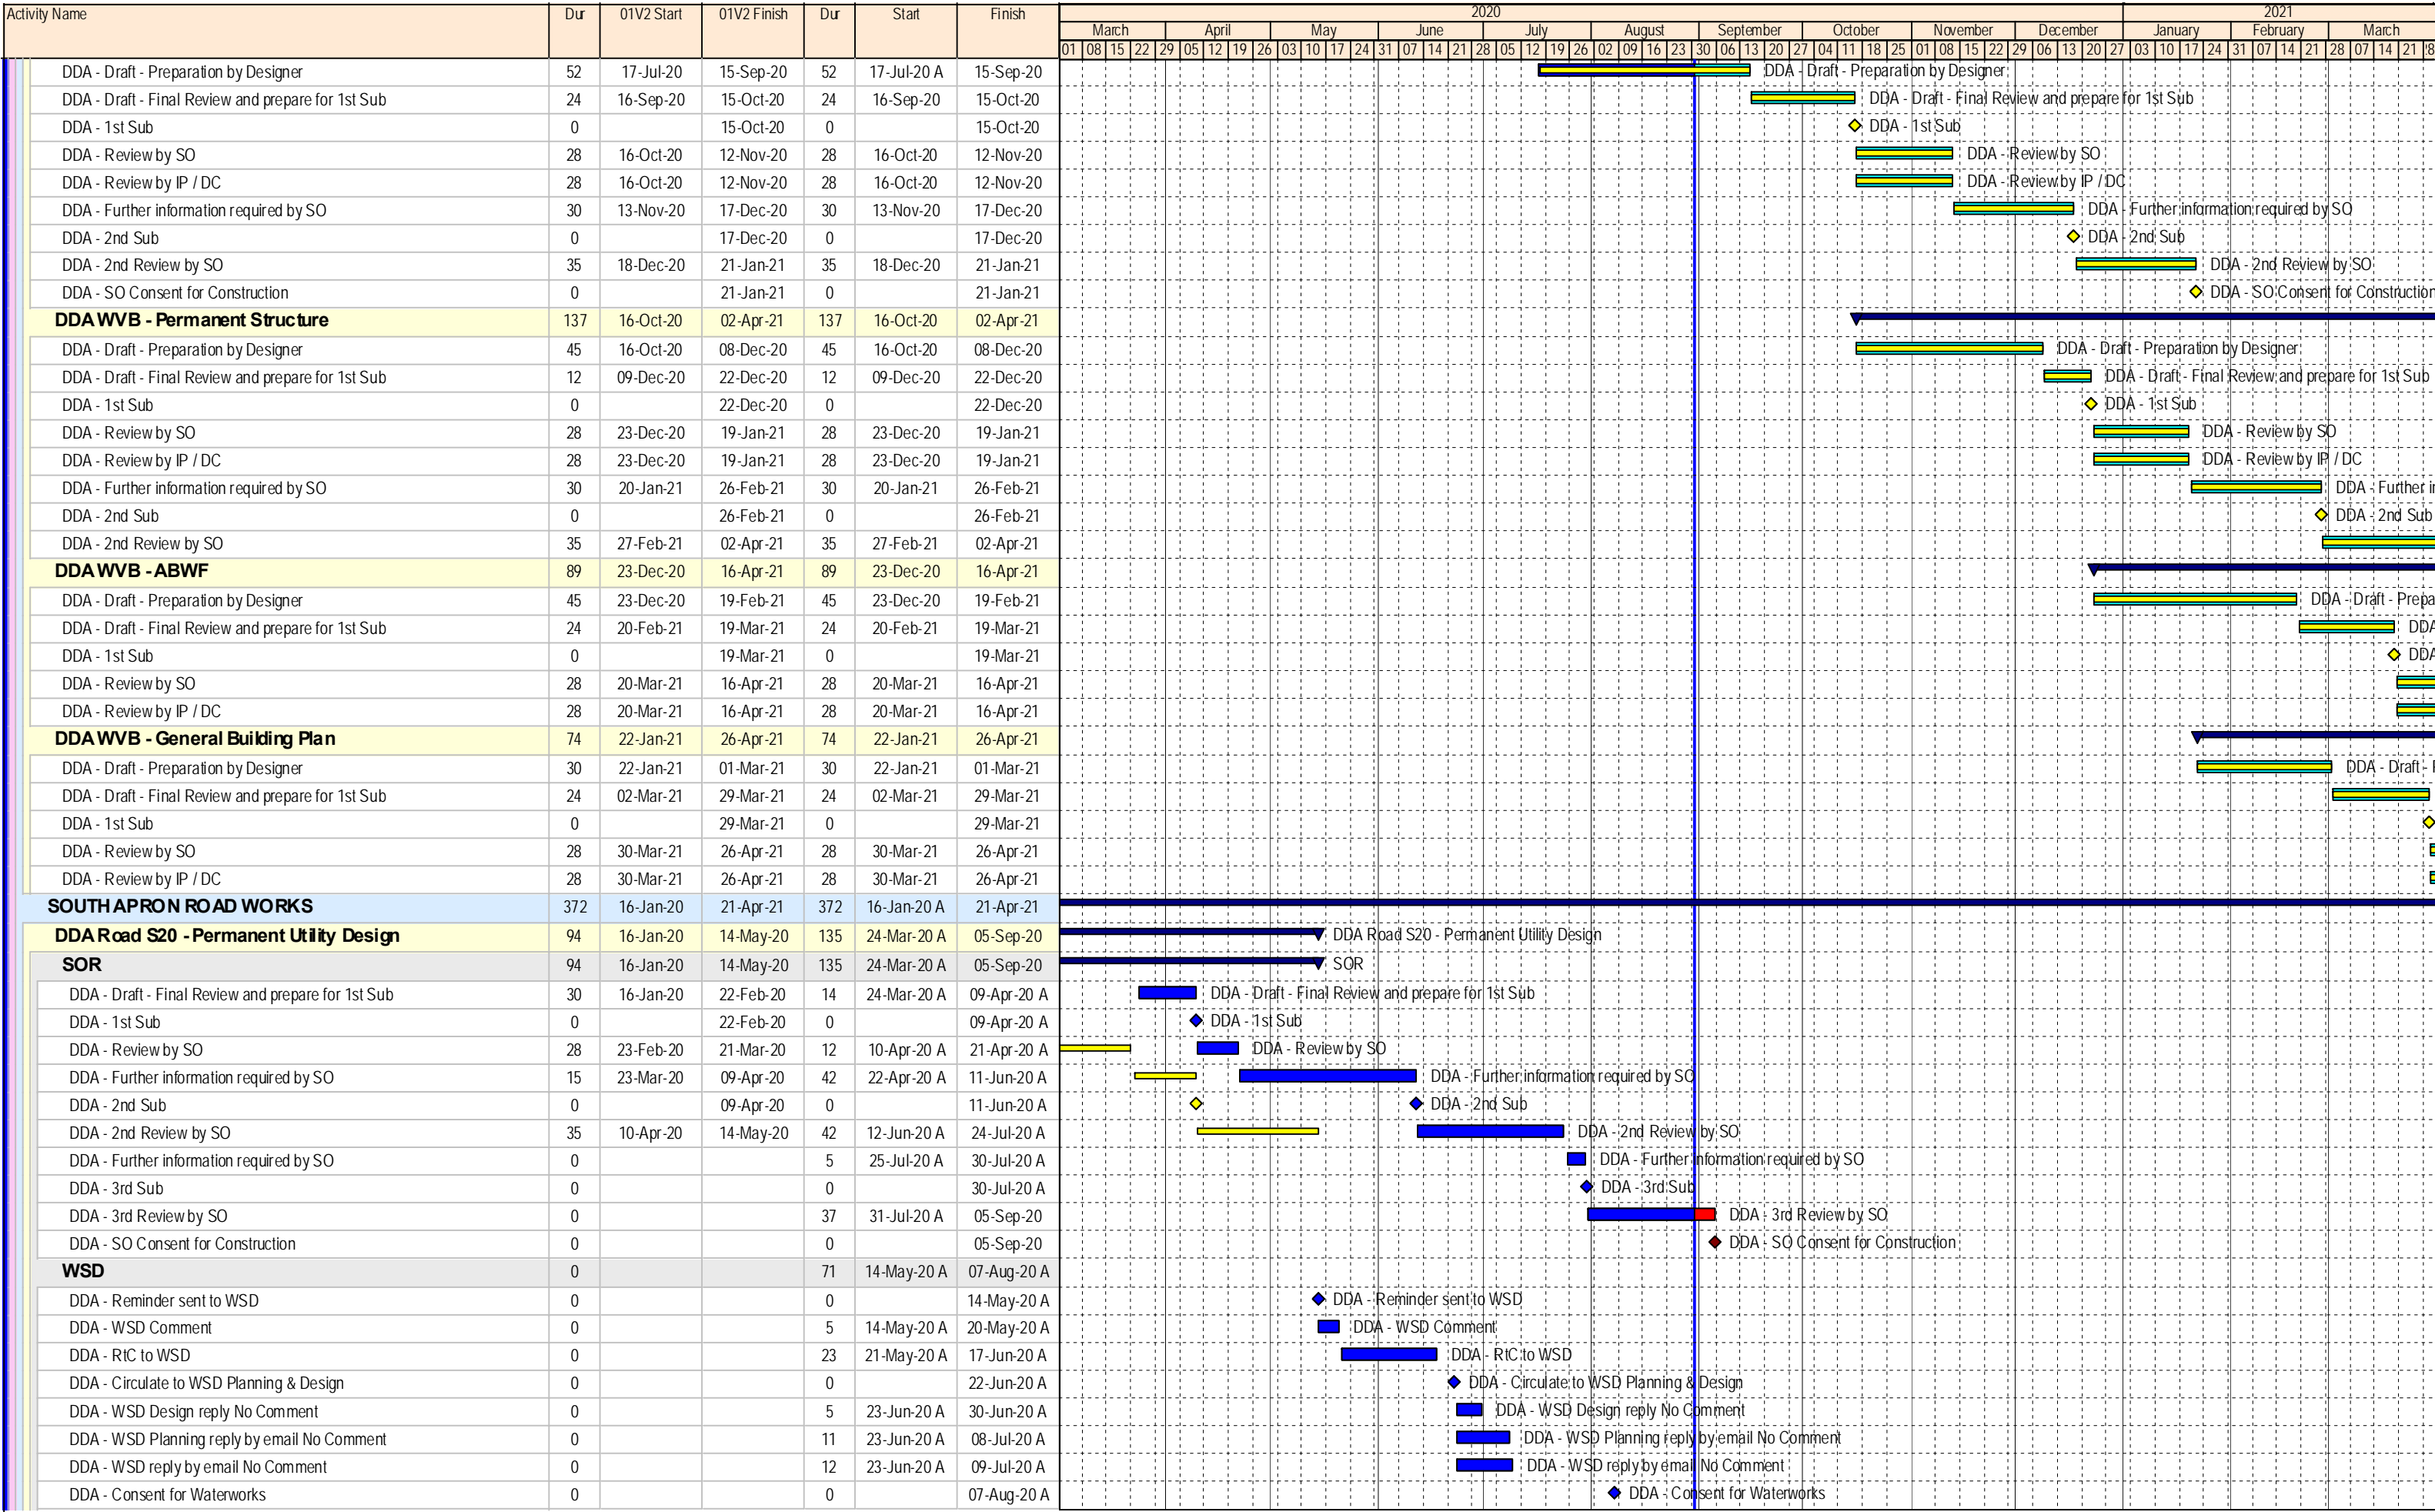

Legend for chart symbols:



- Milestone (Red diamond)
- Planned Bar (Light blue)
- Critical Activity (Red bar)
- Actual Milestone (Blue diamond)
- Actual Work (Blue bar)
- Baseline Milestone (Yellow diamond)
- Baseline Bar (Yellow bar)

### ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu




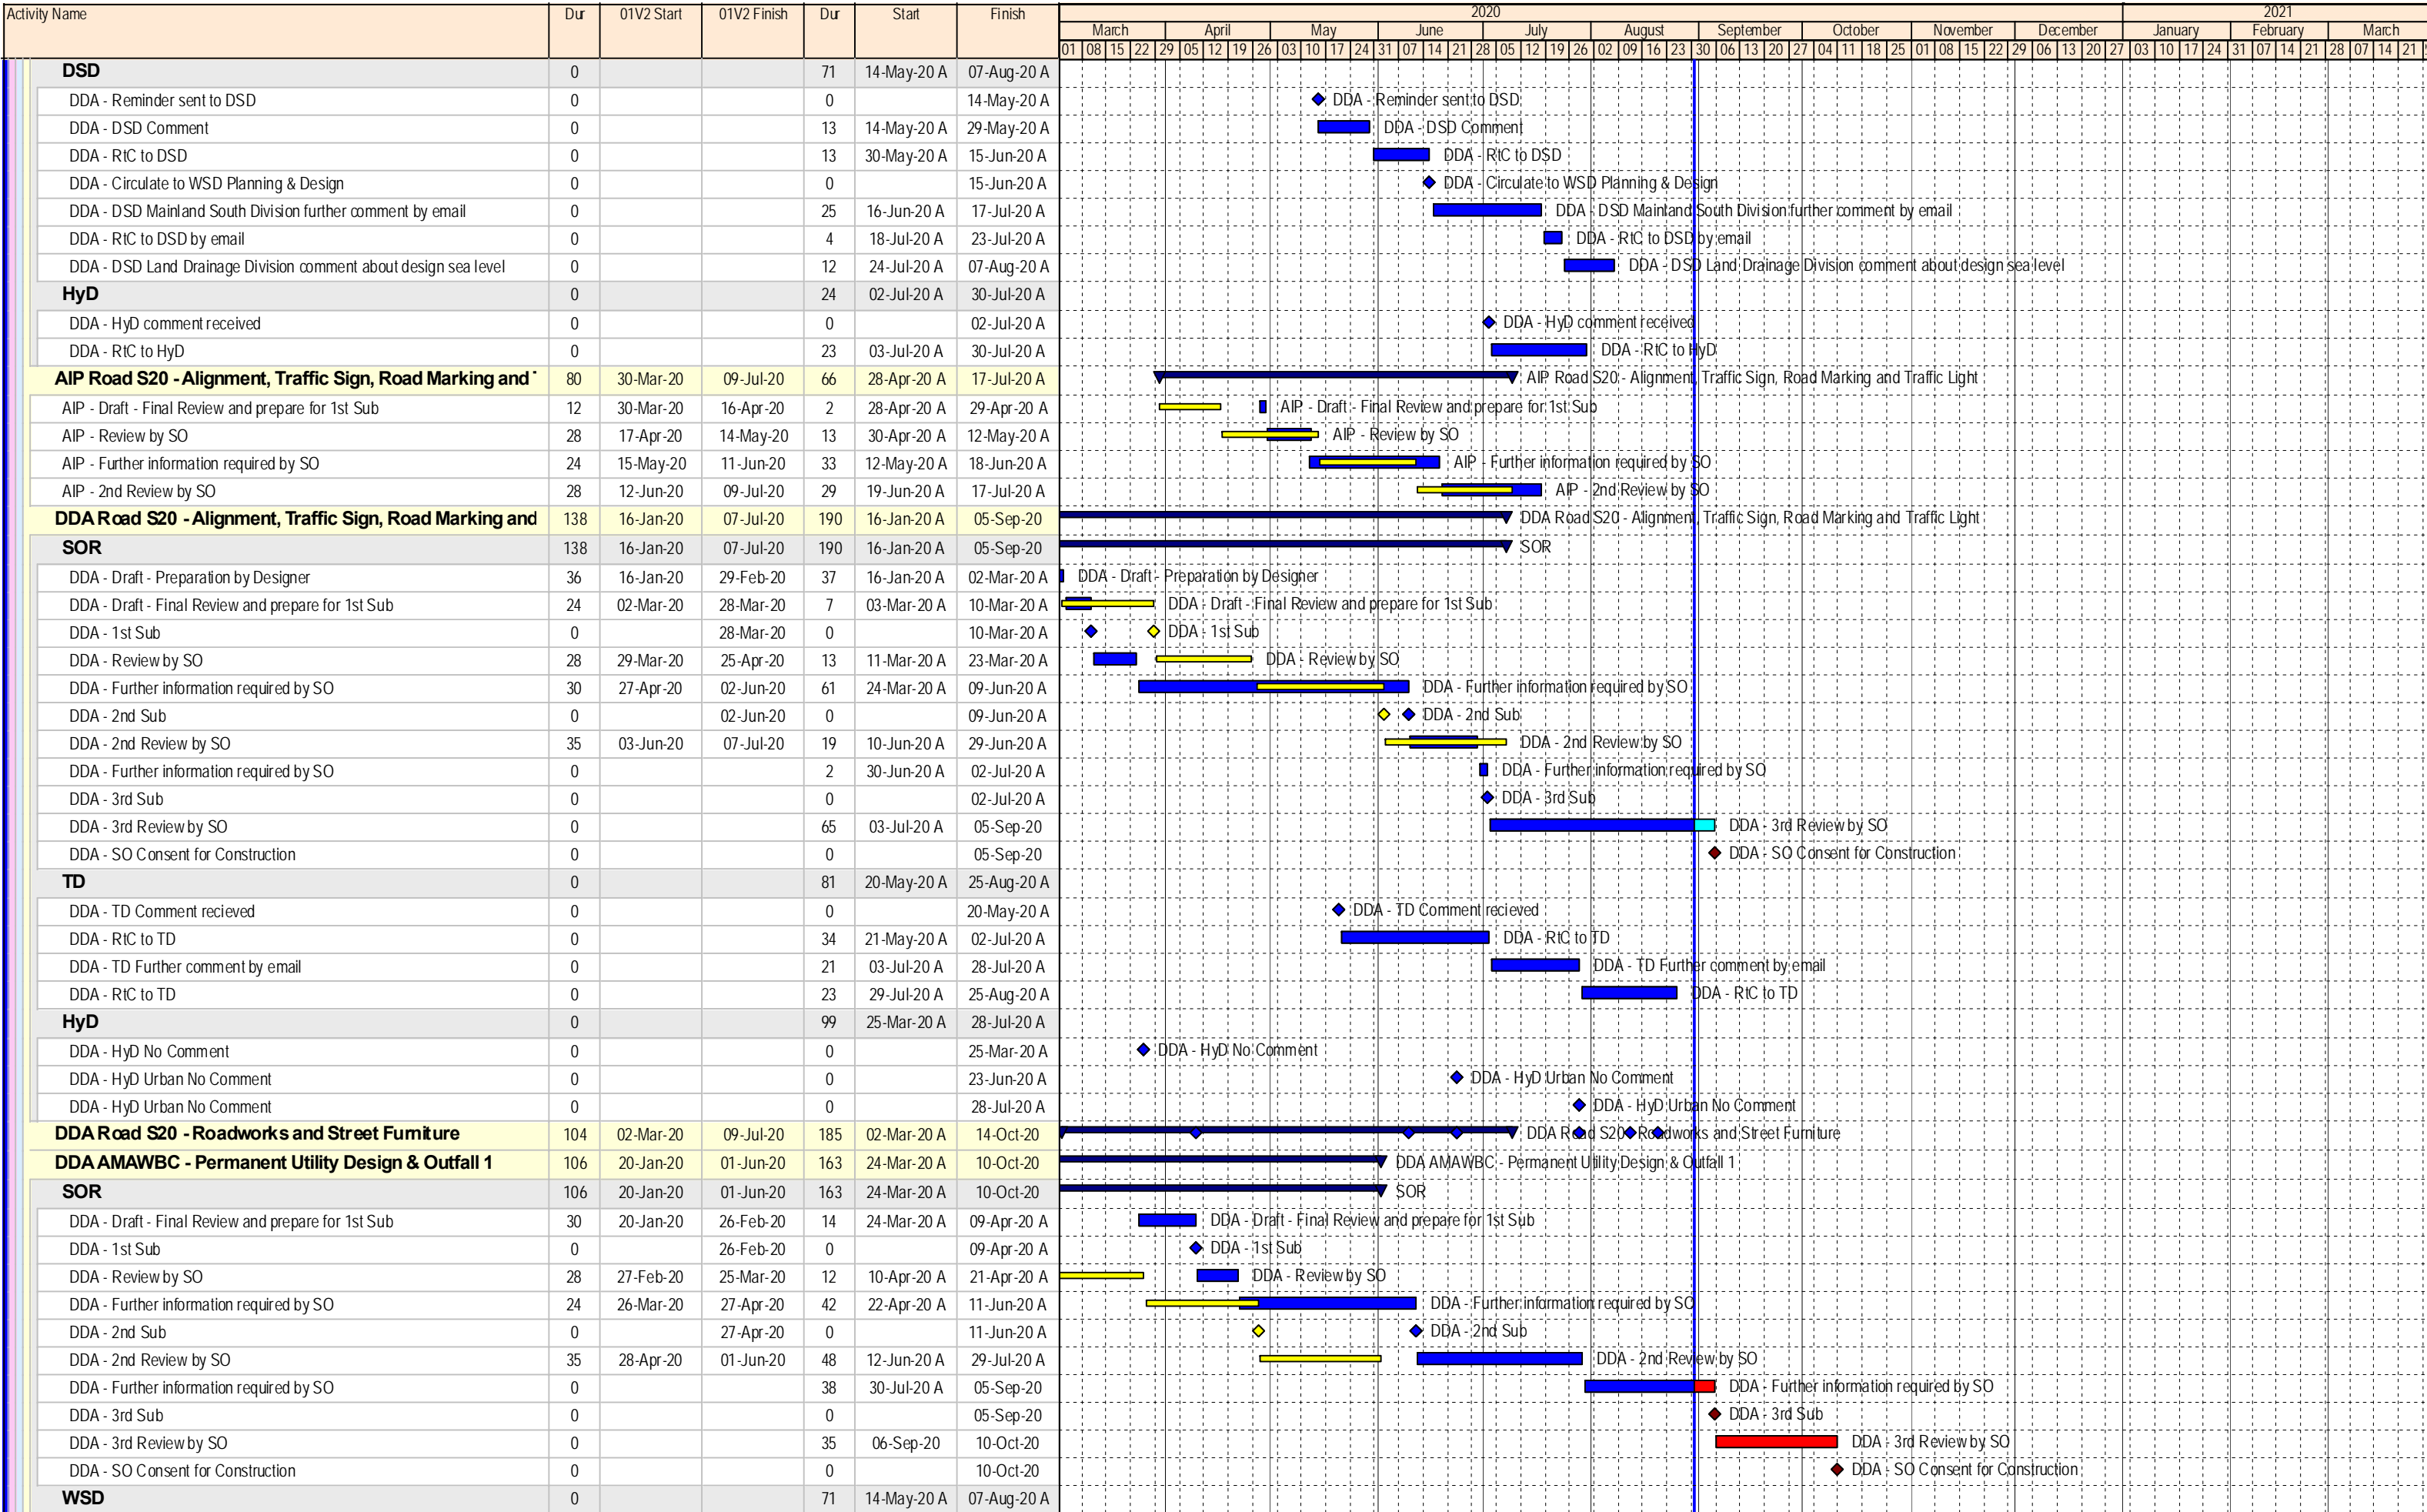

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

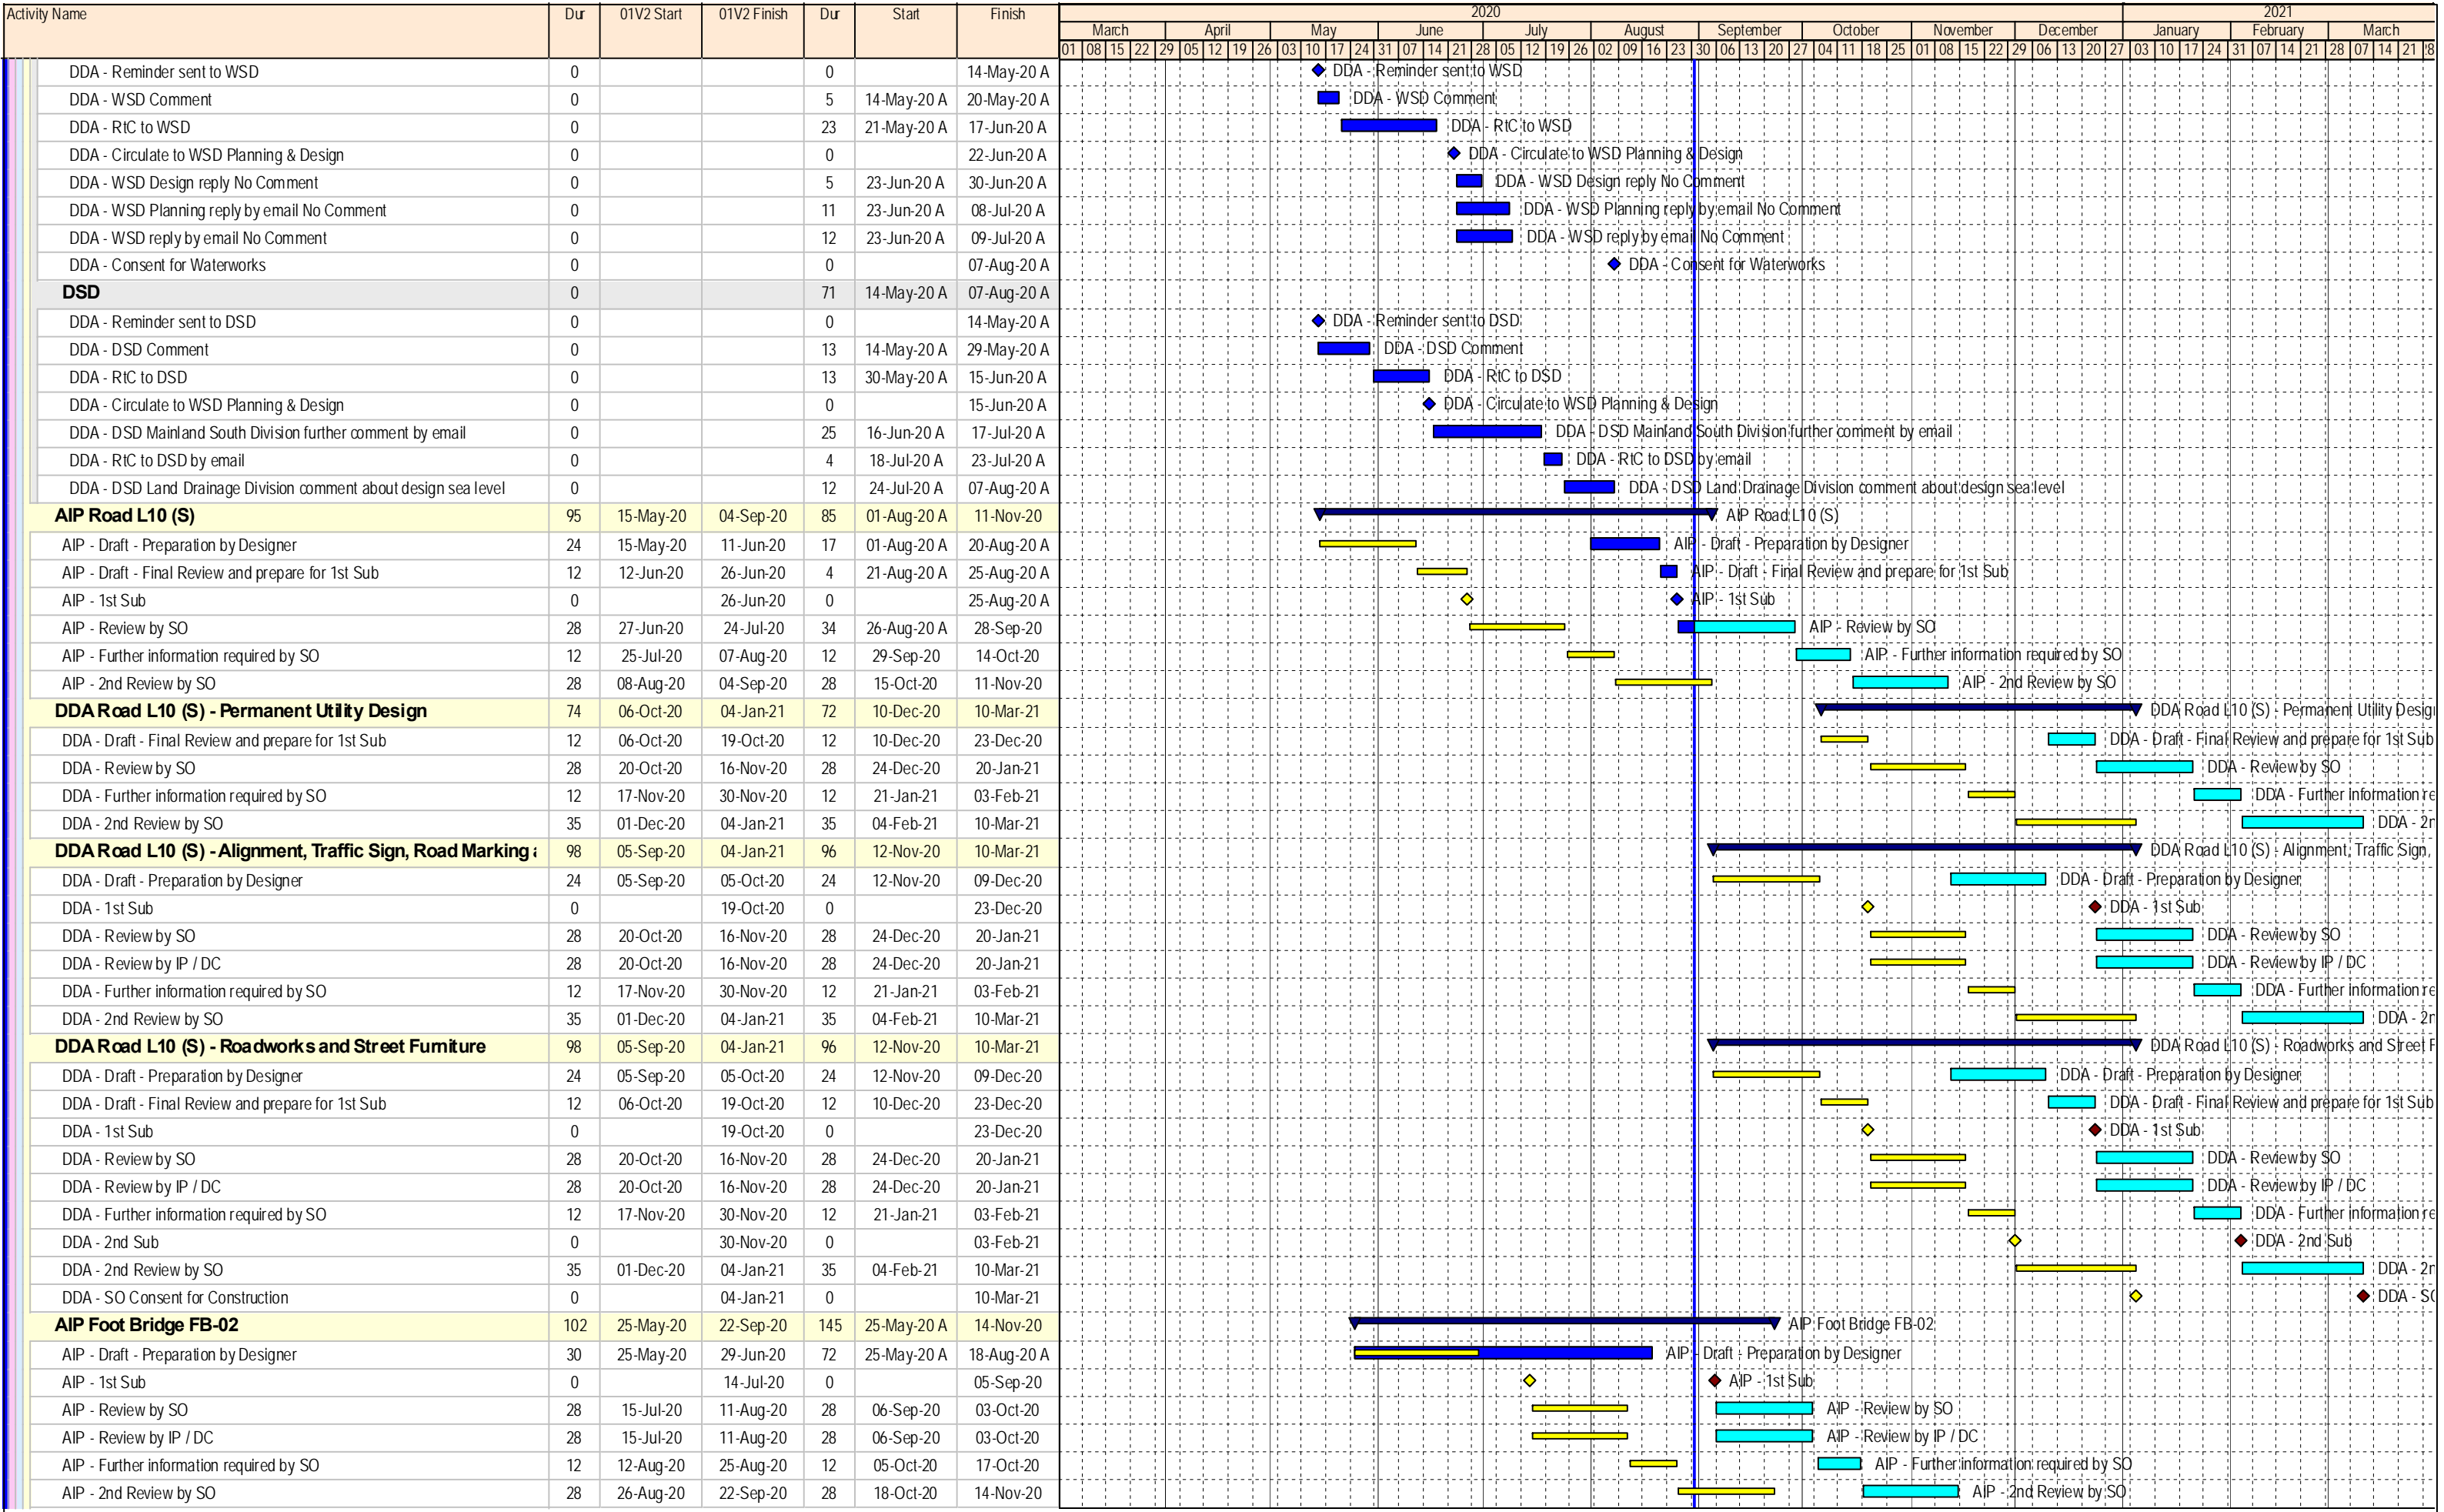


Page 10 of 30	◆ Milestone	◆ Actual Milestone
Data Date: 30-Aug-20	■ Planned Bar	◆ Baseline Milestone
	■ Critical Activity	◆ Baseline Bar
	◆ Actual Work	◆ Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

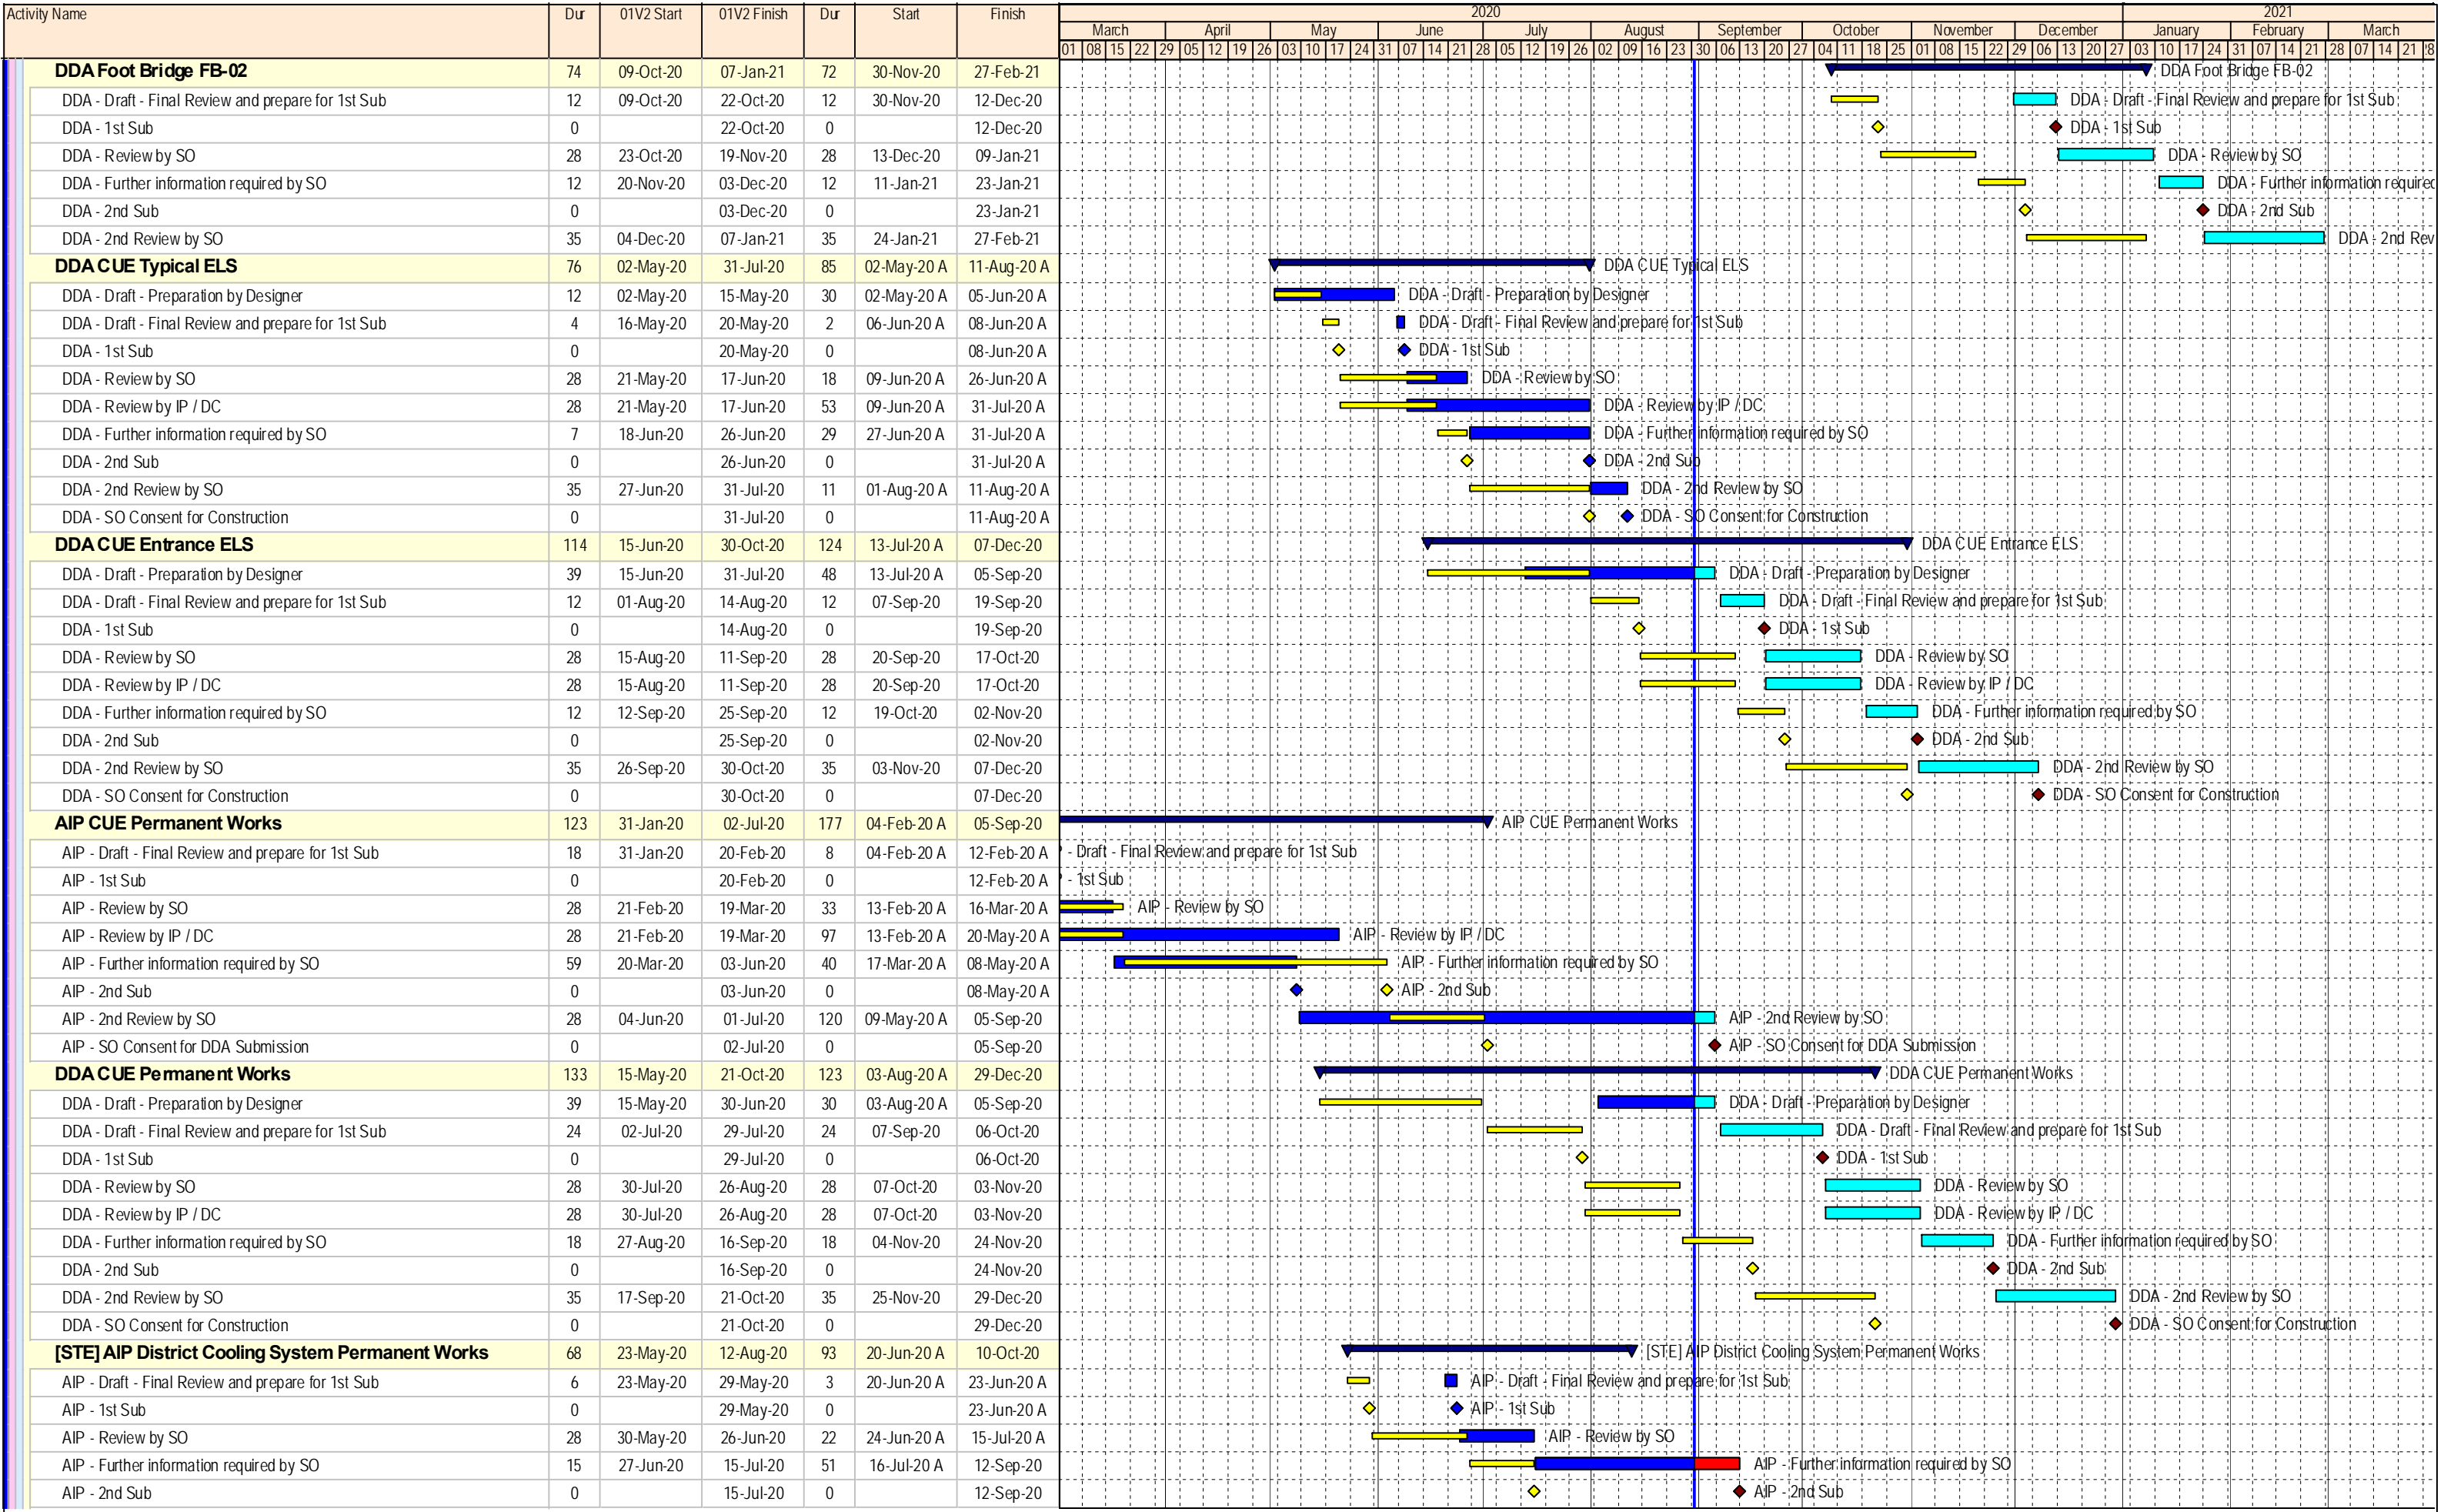


**Legend:**

- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- Planned Bar
- Critical Activity
- Actual Work
- Baseline Bar
- ▶ Summary

# ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron


## Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu





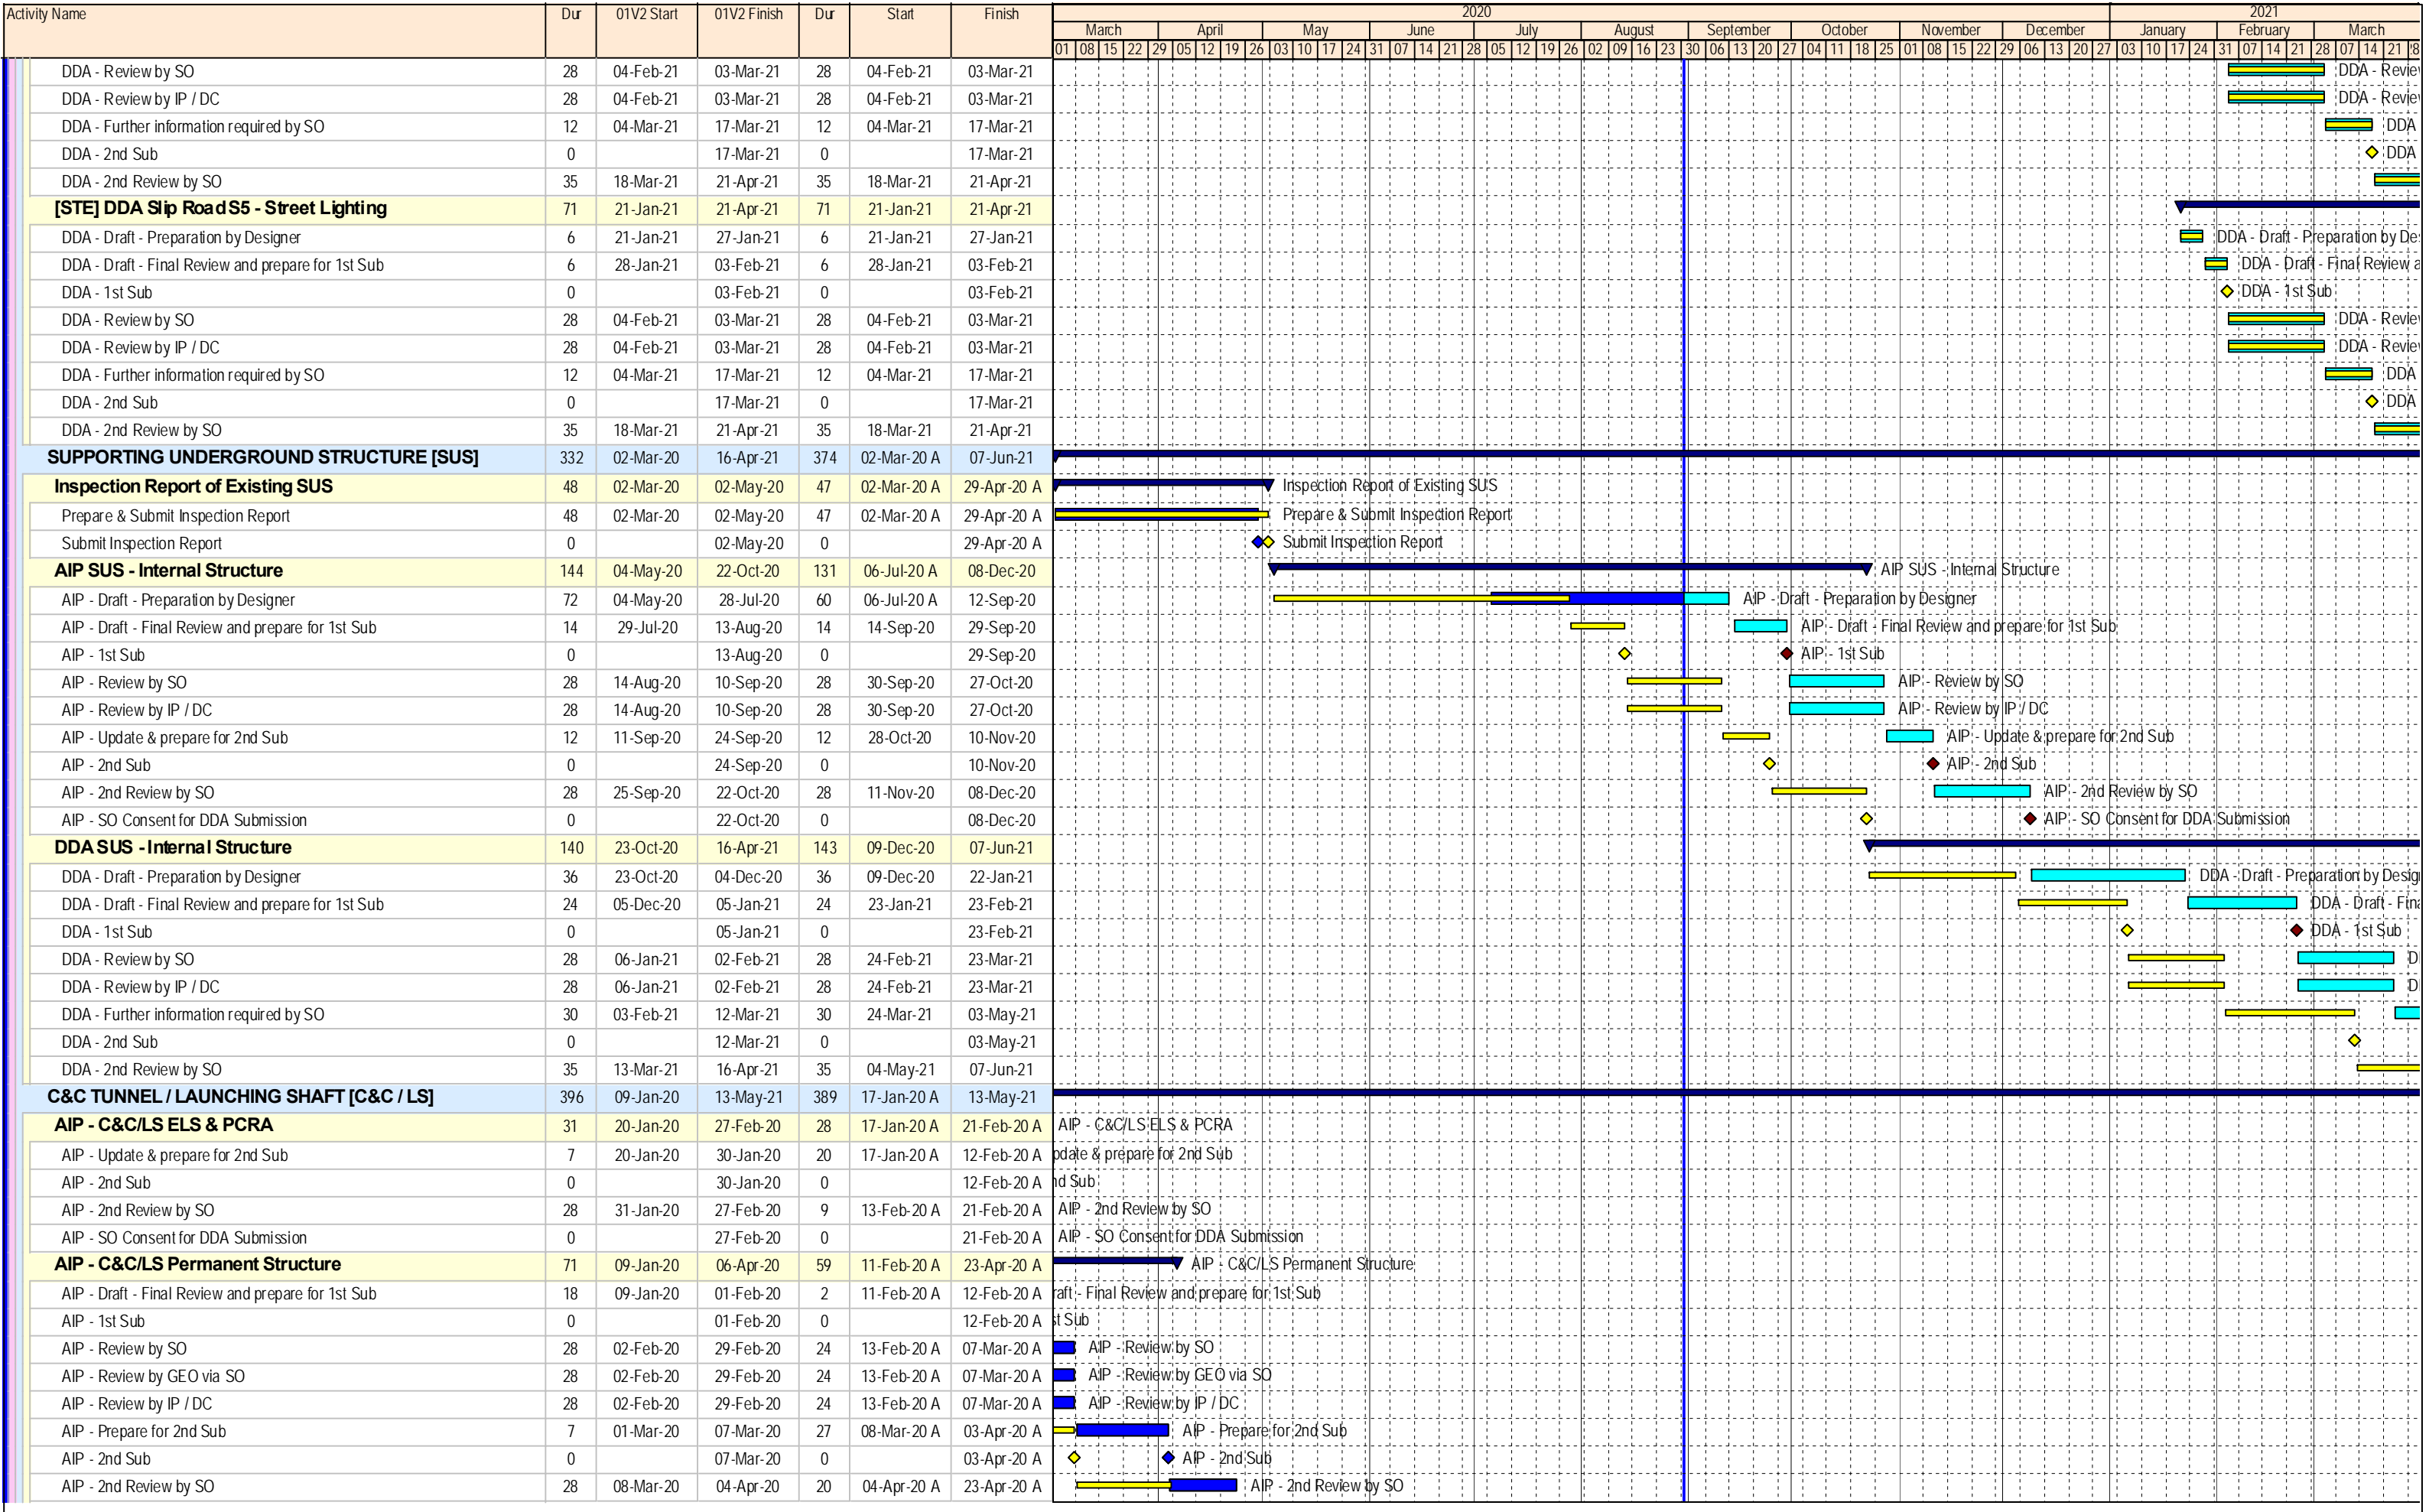


Page 14 of 30  
Data Date: 30-Aug-20

- ◆ Milestone
- ◆ Planned Bar
- ◆ Critical Activity
- ◆ Actual Milestone
- ◆ Actual Work
- ◆ Baseline Milestone
- ◆ Baseline Bar


◆ Summary

# ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

## Three Months Rolling Programme




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

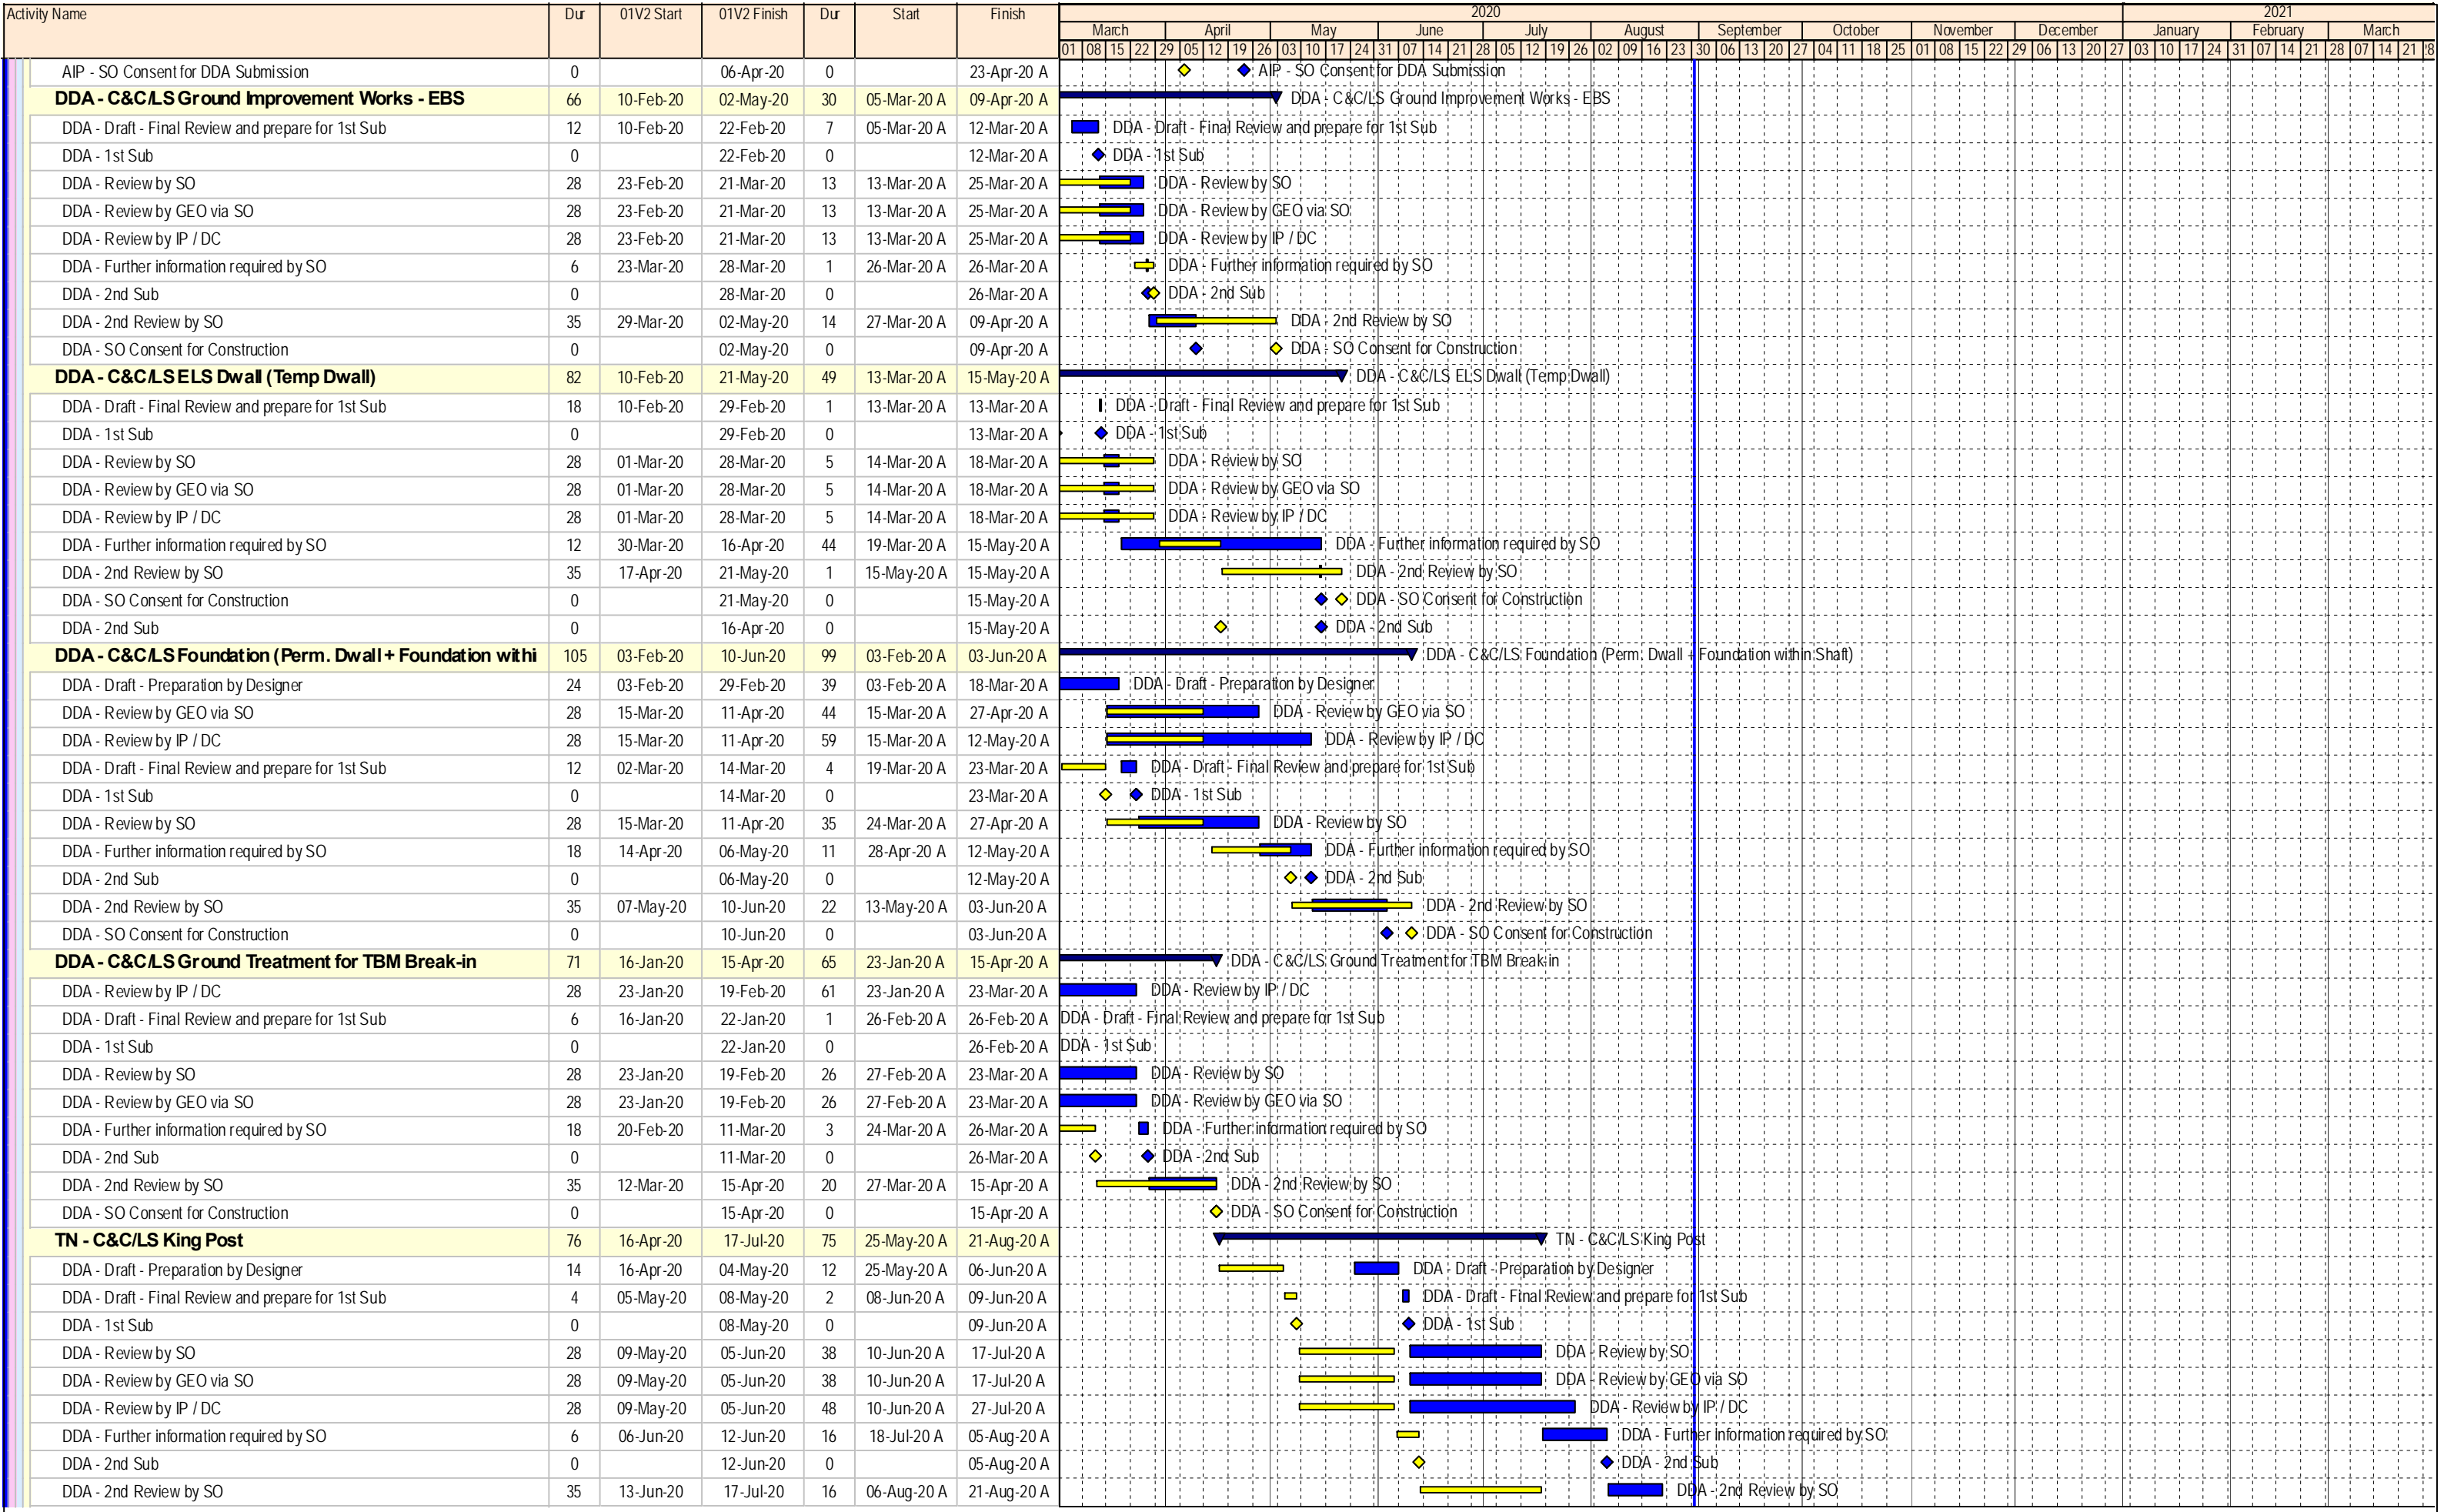


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

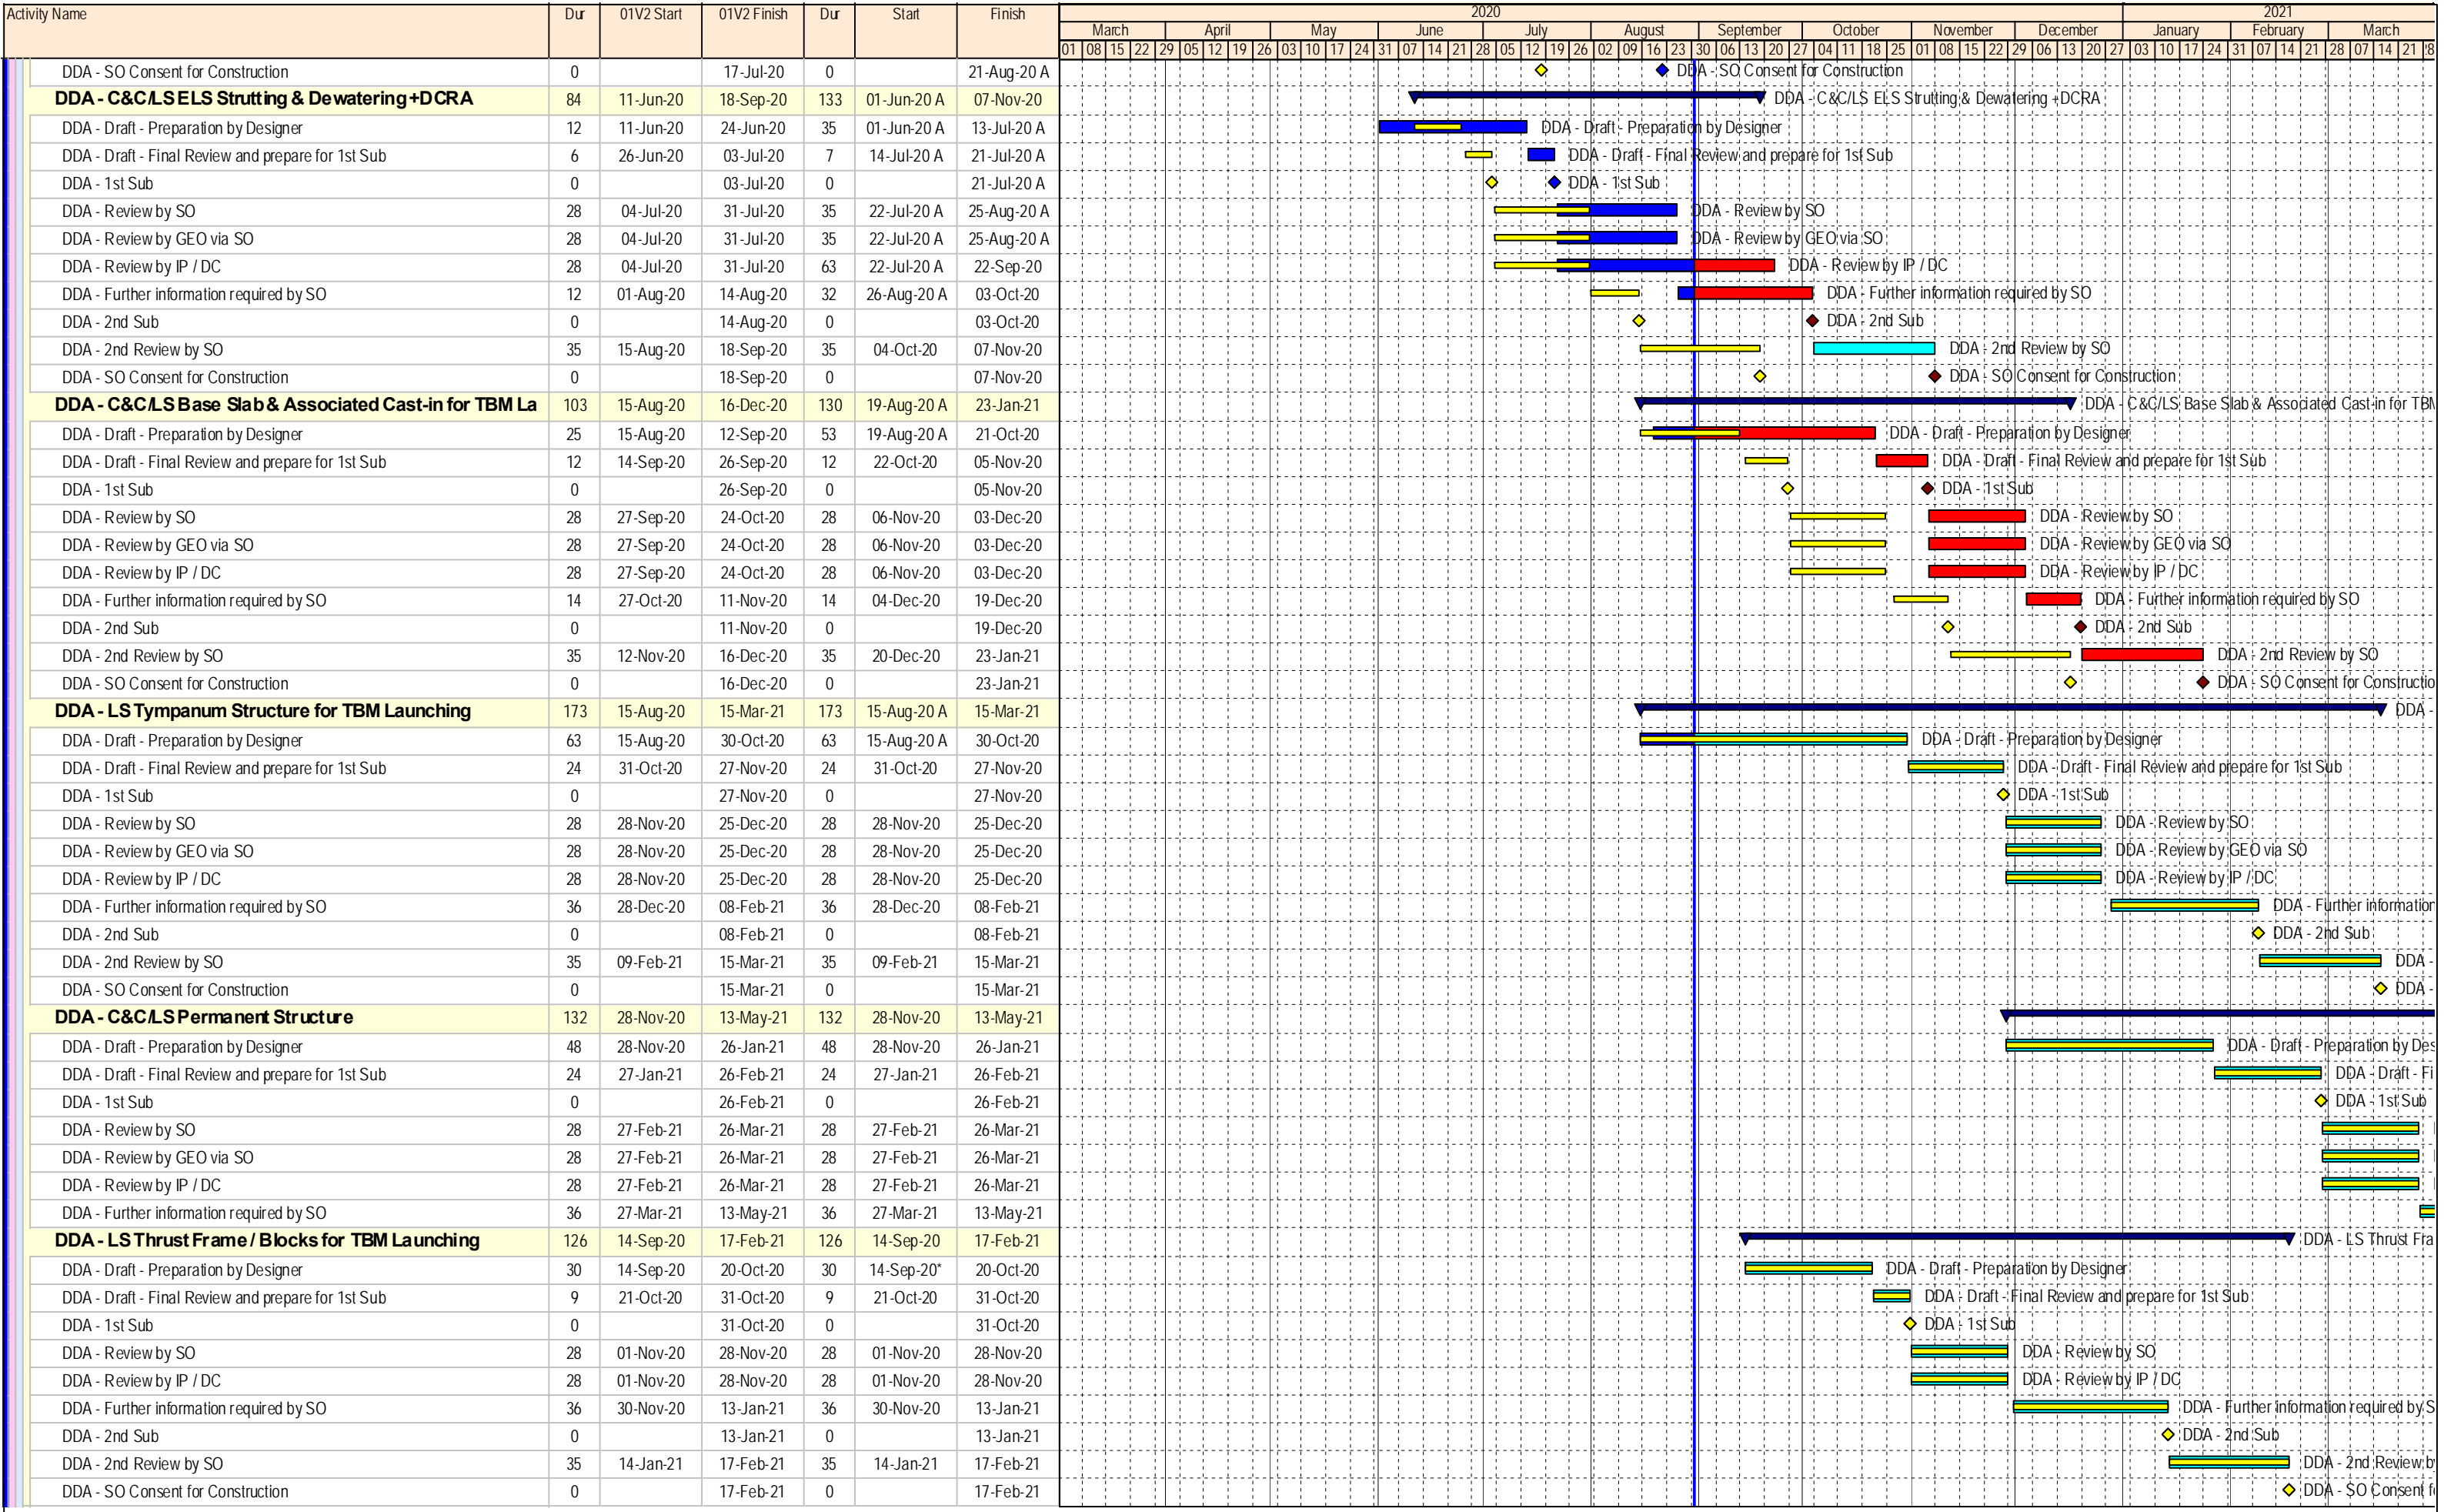

Page 16 of 30  
Data Date: 30-Aug-20


	Milestone		Summary
	Planned Bar		
	Critical Activity		
	Actual Milestone		
	Actual Work		
	Baseline Milestone		
	Baseline Bar		

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu




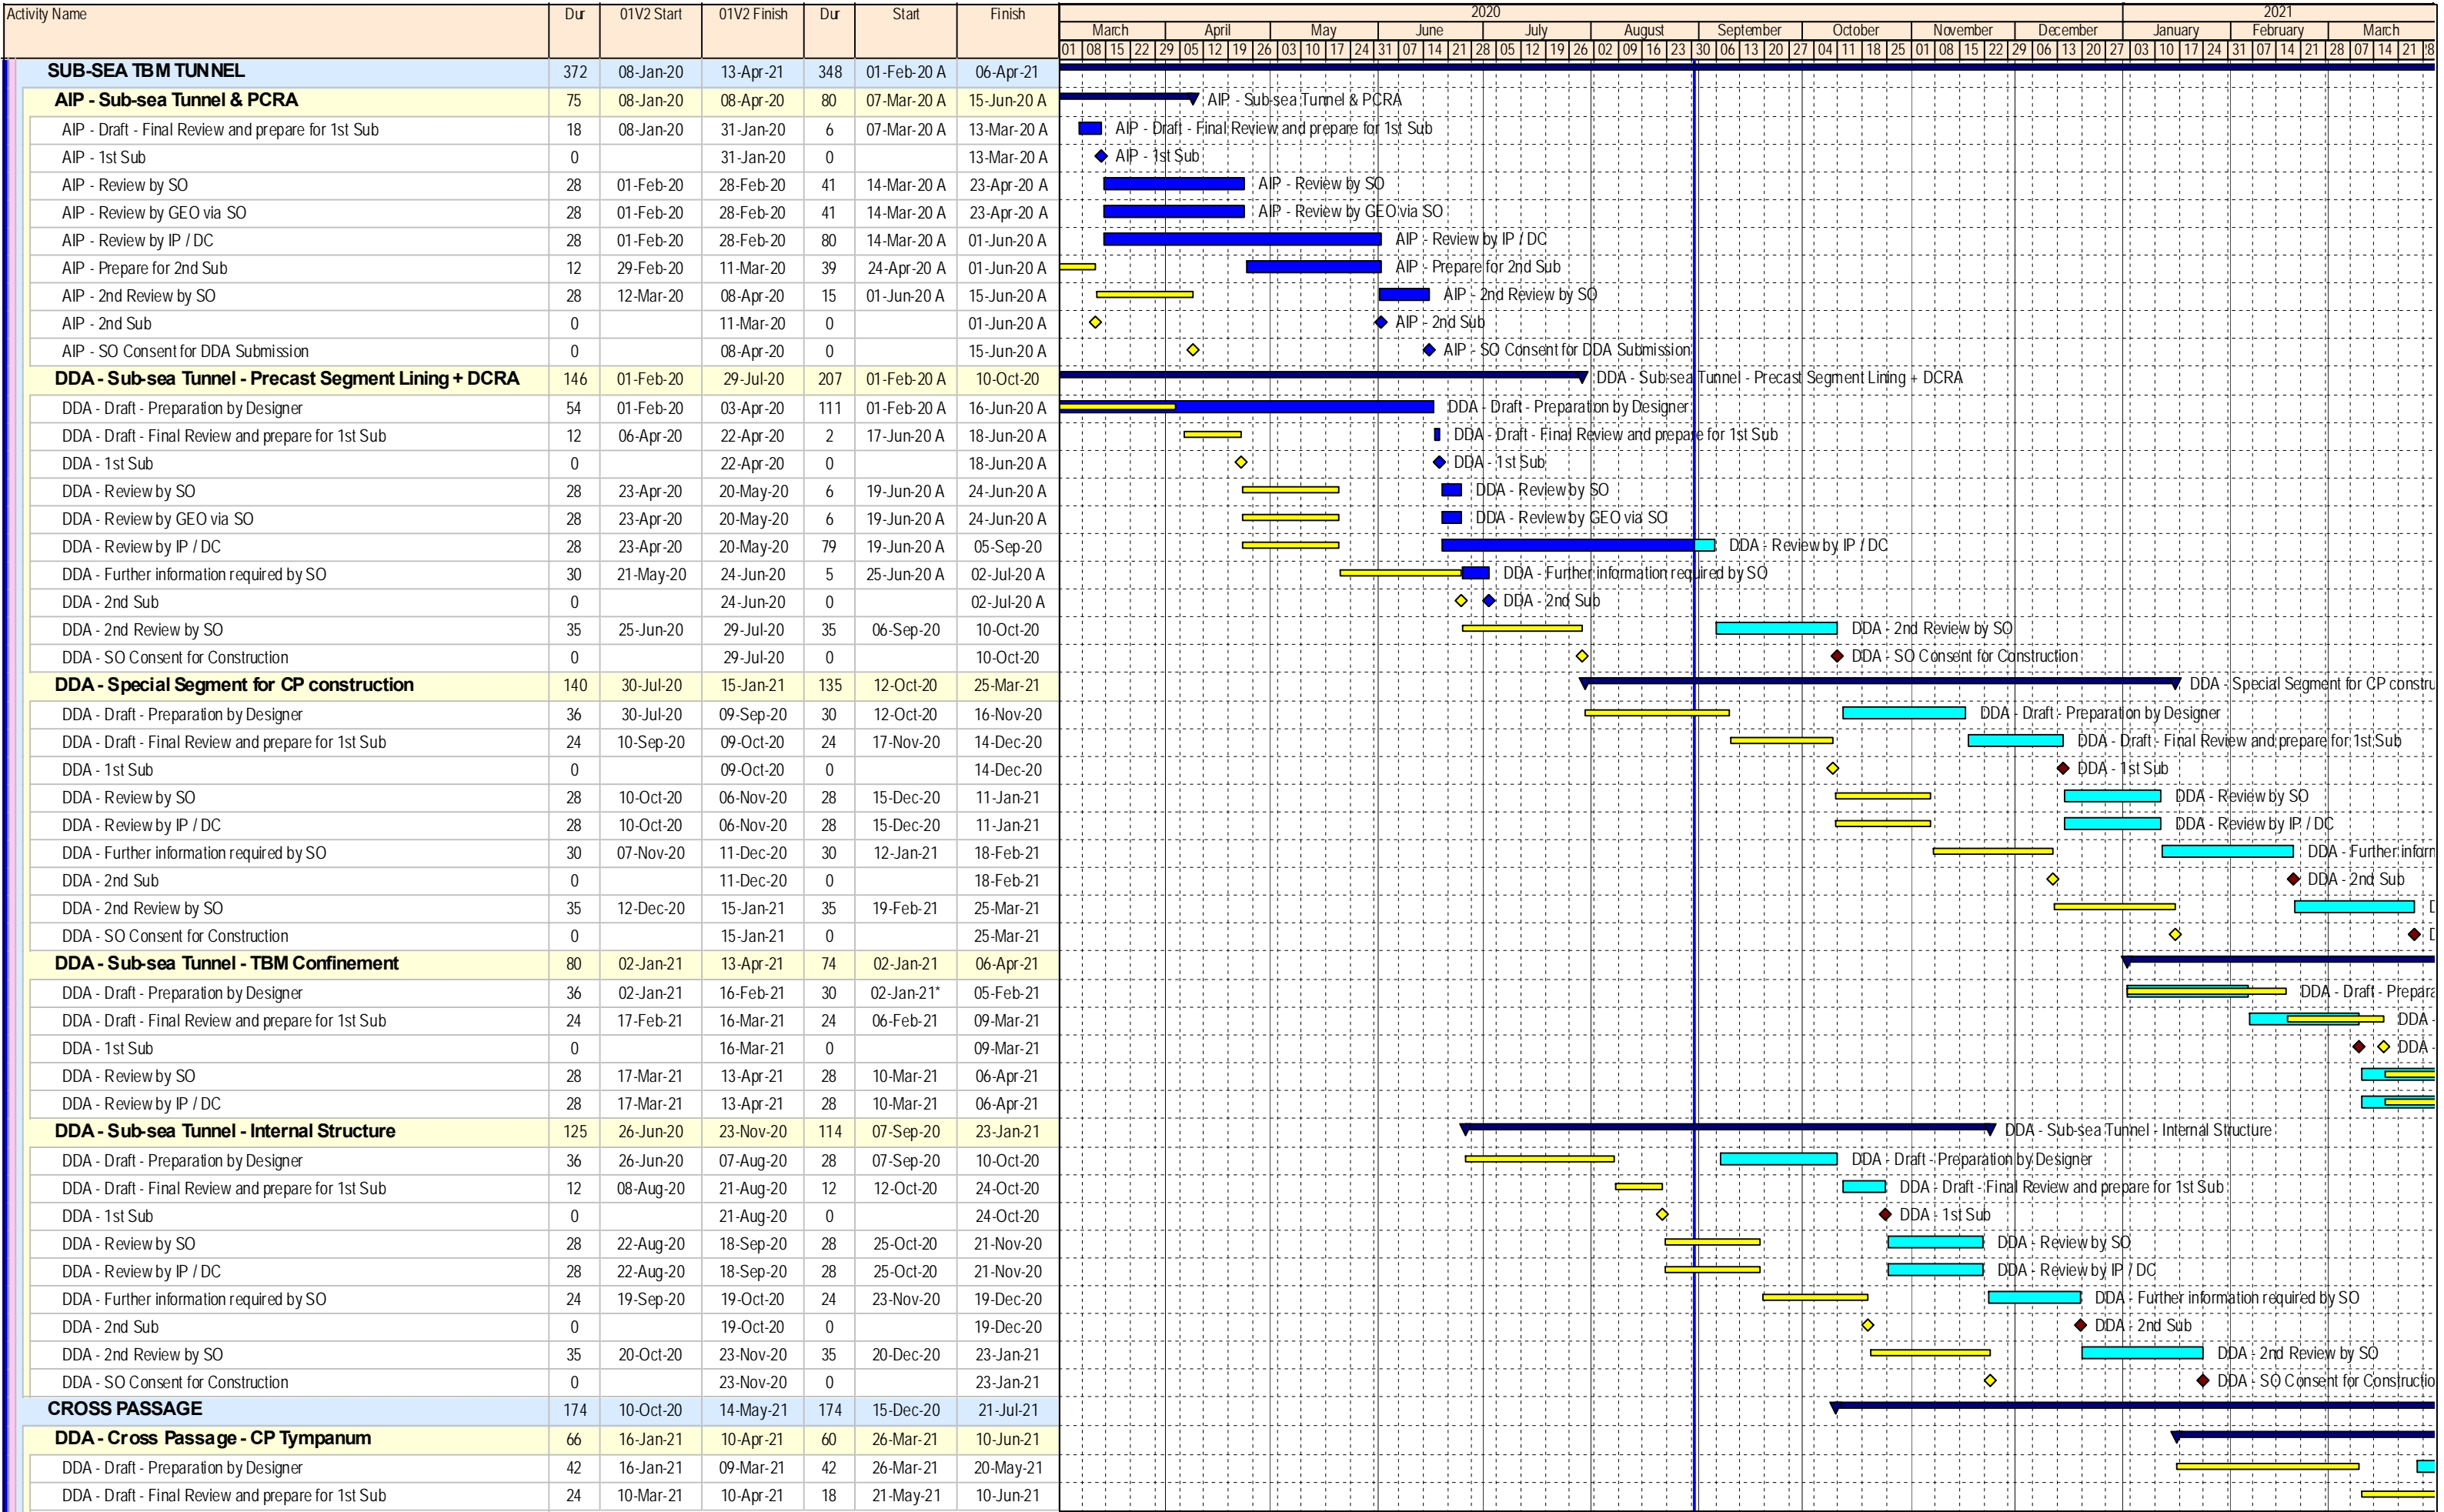

Page 17 of 30  
Data Date: 30-Aug-20


- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ▬ Actual Work
- ▬ Baseline Bar
- ▬ Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu




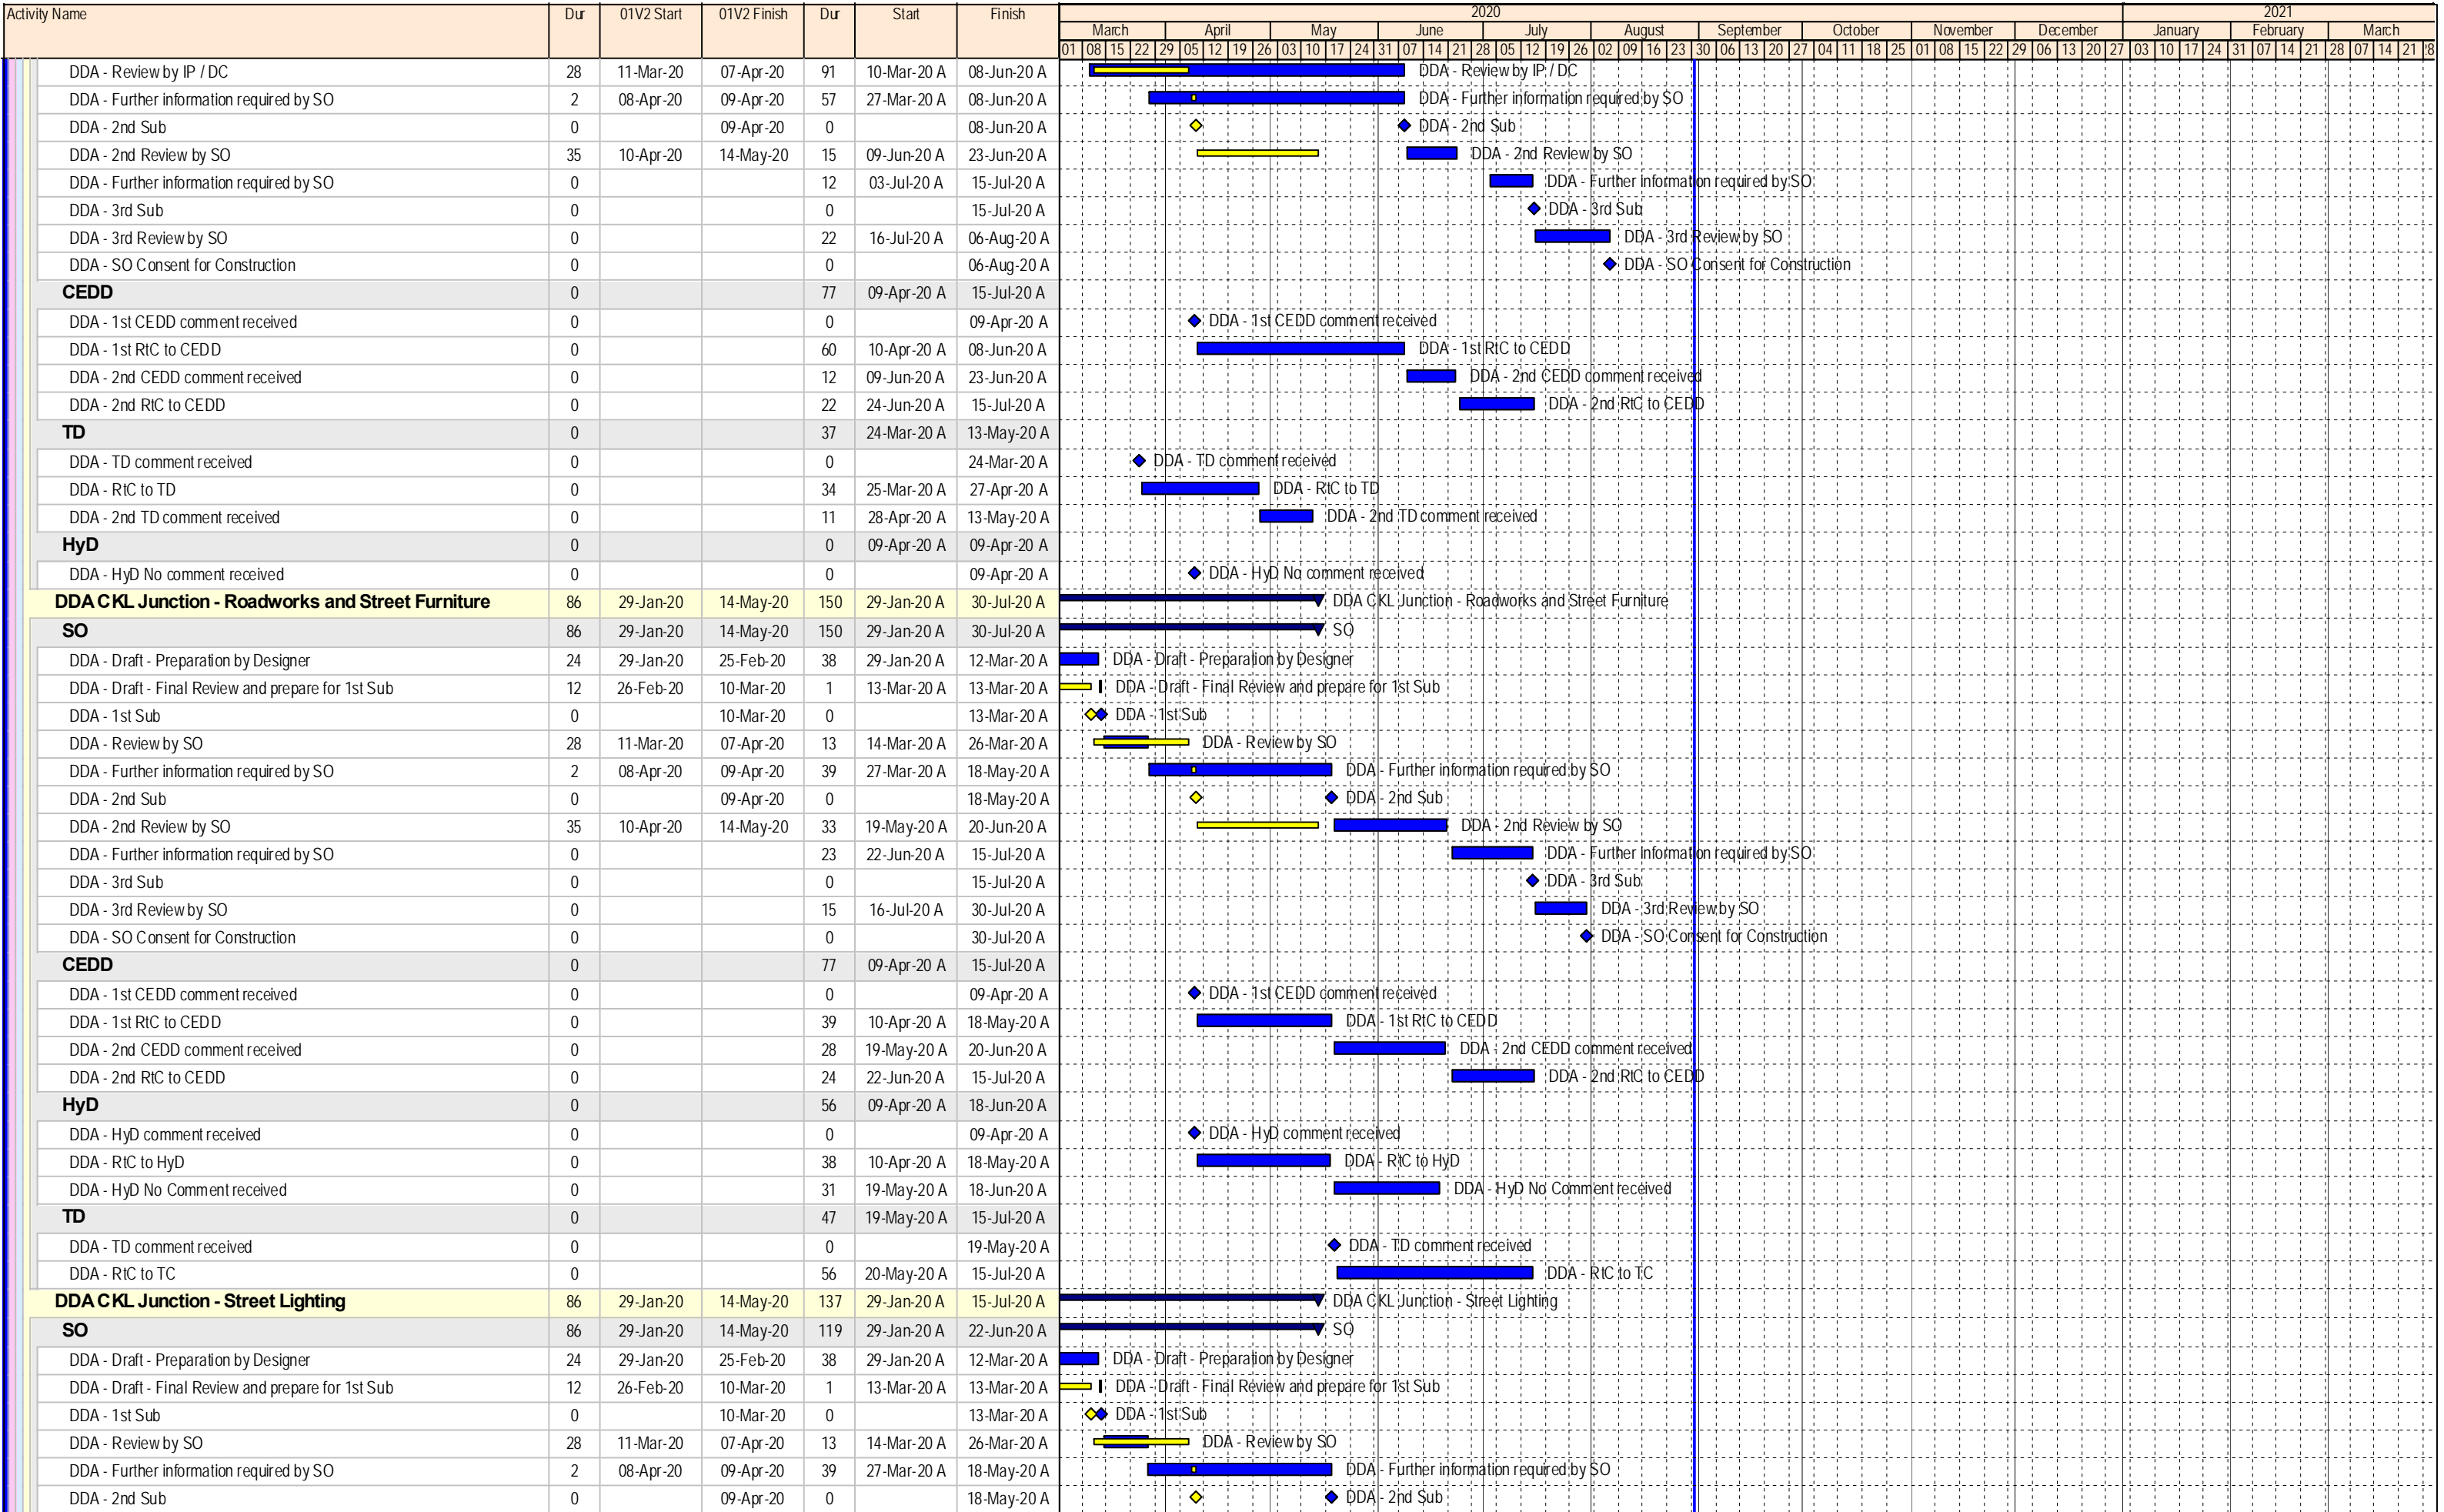

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2020																															2021		
							March	April	May	June	July	August	September	October	November	December	January	February	March																					
DDA - 2nd Review by SO	35	10-Apr-20	14-May-20	35	19-May-20 A	22-Jun-20 A	[Gantt bar]																																	
DDA - SO Consent for Construction	0		14-May-20	0		22-Jun-20 A	[Gantt bar]																																	
<b>CEDD</b>	0			29	09-Apr-20 A	19-May-20 A	[Gantt bar]																																	
DDA - CEDD comment received	0			0	09-Apr-20 A		[Gantt bar]																																	
DDA - RIC to CEDD	0			40	10-Apr-20 A	19-May-20 A	[Gantt bar]																																	
<b>HyD</b>	0			56	09-Apr-20 A	19-Jun-20 A	[Gantt bar]																																	
DDA - HyD No comment received	0			0	09-Apr-20 A		[Gantt bar]																																	
DDA - HyD No comment received	0			0		19-Jun-20 A	[Gantt bar]																																	
<b>HyD Lighting</b>	0			44	22-May-20 A	15-Jul-20 A	[Gantt bar]																																	
DDA - HyD Lighting comment received	0			0		22-May-20 A	[Gantt bar]																																	
DDA - RIC to HyD Lighting	0			54	23-May-20 A	15-Jul-20 A	[Gantt bar]																																	
<b>AIP Wai Yip Street / Wai Fat Road Junction - MOC Modifica</b>	61	16-May-20	28-Jul-20	46	08-May-20 A	02-Jul-20 A	[Gantt bar]																																	
AIP - Draft - Final Review and prepare for 1st Sub	2	16-May-20	18-May-20	7	08-May-20 A	15-May-20 A	[Gantt bar]																																	
AIP - 1st Sub	0		18-May-20	0		15-May-20 A	[Gantt bar]																																	
AIP - Review by SO	28	19-May-20	15-Jun-20	18	16-May-20 A	02-Jun-20 A	[Gantt bar]																																	
AIP - Further information required by SO	12	16-Jun-20	30-Jun-20	1	18-Jun-20 A	18-Jun-20 A	[Gantt bar]																																	
AIP - 2nd Review by SO	28	01-Jul-20	28-Jul-20	14	19-Jun-20 A	02-Jul-20 A	[Gantt bar]																																	
<b>DDA Wai Yip Street / Wai Fat Road Junction - MOC Modific</b>	70	22-Jul-20	13-Oct-20	99	12-May-20 A	05-Sep-20	[Gantt bar]																																	
<b>SOR</b>	70	22-Jul-20	13-Oct-20	99	12-May-20 A	05-Sep-20	[Gantt bar]																																	
DDA - Draft - Final Review and prepare for 1st Sub	6	22-Jul-20	28-Jul-20	4	12-May-20 A	15-May-20 A	[Gantt bar]																																	
DDA - 1st Sub	0		28-Jul-20	0		15-May-20 A	[Gantt bar]																																	
DDA - Review by SO	28	29-Jul-20	25-Aug-20	20	16-May-20 A	04-Jun-20 A	[Gantt bar]																																	
DDA - Further information required by SO	12	26-Aug-20	08-Sep-20	12	05-Jun-20 A	18-Jun-20 A	[Gantt bar]																																	
DDA - 2nd Sub	0		08-Sep-20	0		18-Jun-20 A	[Gantt bar]																																	
DDA - 2nd Review by SO	35	09-Sep-20	13-Oct-20	14	19-Jun-20 A	02-Jul-20 A	[Gantt bar]																																	
DDA - Further information required by SO	0			12	03-Jul-20 A	15-Jul-20 A	[Gantt bar]																																	
DDA - 3rd Sub	0			0		15-Jul-20 A	[Gantt bar]																																	
DDA - 3rd Review by SO	0			52	16-Jul-20 A	05-Sep-20	[Gantt bar]																																	
DDA - SO Consent for Construction	0		13-Oct-20	0		05-Sep-20	[Gantt bar]																																	
<b>HyD</b>	0			76	01-Jun-20 A	31-Aug-20	[Gantt bar]																																	
DDA - HyD comment received	0			0		01-Jun-20 A	[Gantt bar]																																	
DDA - RIC to Hyd under preparation	0			91	02-Jun-20 A	31-Aug-20	[Gantt bar]																																	
<b>TD</b>	0			58	23-Jun-20 A	31-Aug-20	[Gantt bar]																																	
DDA - TD comment received	0			0		23-Jun-20 A	[Gantt bar]																																	
DDA - RIC to TD	0			22	24-Jun-20 A	15-Jul-20 A	[Gantt bar]																																	
DDA - Under review by TD	0			47	16-Jul-20 A	31-Aug-20	[Gantt bar]																																	
<b>DRILL &amp; BREAK [D&amp;BR] / DRILL &amp; BLAST TUNNEL [D&amp;BL]</b>	210	08-Jan-20	22-Sep-20	294	31-Dec-19 A	28-Dec-20	[Gantt bar]																																	
<b>AIP - D&amp;BR / D&amp;BL Tunnel &amp; PCRA (with Temp. Support)</b>	52	08-Jan-20	12-Mar-20	81	31-Dec-19 A	09-Apr-20 A	[Gantt bar]																																	
AIP - 1st Sub	0		08-Jan-20	0		31-Dec-19 A	[Gantt bar]																																	
AIP - Review by SO	28	09-Jan-20	05-Feb-20	47	02-Jan-20 A	17-Feb-20 A	[Gantt bar]																																	
AIP - Review by IP / DC	28	09-Jan-20	05-Feb-20	47	02-Jan-20 A	17-Feb-20 A	[Gantt bar]																																	
AIP - Update & prepare for 2nd Sub	7	06-Feb-20	13-Feb-20	25	18-Feb-20 A	17-Mar-20 A	[Gantt bar]																																	
AIP - 2nd Sub	0		13-Feb-20	0		17-Mar-20 A	[Gantt bar]																																	
AIP - 2nd Review by SO	28	14-Feb-20	12-Mar-20	23	18-Mar-20 A	09-Apr-20 A	[Gantt bar]																																	
AIP - SO Consent for DDA Submission	0		12-Mar-20	0		09-Apr-20 A	[Gantt bar]																																	
<b>AIP - D&amp;BR / D&amp;BL Permanent Structure</b>	115	09-Jan-20	01-Jun-20	196	09-Jan-20 A	07-Sep-20	[Gantt bar]																																	
AIP - Draft - Preparation by Designer	41	09-Jan-20	28-Feb-20	49	09-Jan-20 A	09-Mar-20 A	[Gantt bar]																																	
AIP - Draft - Final Review and prepare for 1st Sub	18	29-Feb-20	20-Mar-20	4	10-Mar-20 A	13-Mar-20 A	[Gantt bar]																																	
AIP - 1st Sub	0		20-Mar-20	0		13-Mar-20 A	[Gantt bar]																																	
AIP - Review by SO	28	21-Mar-20	17-Apr-20	38	14-Mar-20 A	20-Apr-20 A	[Gantt bar]																																	
AIP - Review by IP / DC	28	21-Mar-20	17-Apr-20	106	14-Mar-20 A	27-Jun-20 A	[Gantt bar]																																	
AIP - Update & prepare for 2nd Sub	12	18-Apr-20	04-May-20	2	29-Jun-20 A	30-Jun-20 A	[Gantt bar]																																	


Page 20 of 30  
Data Date: 30-Aug-20

- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

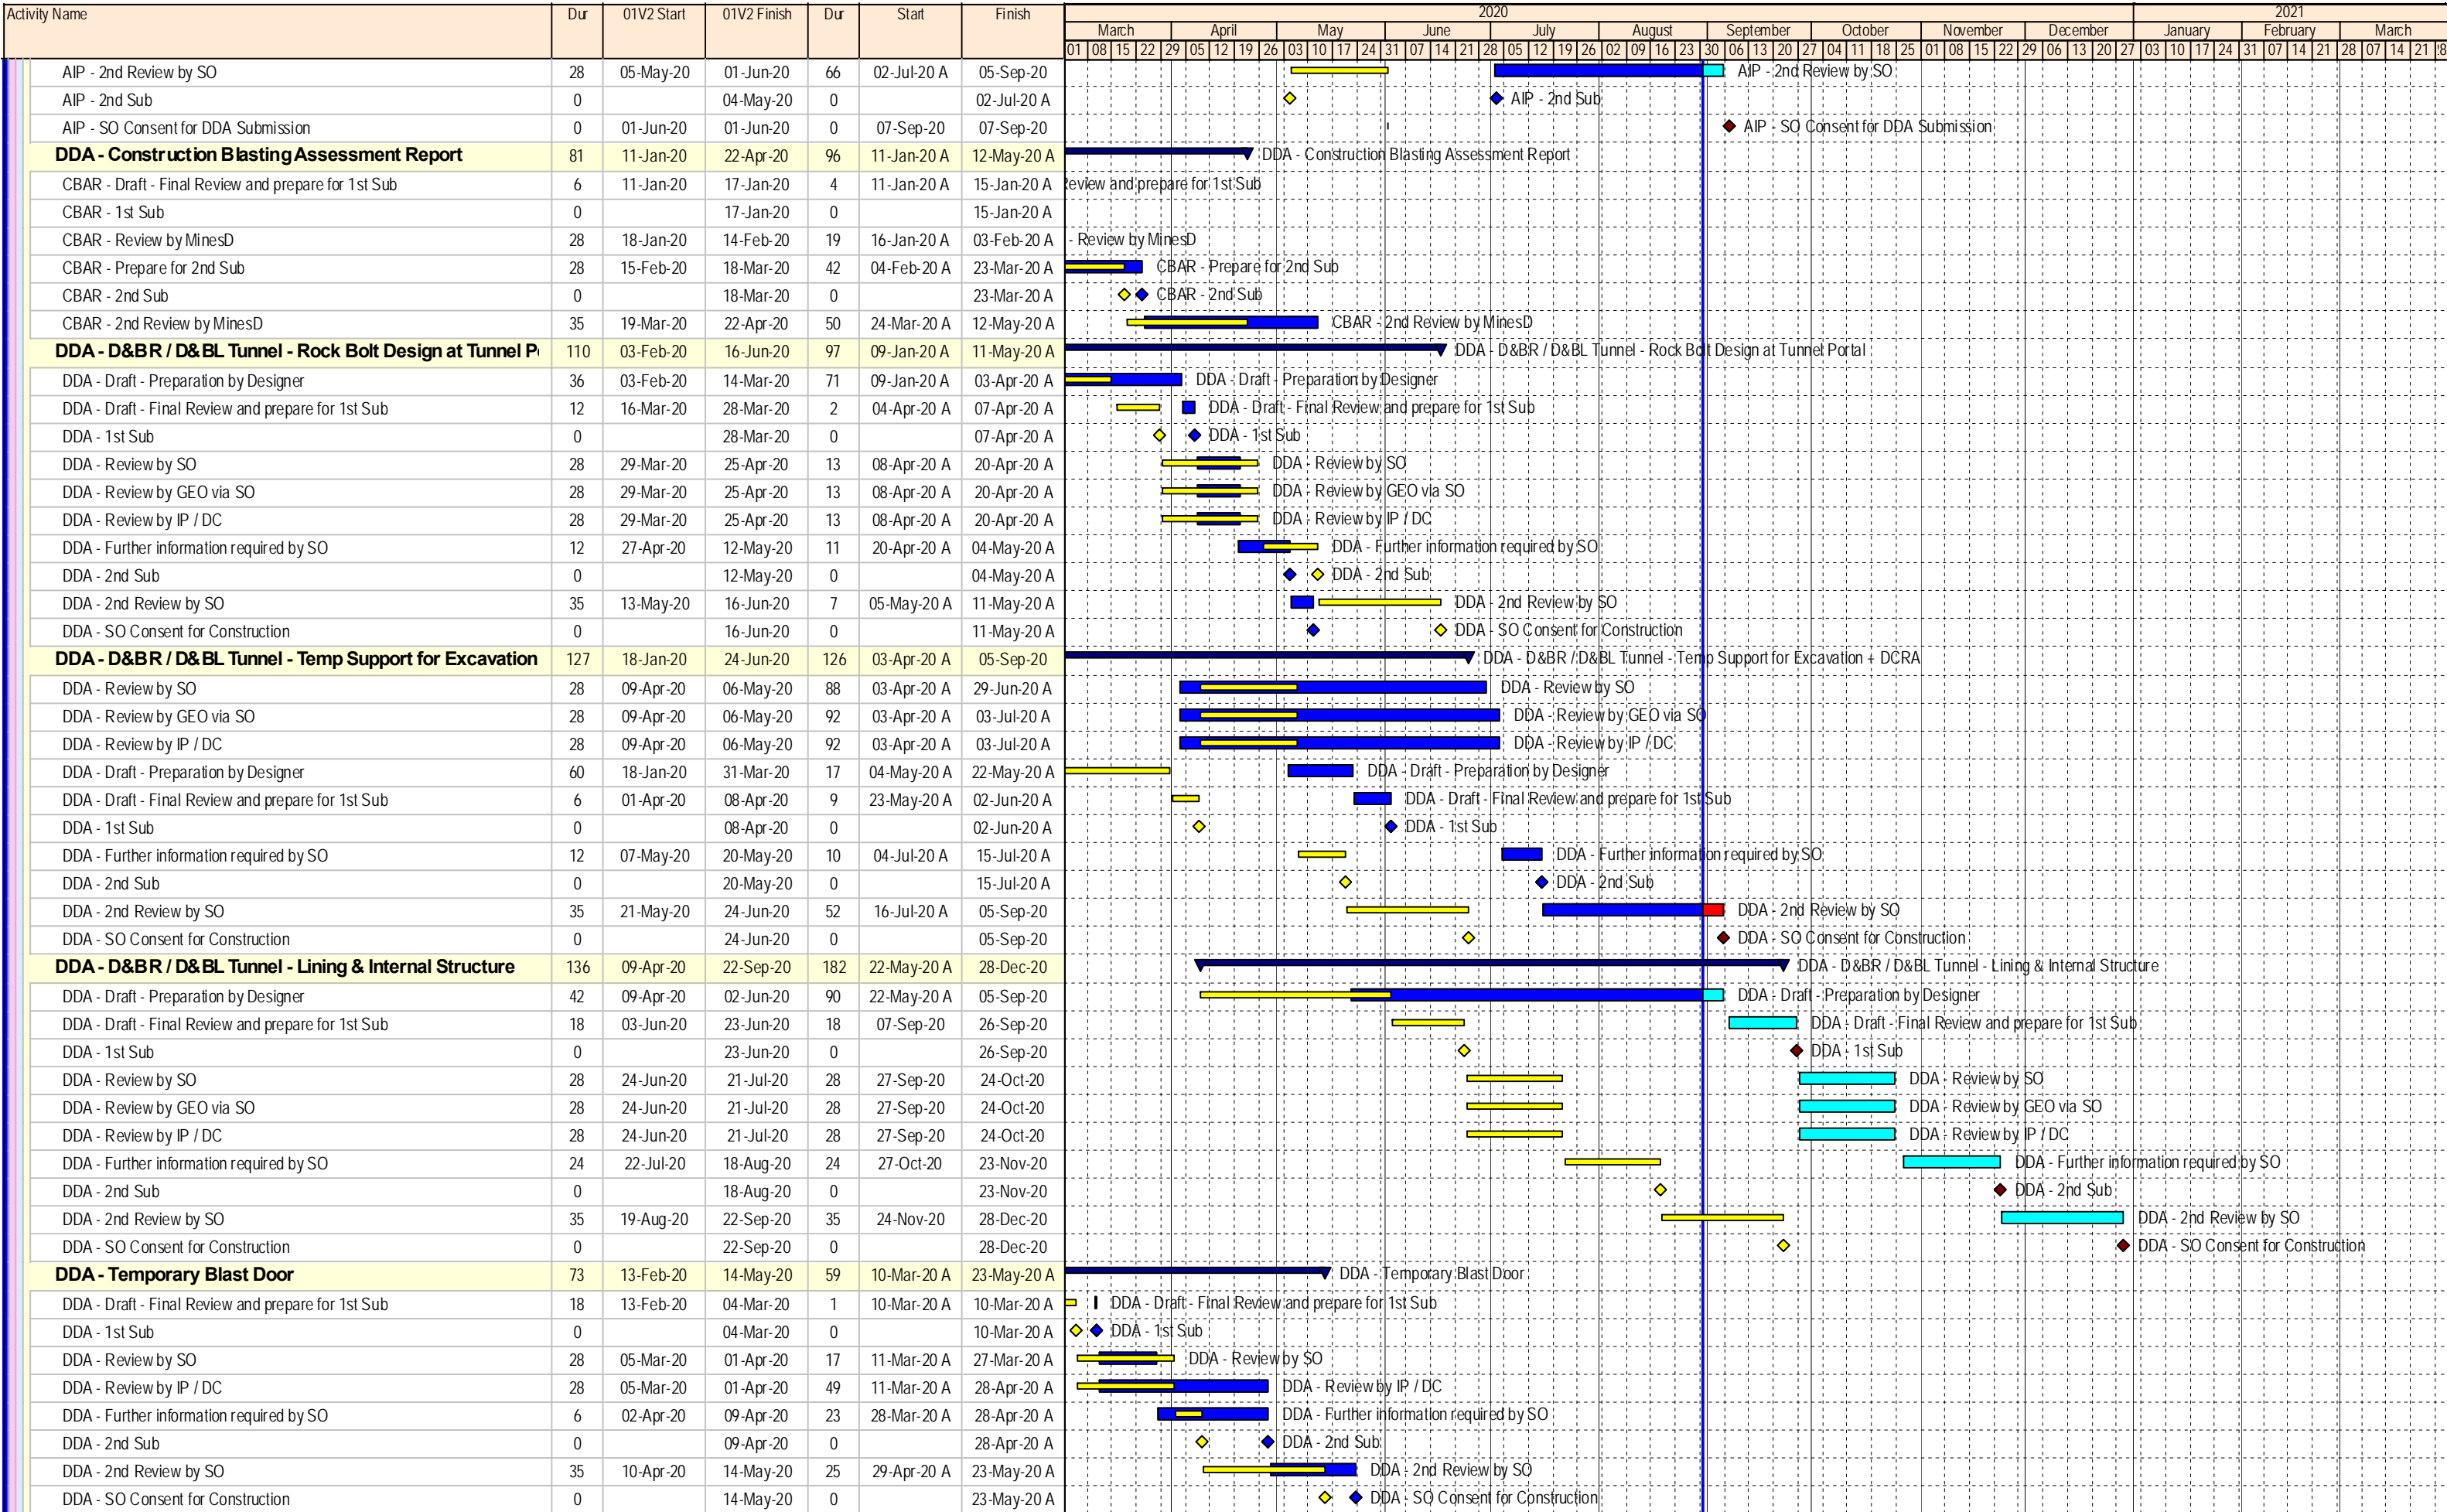


Page 21 of 30  
Data Date: 30-Aug-20

- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- ◆ Summary
- Planned Bar
- Critical Activity
- Actual Work
- Baseline Bar

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

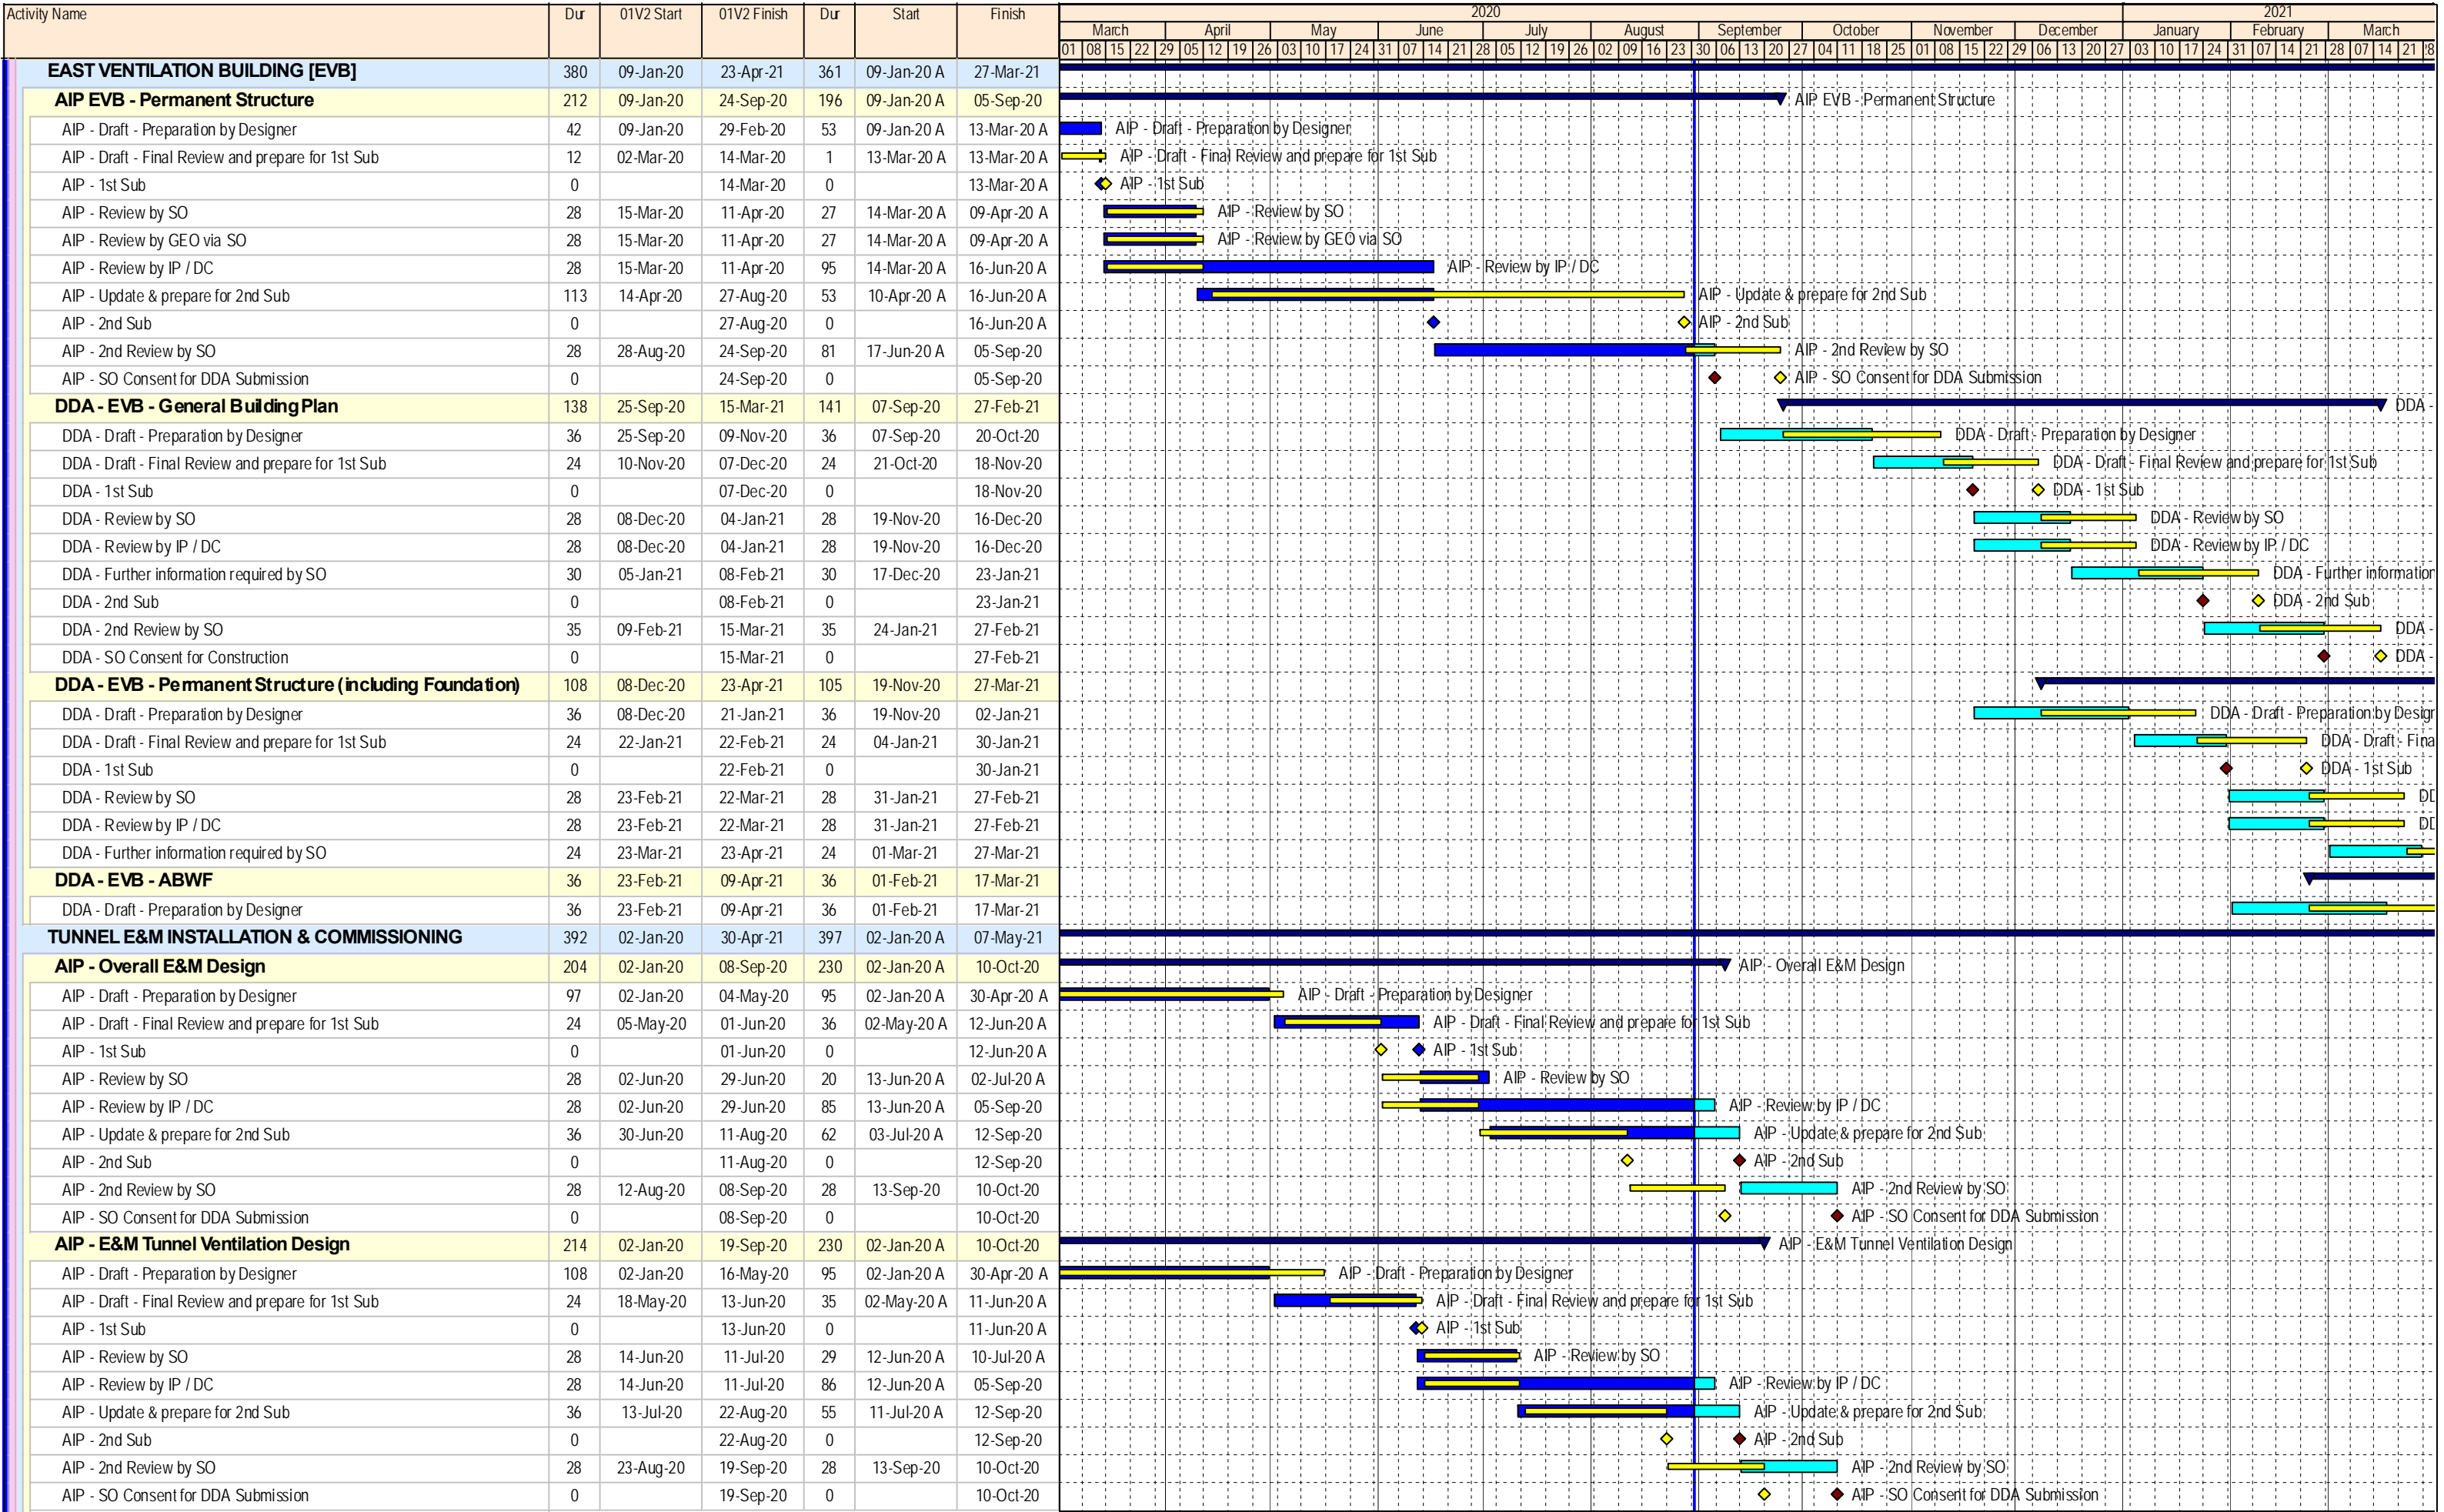


Page 22 of 30  
Data Date: 30-Aug-20

- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar


Summary ▬

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

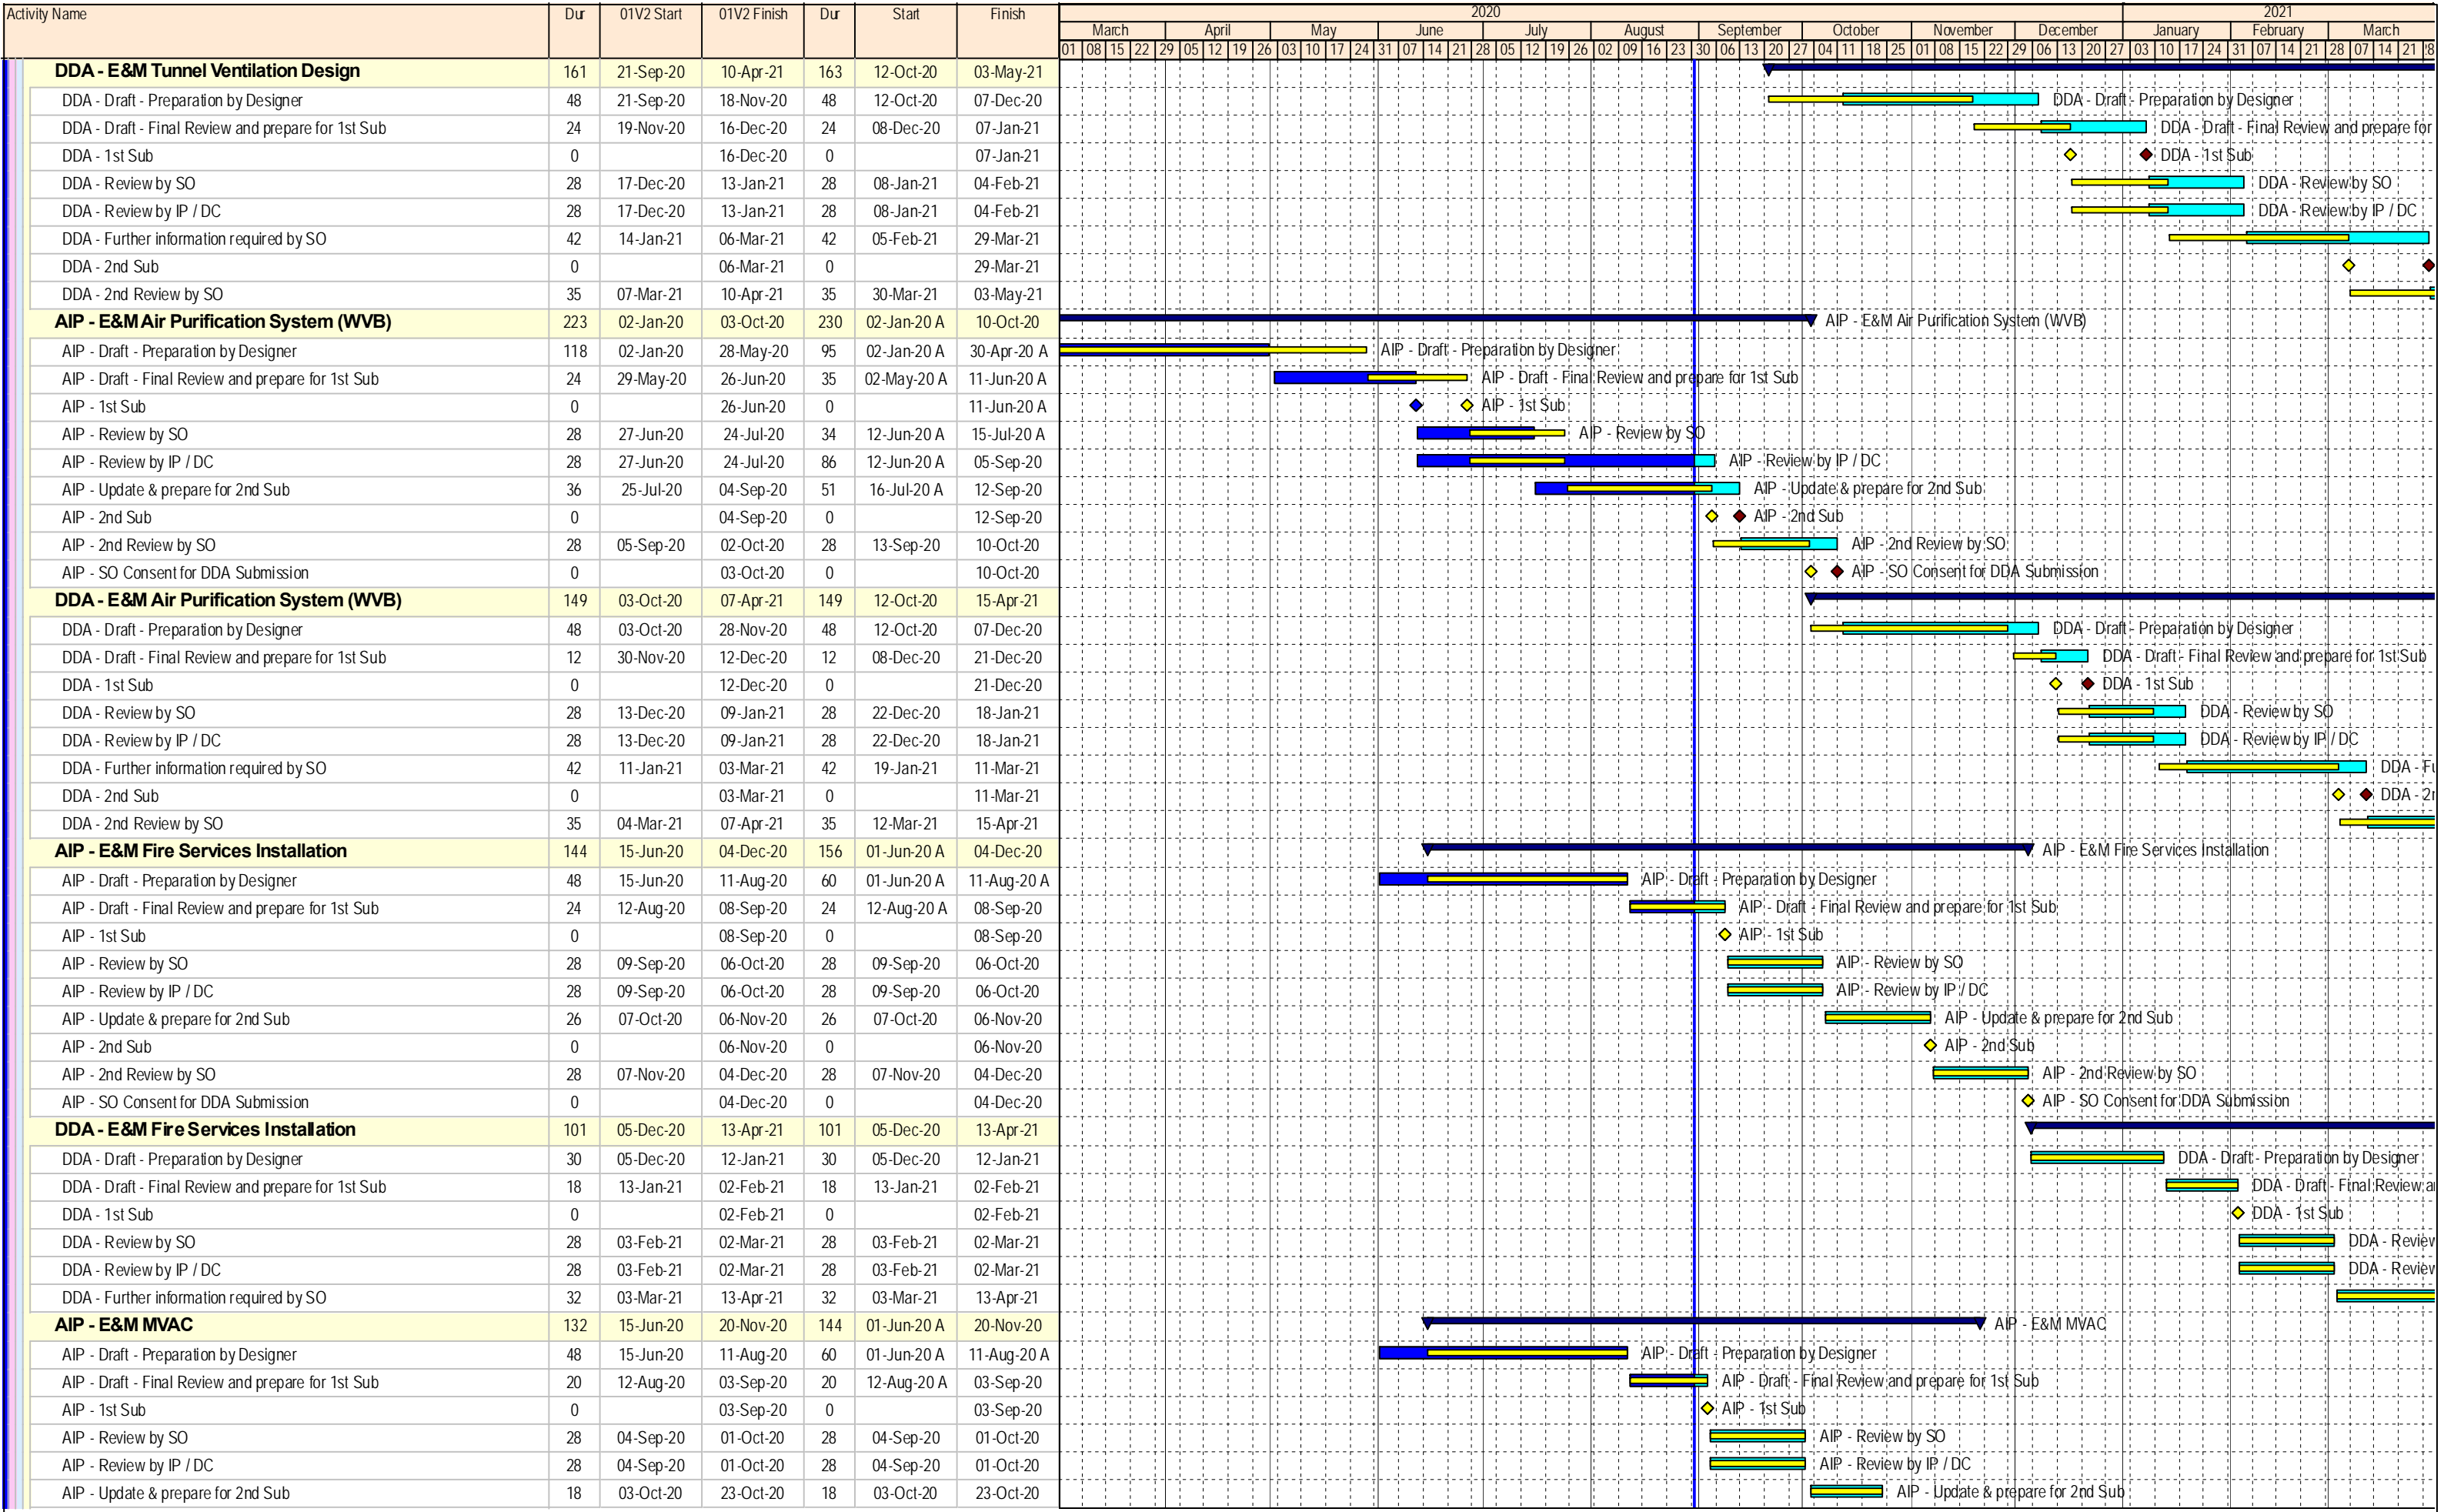

Page 23 of 30 Data Date: 30-Aug-20			<h2 style="text-align: center;">ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron</h2> <h3 style="text-align: center;">Three Months Rolling Programme</h3>			Date	Revision	Checked	Approved
						05-Nov-19	00V0	WYu	
						18-Dec-19	00V1	WYu	
						22-Feb-20	01V0	SPa/LLo	WYu
						09-Apr-20	01V1	SPa/LLo	WYu
						17-Jul-20	01V2	SPa/LLo	WYu





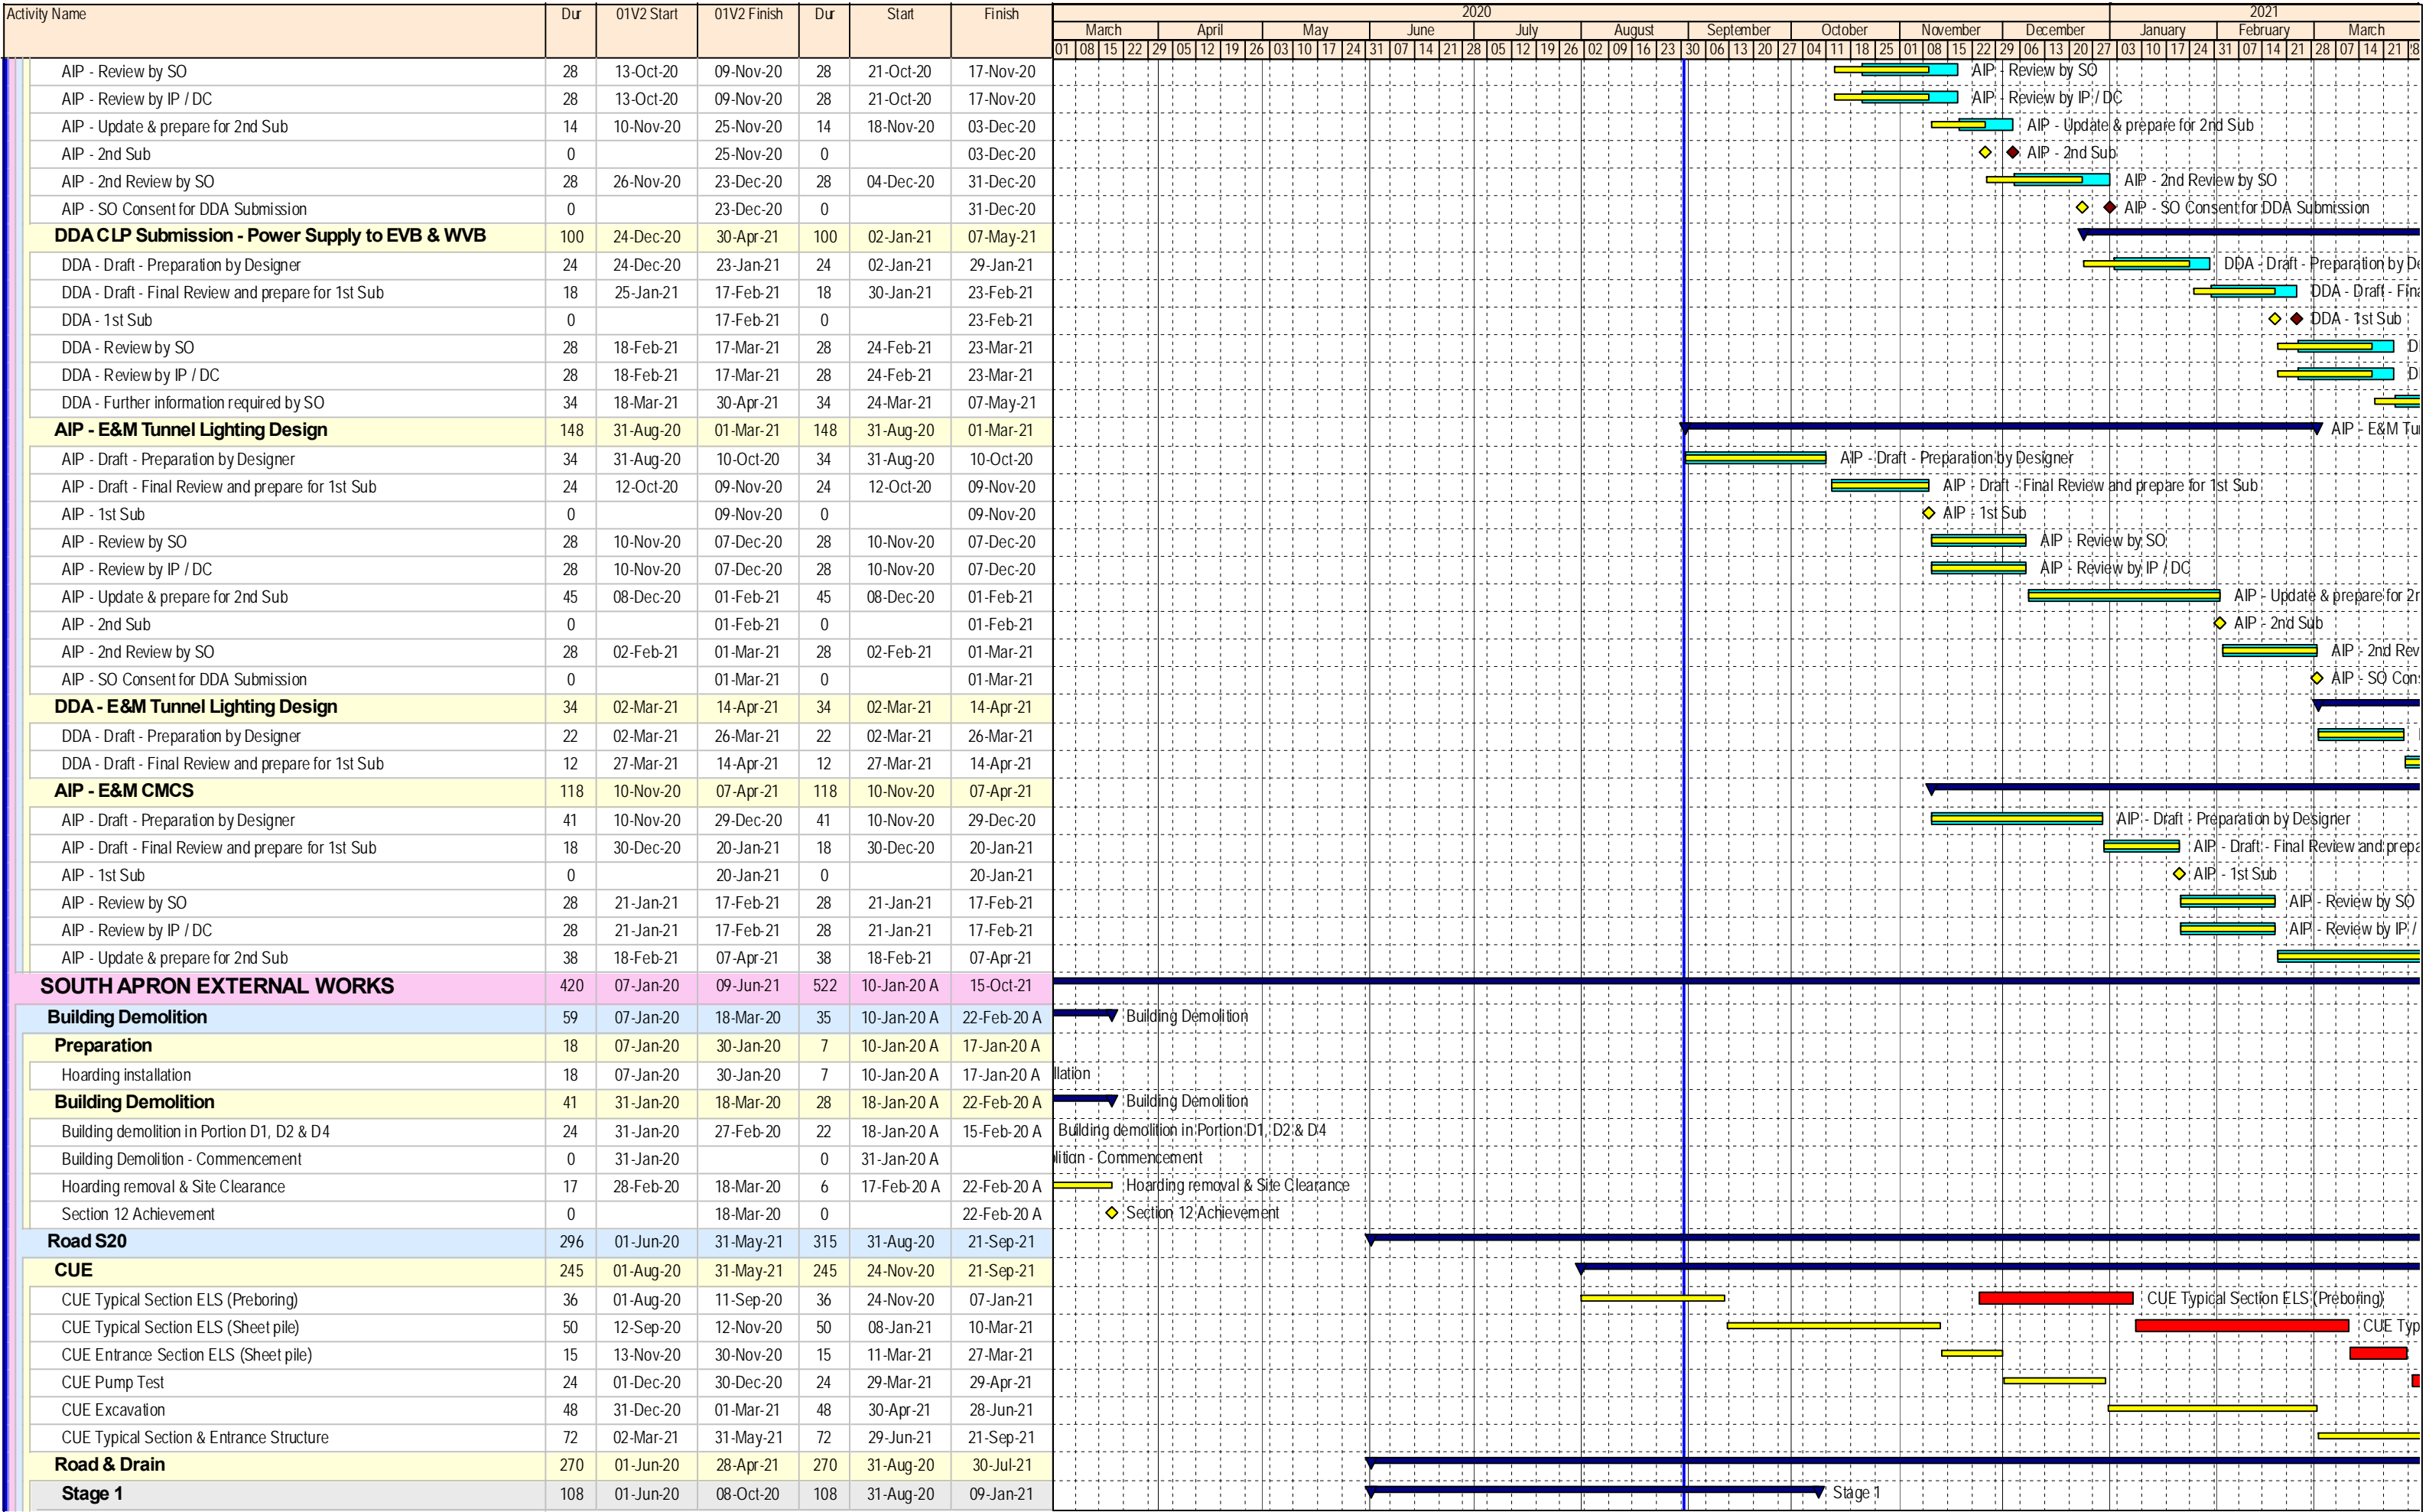

Page 25 of 30  
Data Date: 30-Aug-20

- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar


## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

### Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu



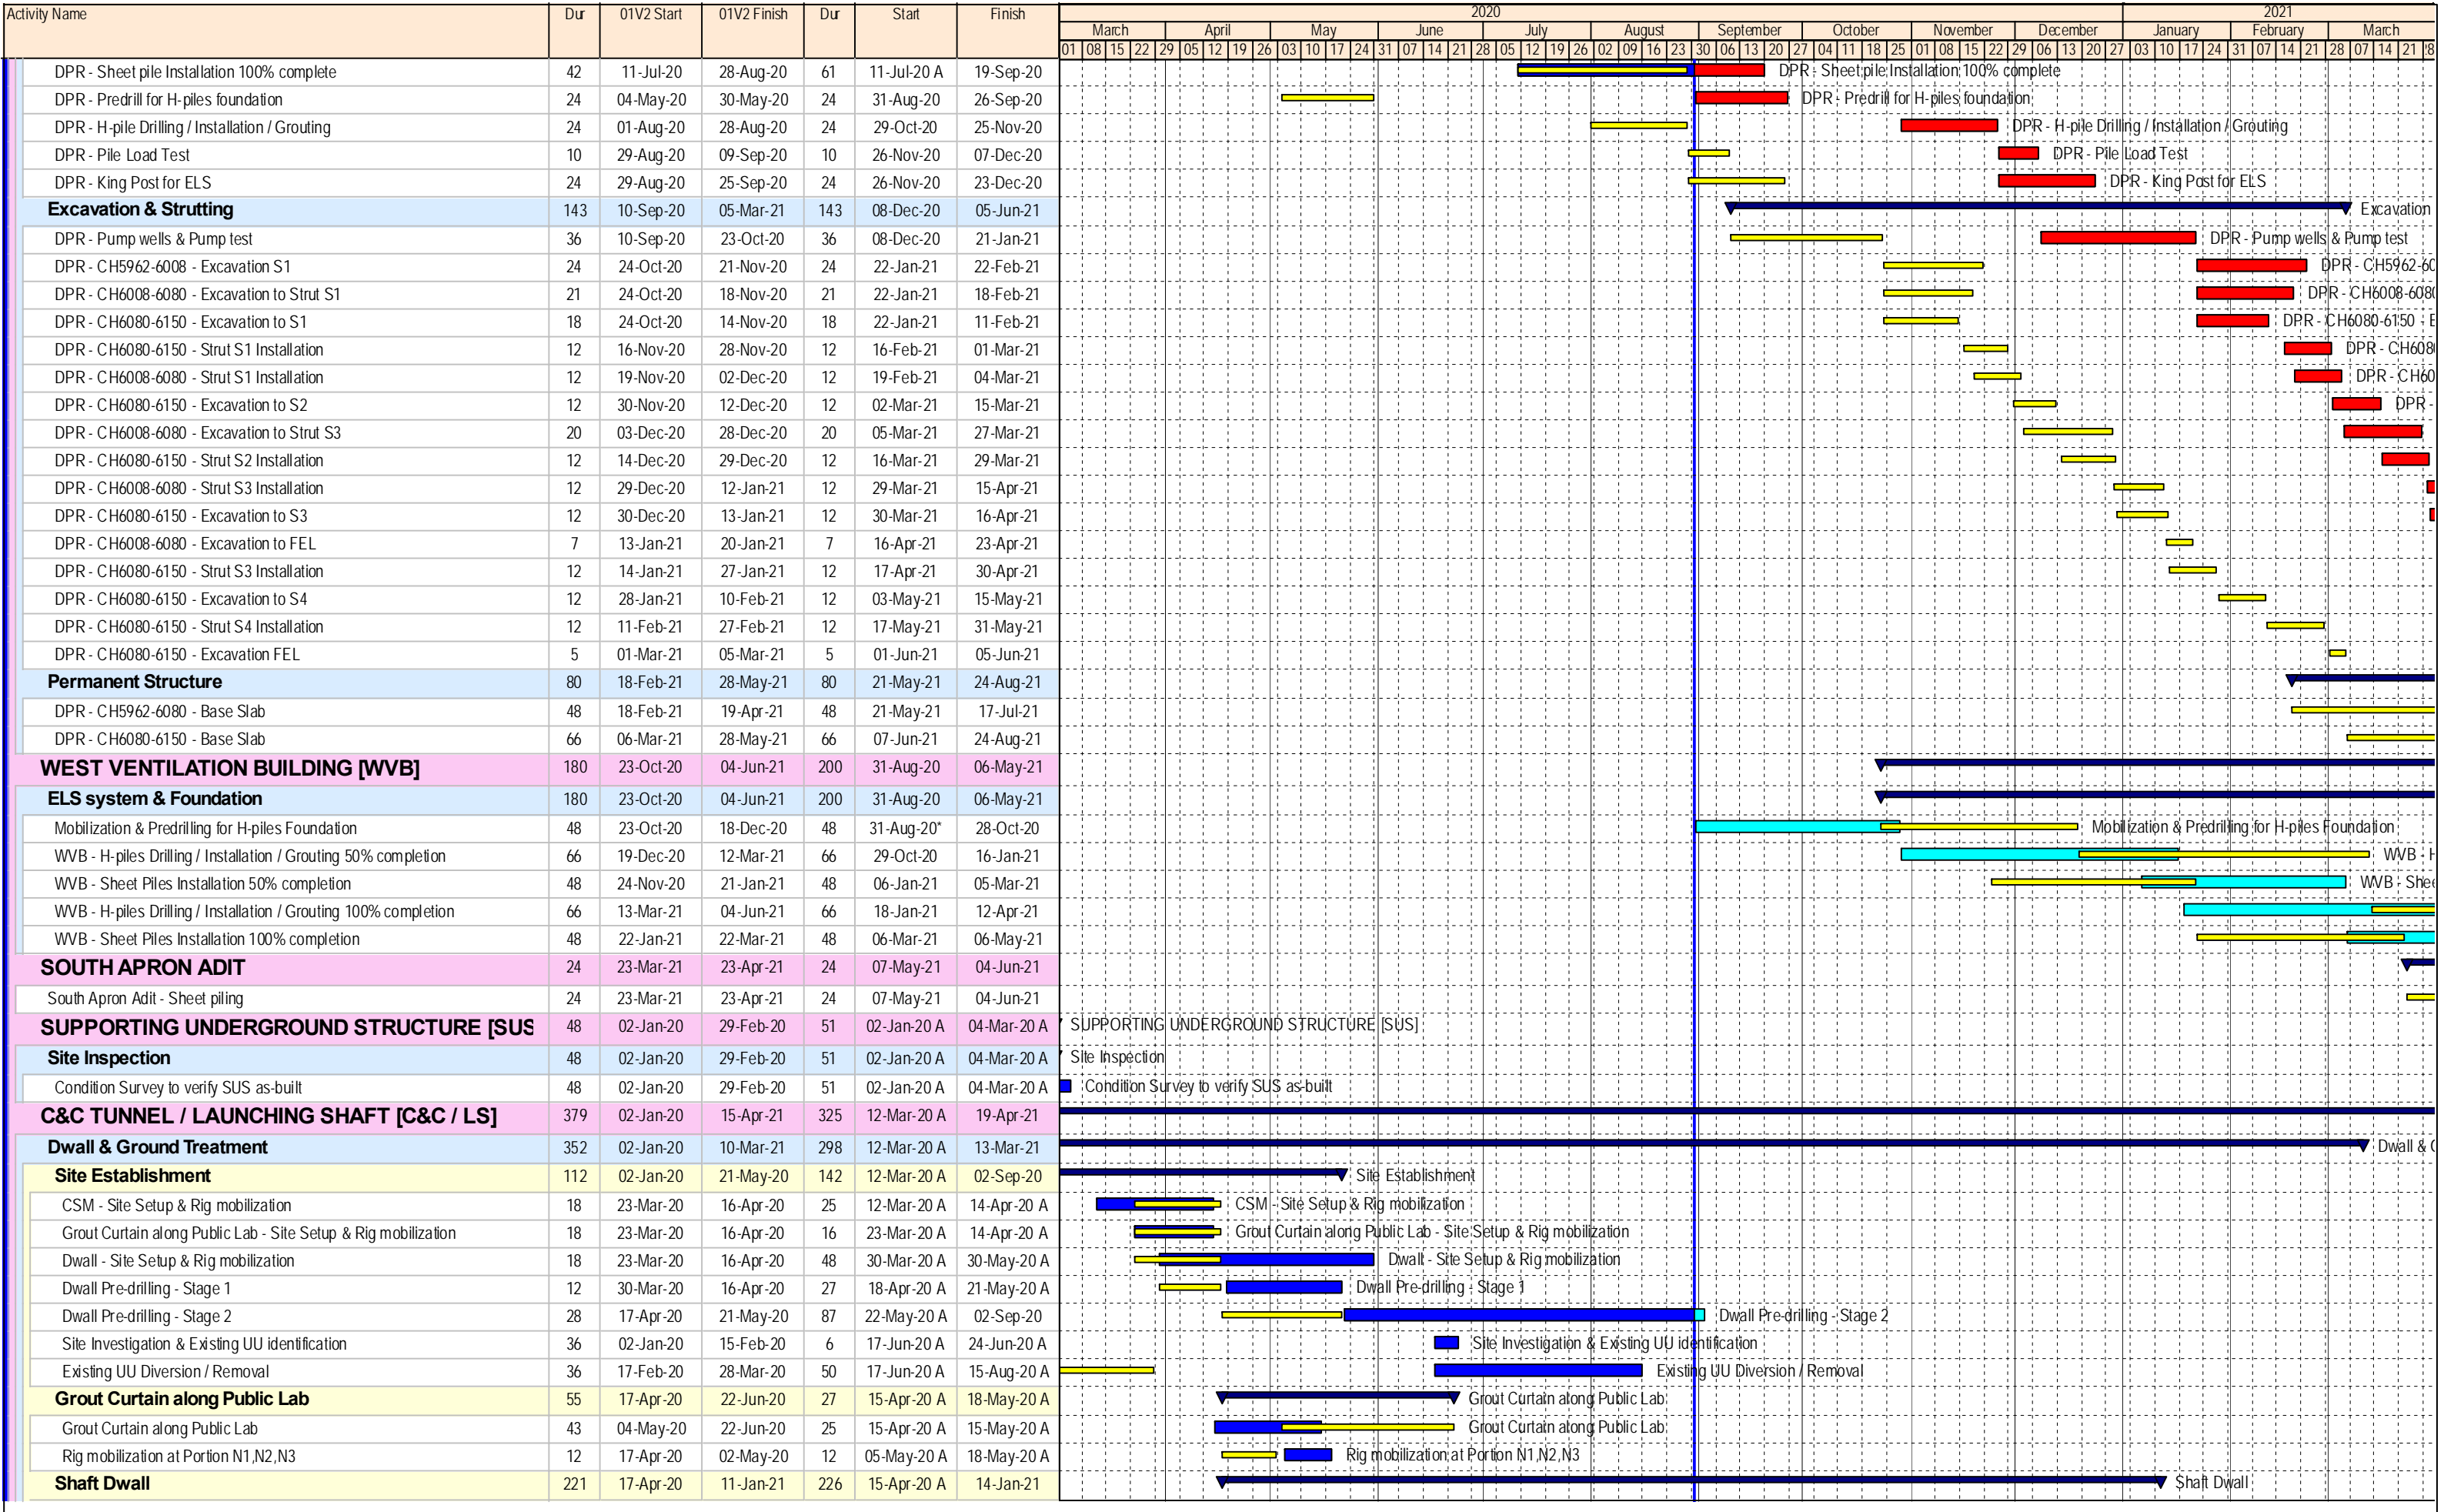

Page 27 of 30  
Data Date: 30-Aug-20


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬▬▬ Summary

# ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

## Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

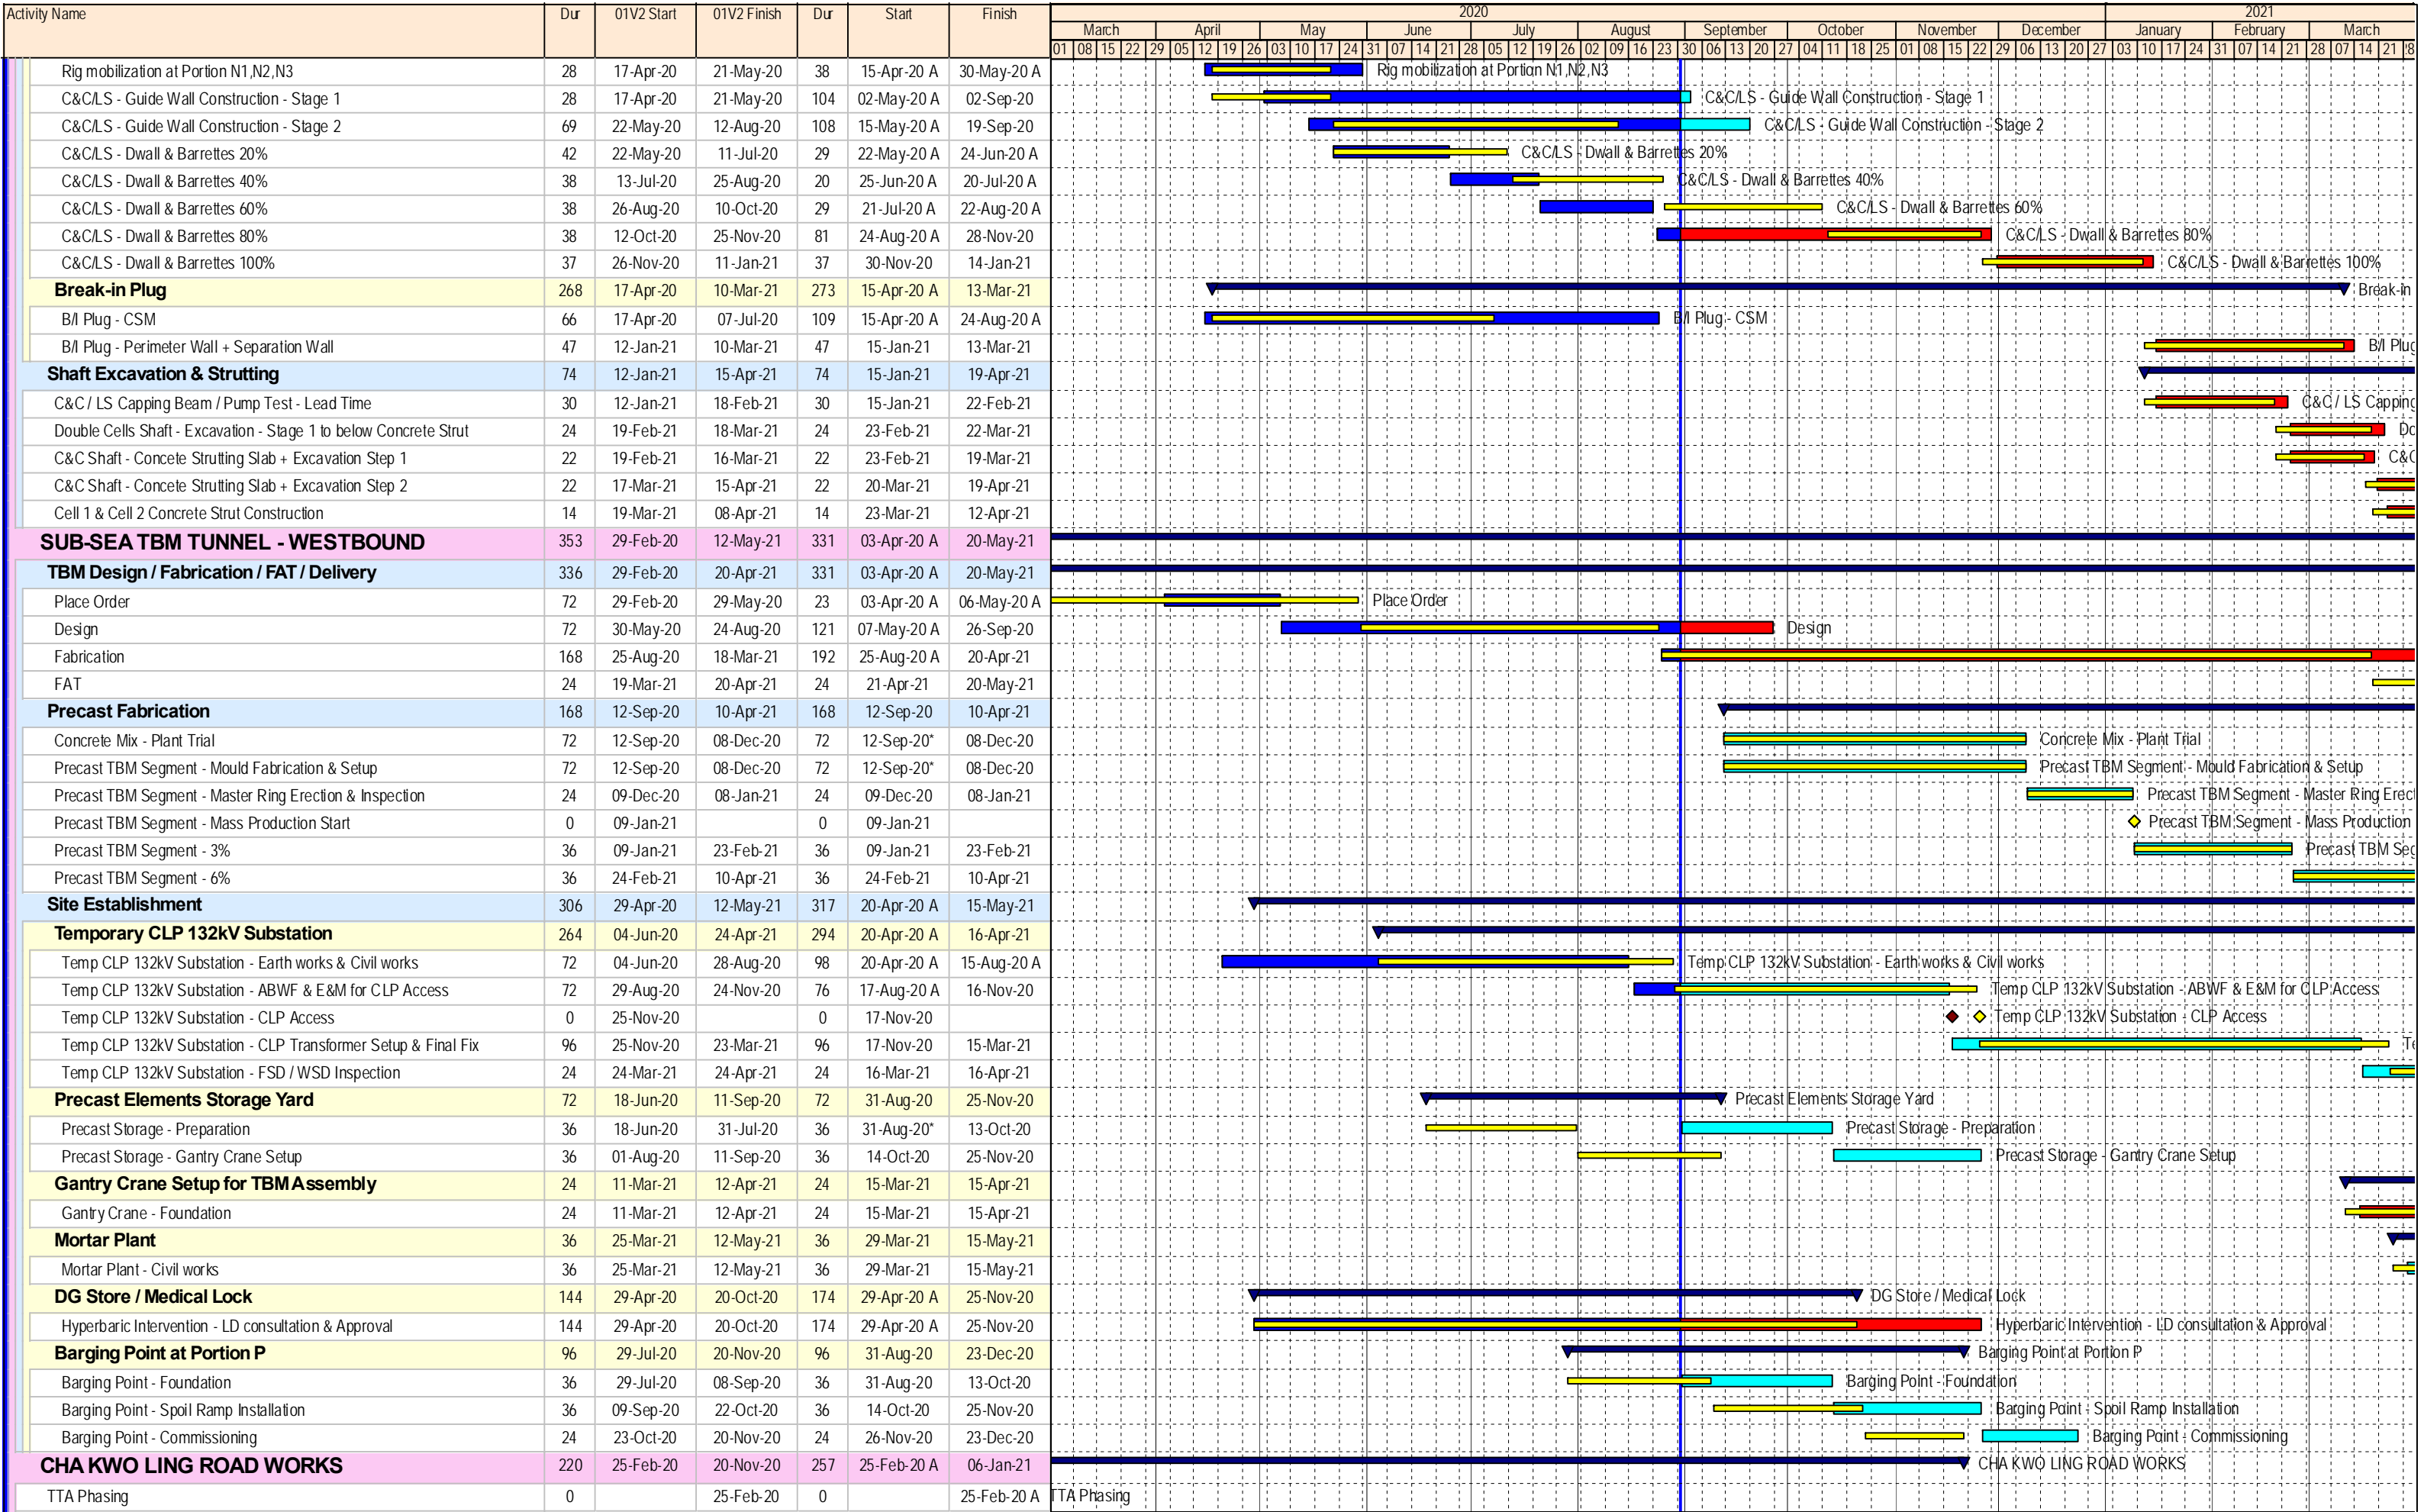


Page 28 of 30 Data Date: 30-Aug-20	<ul style="list-style-type: none"> <li><span style="color: red;">◆</span> Milestone</li> <li><span style="color: blue;">◆</span> Summary</li> <li><span style="color: cyan;">■</span> Planned Bar</li> <li><span style="color: red;">■</span> Critical Activity</li> <li><span style="color: blue;">■</span> Actual Milestone</li> <li><span style="color: blue;">■</span> Actual Work</li> <li><span style="color: yellow;">◆</span> Baseline Milestone</li> <li><span style="color: yellow;">■</span> Baseline Bar</li> </ul>
---------------------------------------	---

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme




Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

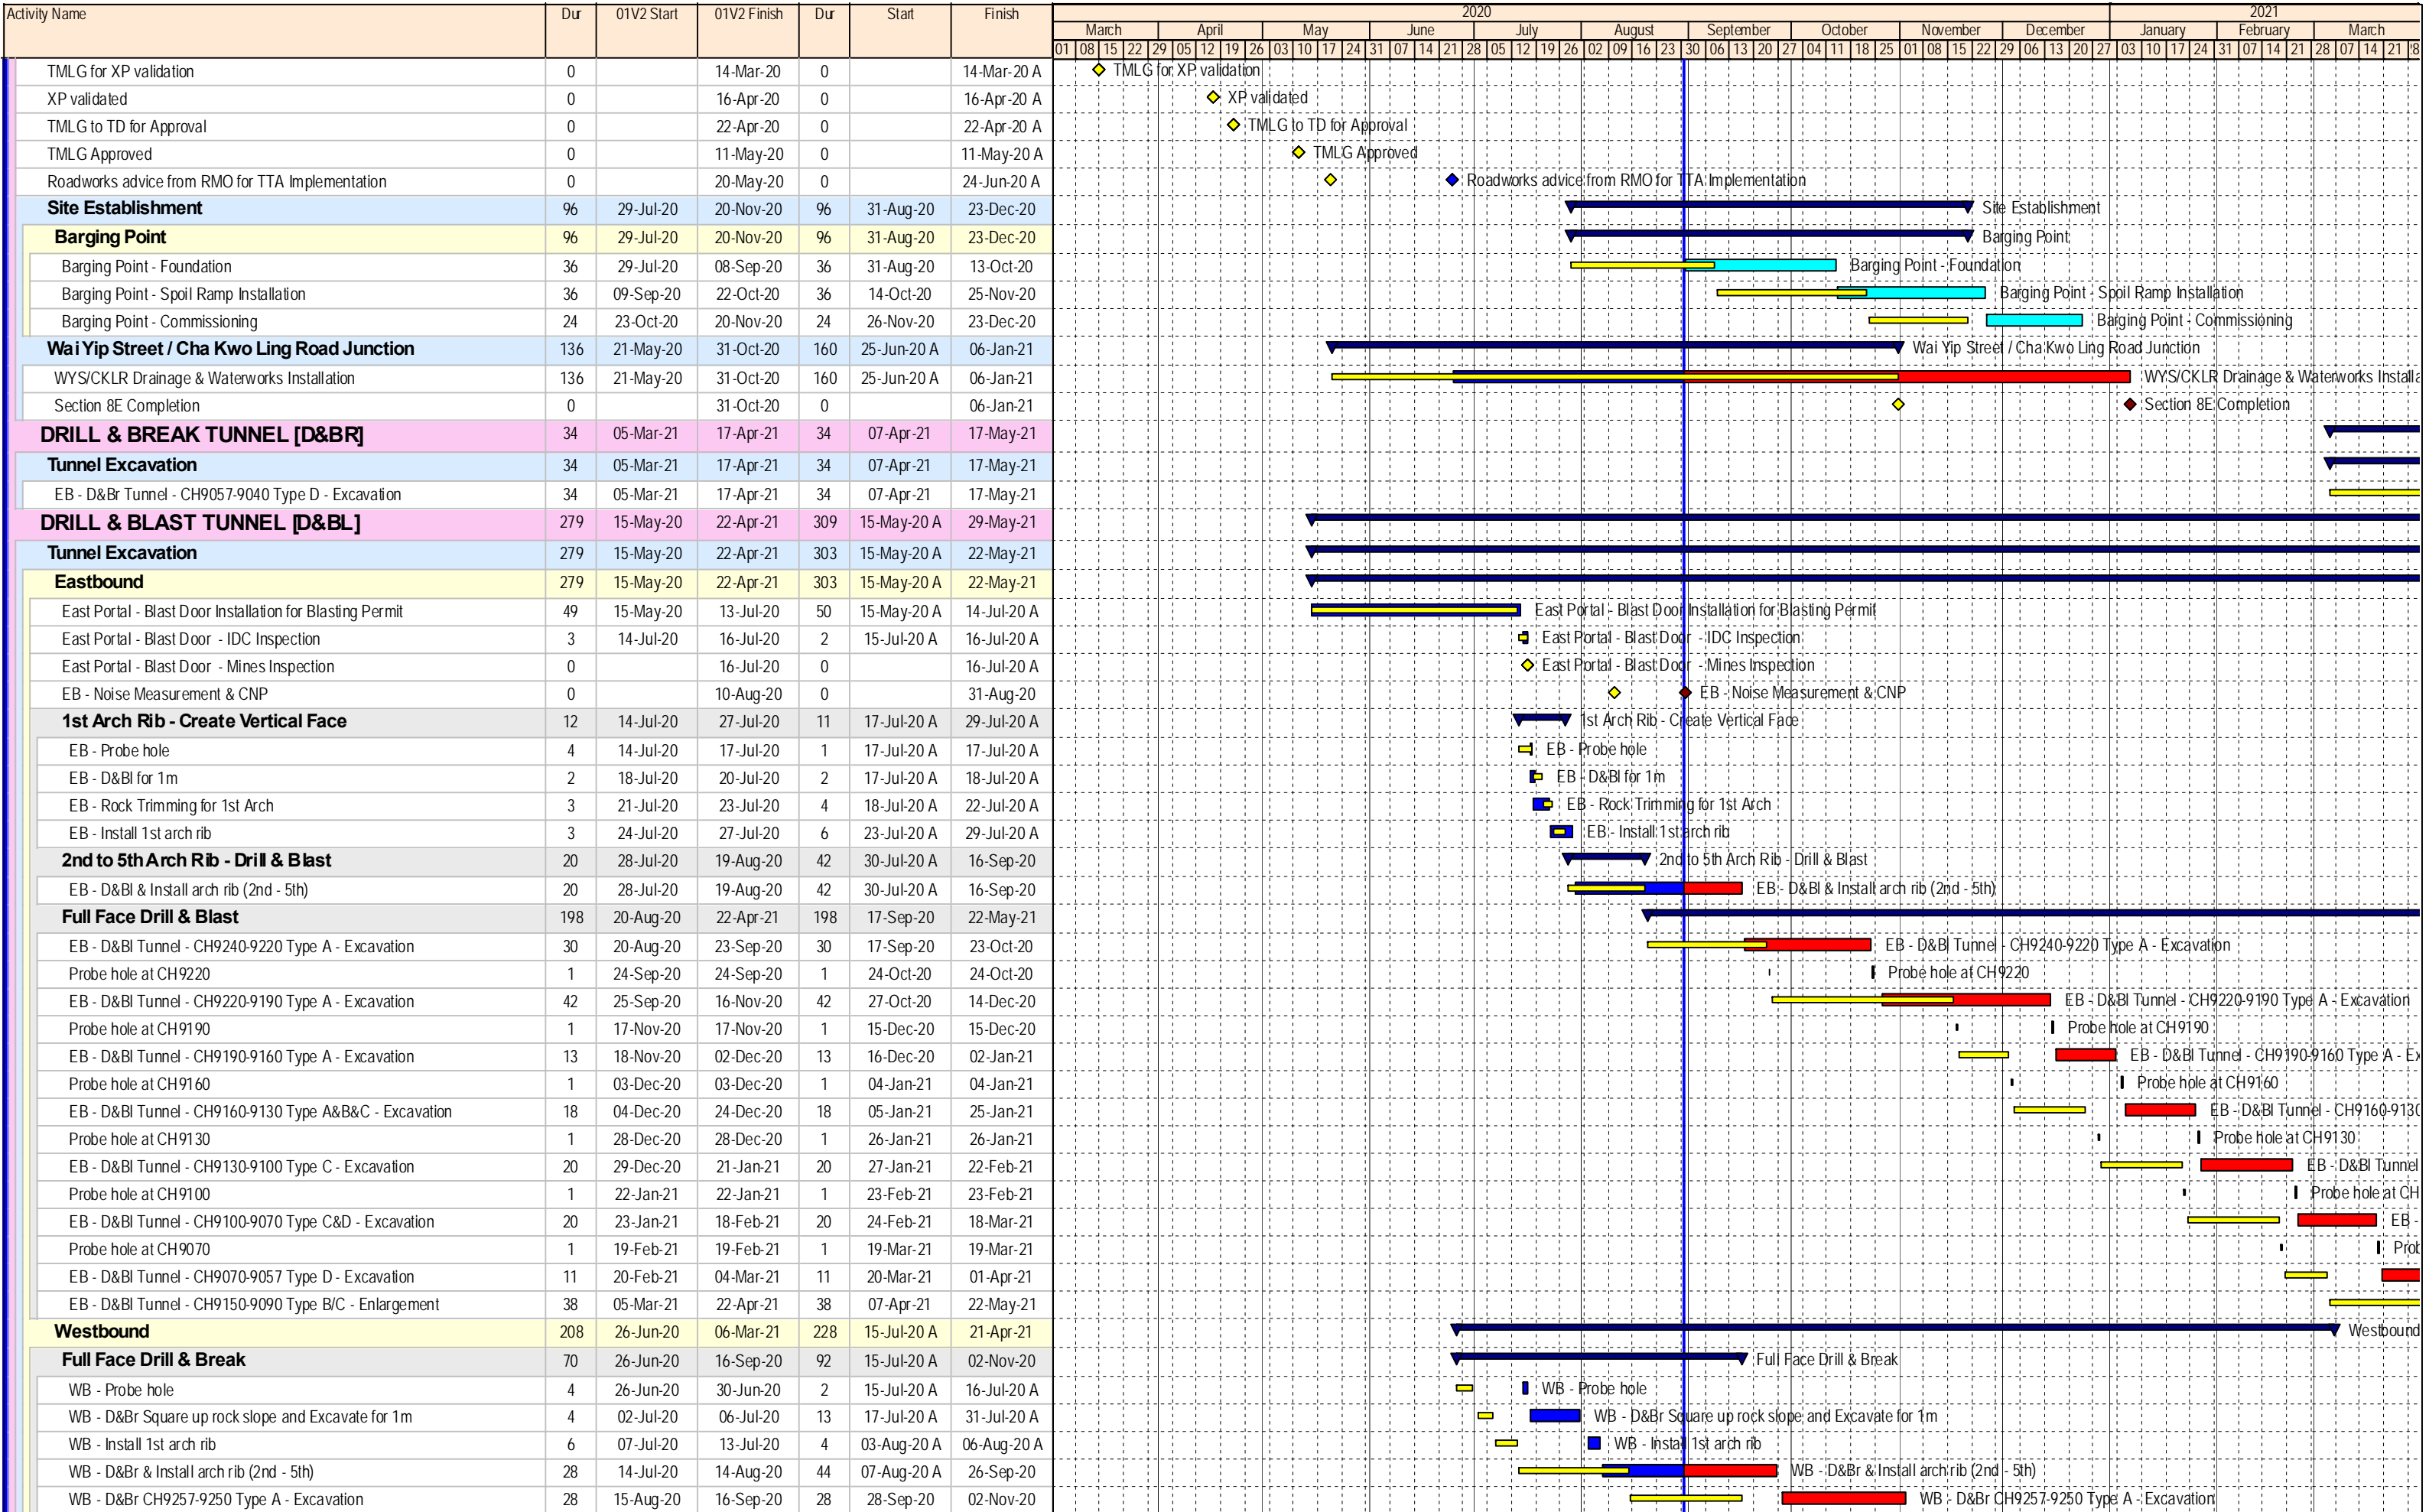

Page 29 of 30  
Data Date: 30-Aug-20

	Milestone		Summary
	Planned Bar		
	Critical Activity		
	Actual Milestone		
	Actual Work		
	Baseline Milestone		
	Baseline Bar		

## ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron Three Months Rolling Programme



Date	Revision	Checked	Approved
05-Nov-19	00V0	WYu	
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu

Activity Name	Dur	01V2 Start	01V2 Finish	Dur	Start	Finish	2020												2021																																					
							March			April			May			June			July			August			September			October			November			December			January			February			March													
							01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	06	13	20	27	03	10	17	24	31	07
<b>Full Face Drill &amp; Blast</b>	138	17-Sep-20	06-Mar-21	136	03-Nov-20	21-Apr-21	[Gantt chart bars and milestones for Full Face Drill & Blast]																																																	
WB- Blast Door Installation	24	17-Sep-20	16-Oct-20	24	03-Nov-20	30-Nov-20	[Gantt chart bars and milestones for WB- Blast Door Installation]																																																	
WB- D&BI start	0		16-Oct-20	0		30-Nov-20	[Gantt chart bars and milestones for WB- D&BI start]																																																	
WB - D&BI Tunnel - CH9250-9230 Type A - Excavation	31	17-Oct-20	23-Nov-20	31	01-Dec-20	08-Jan-21	[Gantt chart bars and milestones for WB - D&BI Tunnel - CH9250-9230 Type A - Excavation]																																																	
Probe hole at CH9230	1		24-Nov-20	0		08-Jan-21	[Gantt chart bars and milestones for Probe hole at CH9230]																																																	
WB - D&BI Tunnel - CH9230-9200 Type A - Excavation	34	25-Nov-20	06-Jan-21	34	09-Jan-21	20-Feb-21	[Gantt chart bars and milestones for WB - D&BI Tunnel - CH9230-9200 Type A - Excavation]																																																	
Probe hole at CH9200	1		07-Jan-21	0		20-Feb-21	[Gantt chart bars and milestones for Probe hole at CH9200]																																																	
WB - D&BI Tunnel - CH9200-9170 Type A - Excavation	23	08-Jan-21	03-Feb-21	23	22-Feb-21	19-Mar-21	[Gantt chart bars and milestones for WB - D&BI Tunnel - CH9200-9170 Type A - Excavation]																																																	
Probe hole at CH9170	1	04-Feb-21	04-Feb-21	1	20-Mar-21	20-Mar-21	[Gantt chart bars and milestones for Probe hole at CH9170]																																																	
WB - D&BI Tunnel - CH9170-9140 Type A - Excavation	23	05-Feb-21	06-Mar-21	23	22-Mar-21	21-Apr-21	[Gantt chart bars and milestones for WB - D&BI Tunnel - CH9170-9140 Type A - Excavation]																																																	
<b>Cross Passage</b>	31	08-Mar-21	16-Apr-21	31	22-Apr-21	29-May-21	[Gantt chart bars and milestones for Cross Passage]																																																	
<b>CP31</b>	13	16-Mar-21	30-Mar-21	13	30-Apr-21	15-May-21	[Gantt chart bars and milestones for CP31]																																																	
CP31 - D&BI Excavation 16.7m	13	16-Mar-21	30-Mar-21	13	30-Apr-21	15-May-21	[Gantt chart bars and milestones for CP31 - D&BI Excavation 16.7m]																																																	
<b>CP32</b>	31	08-Mar-21	16-Apr-21	31	22-Apr-21	29-May-21	[Gantt chart bars and milestones for CP32]																																																	
CP32 - D&BI Excavation 13.5m	7	08-Mar-21	15-Mar-21	7	22-Apr-21	29-Apr-21	[Gantt chart bars and milestones for CP32 - D&BI Excavation 13.5m]																																																	
CP32 - Blast Door	24	16-Mar-21	16-Apr-21	24	30-Apr-21	29-May-21	[Gantt chart bars and milestones for CP32 - Blast Door]																																																	

Page 30 of 30 Data Date: 30-Aug-20		<h2>ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron</h2> <h3>Three Months Rolling Programme</h3>		Date	Revision	Checked	Approved
				05-Nov-19	00V0	WYu	
				18-Dec-19	00V1	WYu	
				22-Feb-20	01V0	SPa/LLo	WYu
				09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu				
