


Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish
ED/2018/04 - Trunk Road T2	513	23-Sep-20	21-Jun-22	01-Mar-21 A	31-Jan-22
DESIGN SUBMISSION & APPROVAL	513	23-Sep-20	21-Jun-22	01-Mar-21 A	01-Dec-21
GENERAL	359	06-Oct-20	20-Dec-21	02-Mar-21 A	06-Nov-21
Design Memorandum	0	06-Oct-20	06-Oct-20	23-Mar-21 A	07-Jun-21 A
Design Memorandum - 6th Sub	0				23-Mar-21 A
Design Memorandum - 6th Review	0			24-Mar-21 A	20-Apr-21 A
Design Memorandum - Further Information required	0			21-Apr-21 A	16-May-21 A
Design Memorandum - 7th Sub	0				16-May-21 A
Design Memorandum - Approval	0		06-Oct-20		07-Jun-21 A
Design Memorandum - 7th Review	0			17-May-21 A	07-Jun-21 A
Ground Investigation Report - Kai Tak Area	0	05-Jan-21	05-Jan-21	24-Aug-21	24-Aug-21
Ground Investigation Report Vol 1 - Approval	0		05-Jan-21		24-Aug-21
Ground Investigation Report - Tunnel	47	14-Oct-20	09-Dec-20	12-Aug-21	07-Oct-21
Ground Investigation Report Vol 2 - 1st Sub	0		14-Oct-20		12-Aug-21
Ground Investigation Report Vol 2 - Review 1st Sub	28	15-Oct-20	11-Nov-20	13-Aug-21	09-Sep-21
Ground Investigation Report Vol 2 - 2nd Sub	0		11-Nov-20		09-Sep-21
Ground Investigation Report Vol 2 - Review 2nd Sub	28	12-Nov-20	09-Dec-20	10-Sep-21	07-Oct-21
Ground Investigation Report Vol 2 - Approval	0		09-Dec-20		07-Oct-21
Construction Traffic Impact Assessment - Kai Tak Area	0	06-Oct-20	06-Oct-20	24-Mar-21 A	04-Sep-21
CTIA Kai Tak Area - 5th Sub	0				24-Mar-21 A
CTIA Kai Tak Area - 5th Review	0			25-Mar-21 A	30-Apr-21 A
CTIA Kai Tak Area - Resubmission	0			03-May-21 A	03-Aug-21
CTIA Kai Tak Area - 6th Sub	0				03-Aug-21
CTIA Kai Tak Area - Approval	0		06-Oct-20		04-Sep-21
CTIA Kai Tak Area - 6th Review	0			04-Aug-21	04-Sep-21
ACABAS - Western Tunnel Portal	52	24-Oct-20	24-Dec-20	17-Mar-21 A	18-May-21 A
DDA - Further information required by SO	22	24-Oct-20	19-Nov-20	17-Mar-21 A	28-Apr-21 A
DDA - 2nd Sub	0		19-Nov-20		28-Apr-21 A
DDA - 2nd Review by SO	35	20-Nov-20	24-Dec-20	29-Apr-21 A	18-May-21 A
DDA - SO Consent for Construction	0		24-Dec-20		18-May-21 A
ACABAS- Footbridge FB-02	78	28-Dec-20	01-Apr-21	02-Aug-21	03-Nov-21
DDA - Draft - Preparation by Designer	48	28-Dec-20	25-Feb-21	02-Aug-21	27-Sep-21
DDA - Draft - Final Review and prepare for 1st Sub	30	26-Feb-21	01-Apr-21	28-Sep-21	03-Nov-21
DDA Project Alignment	0	09-Oct-20	09-Oct-20	11-Mar-21 A	11-Mar-21 A
DDA - SO Consent for Construction	0		09-Oct-20		11-Mar-21 A
AIP Roadworks and Street Furniture	0	16-Feb-21	16-Feb-21	29-Mar-21 A	01-Sep-21
AIP - 3rd Sub	0				29-Mar-21 A
AIP - 3rd Review by SO	0			01-Apr-21 A	05-May-21 A
AIP - Further information required by SO	0			06-May-21 A	28-May-21 A
AIP - 4th Sub	0				28-May-21 A
AIP - 4th Review by SO	0			29-May-21 A	29-Jun-21 A
AIP - Further information required by SO	0			30-Jun-21 A	30-Jul-21 A
AIP - 5th Sub	0				31-Jul-21 A
AIP - SO Consent for DDA Submission	0		16-Feb-21		01-Sep-21
AIP - 5th Review by SO	0			31-Jul-21 A	01-Sep-21
DDA Roadworks and Street Furniture	54	16-Feb-21	23-Apr-21	02-Sep-21	06-Nov-21
DDA - Draft - Preparation by Designer	36	16-Feb-21	29-Mar-21	02-Sep-21	16-Oct-21
DDA - Draft - Final Review and prepare for 1st Sub	18	30-Mar-21	23-Apr-21	18-Oct-21	06-Nov-21

Page 1 of 23
Data Date: 31-Jul-21


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

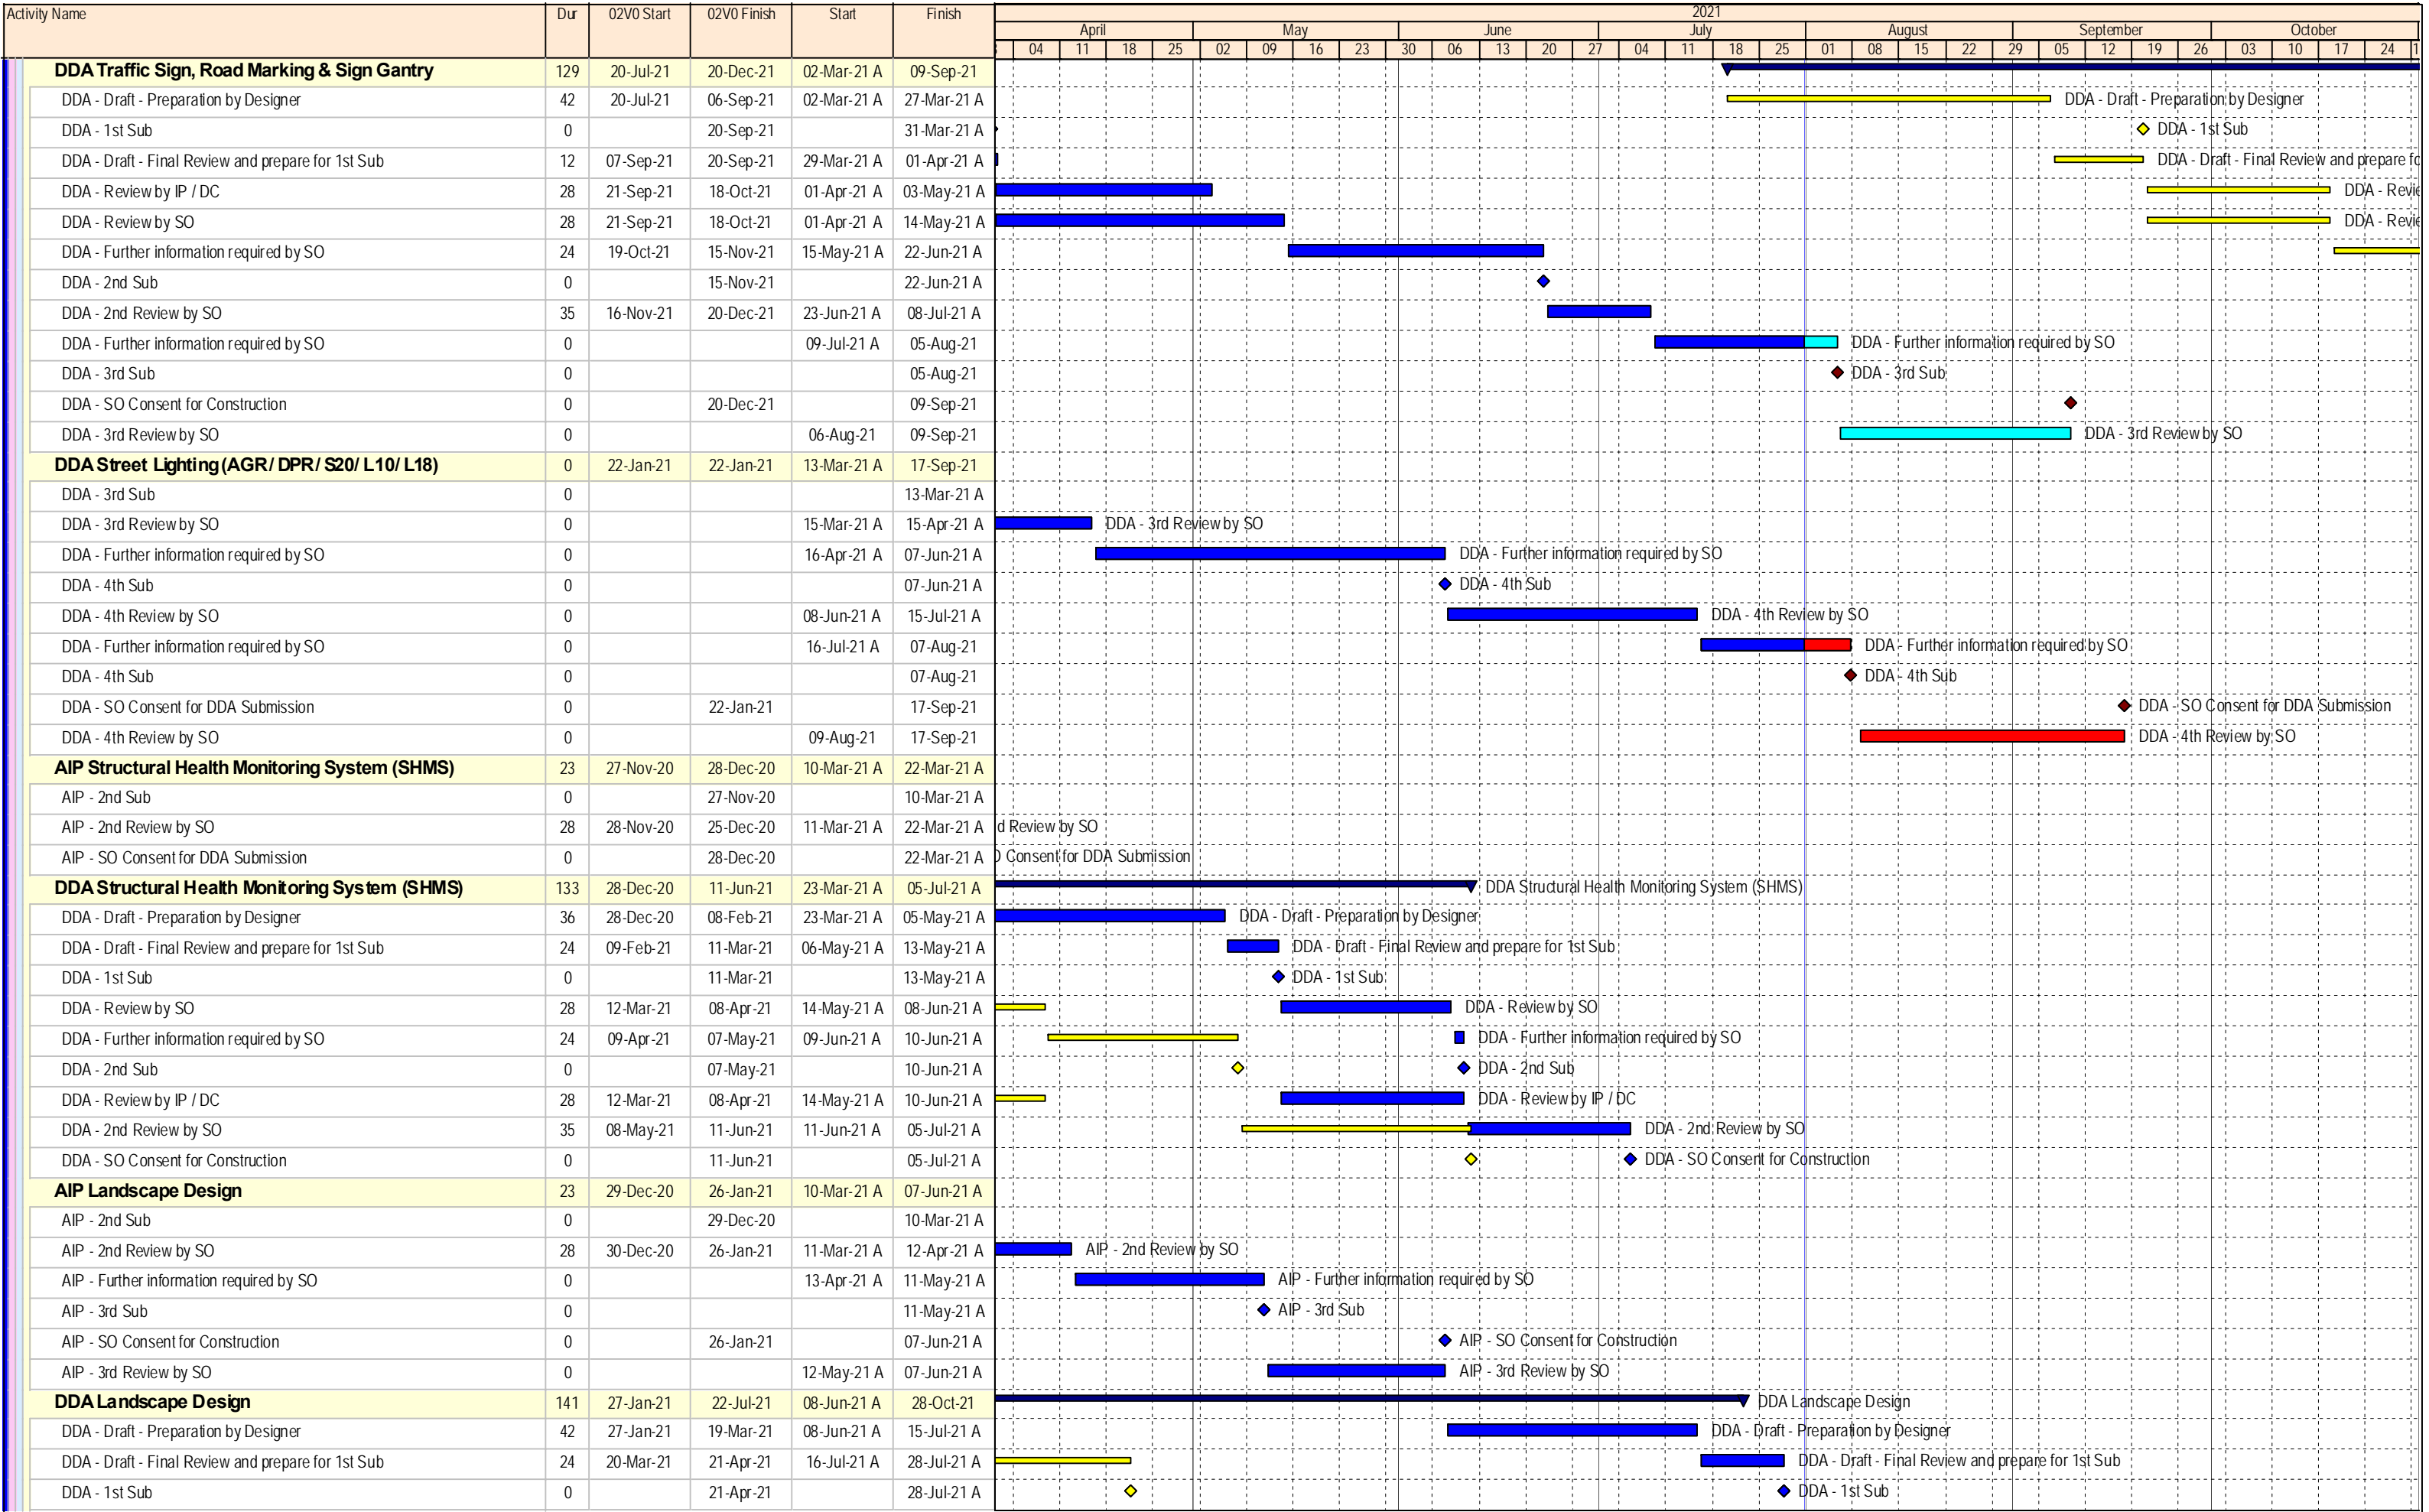


Page 2 of 23
Data Date: 31-Jul-21

- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

Activity Name	Dur	02V0 Start	02V0 Finish	Start	Finish	2021																													
						April				May				June				July				August				September				October					
						04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19	26	03	10	17	24
DDA - Review by SO	28	22-Apr-21	19-May-21	29-Jul-21 A	25-Aug-21	[Gantt chart bar from 22-Apr to 25-Aug]																													
DDA - Review by IP / DC	28	22-Apr-21	19-May-21	29-Jul-21 A	25-Aug-21	[Gantt chart bar from 22-Apr to 25-Aug]																													
DDA - Further information required by SO	24	20-May-21	17-Jun-21	26-Aug-21	23-Sep-21	[Gantt chart bar from 20-May to 23-Sep]																													
DDA - 2nd Sub	0		17-Jun-21		23-Sep-21	[Gantt chart bar from 17-Jun to 23-Sep]																													
DDA - 2nd Review by SO	35	18-Jun-21	22-Jul-21	24-Sep-21	28-Oct-21	[Gantt chart bar from 18-Jun to 28-Oct]																													
DDA - SO Consent for Construction	0		22-Jul-21		28-Oct-21	[Gantt chart bar from 22-Jul to 28-Oct]																													
MISC. TEMP WORKS	0	24-Mar-21	24-Mar-21	24-Mar-21 A	24-Mar-21 A	[Summary bar from 24-Mar to 24-Mar]																													
Barging Point design at Portion Q	0	24-Mar-21	24-Mar-21	24-Mar-21 A	24-Mar-21 A	[Summary bar from 24-Mar to 24-Mar]																													
TN - SO Consent for Construction	0		24-Mar-21		24-Mar-21 A	[Gantt chart bar from 24-Mar to 24-Mar]																													
DEPRESSED ROAD [DPR]	120	23-Sep-20	19-Feb-21	15-Apr-21 A	23-Oct-21	[Summary bar from 23-Sep to 23-Oct]																													
DDA DPR - Permanent Structure	0	16-Dec-20	16-Dec-20	15-Apr-21 A	15-Apr-21 A	[Summary bar from 16-Dec to 15-Apr]																													
DDA - SO Consent for Construction	0		16-Dec-20		15-Apr-21 A	[Gantt chart bar from 16-Dec to 15-Apr]																													
Stage 2A Completion	0		16-Dec-20		15-Apr-21 A	[Gantt chart bar from 16-Dec to 15-Apr]																													
DDA DPR - Portal Structure	120	23-Sep-20	19-Feb-21	29-Apr-21 A	23-Oct-21	[Summary bar from 23-Sep to 23-Oct]																													
DDA - Draft - Preparation by Designer	30	23-Sep-20	30-Oct-20	29-Apr-21 A	28-May-21 A	[Gantt chart bar from 23-Sep to 28-May]																													
DDA - Draft - Final Review and prepare for 1st Sub	24	07-Nov-20	04-Dec-20	29-May-21 A	07-Aug-21	[Gantt chart bar from 07-Nov to 07-Aug]																													
DDA - 1st Sub	0		04-Dec-20		07-Aug-21	[Gantt chart bar from 04-Dec to 07-Aug]																													
DDA - Review by SO	28	05-Dec-20	01-Jan-21	08-Aug-21	04-Sep-21	[Gantt chart bar from 05-Dec to 04-Sep]																													
DDA - Review by IP / DC	28	05-Dec-20	01-Jan-21	08-Aug-21	04-Sep-21	[Gantt chart bar from 05-Dec to 04-Sep]																													
DDA - Further information required by SO	12	02-Jan-21	15-Jan-21	06-Sep-21	18-Sep-21	[Gantt chart bar from 02-Jan to 18-Sep]																													
DDA - 2nd Sub	0		15-Jan-21		18-Sep-21	[Gantt chart bar from 15-Jan to 18-Sep]																													
DDA - SO Consent for Construction	0		19-Feb-21		23-Oct-21	[Gantt chart bar from 19-Feb to 23-Oct]																													
DDA - 2nd Review by SO	35	16-Jan-21	19-Feb-21	19-Sep-21	23-Oct-21	[Gantt chart bar from 16-Jan to 23-Oct]																													
Stage 1A Completion	0		19-Feb-21		23-Oct-21	[Gantt chart bar from 19-Feb to 23-Oct]																													
WEST VENTILATION BUILDING [WVB]	199	13-Jan-21	14-Sep-21	09-Mar-21 A	15-Nov-21	[Summary bar from 13-Jan to 15-Nov]																													
DDA WVB - ELS Design (DCRA + Dewatering & Pumping T	0	08-Feb-21	08-Feb-21	01-Apr-21 A	27-Jul-21 A	[Summary bar from 08-Feb to 27-Jul]																													
DDA - 4th Sub	0				01-Apr-21 A	[Gantt chart bar from 01-Apr to 01-Apr]																													
DDA - 4th Review by SO	0			02-Apr-21 A	04-May-21 A	[Gantt chart bar from 02-Apr to 04-May]																													
DDA - Further information required by SO	0			05-May-21 A	11-May-21 A	[Gantt chart bar from 05-May to 11-May]																													
DDA - 5th Sub	0				11-May-21 A	[Gantt chart bar from 11-May to 11-May]																													
DDA - 5th Review by SO	0			12-May-21 A	16-Jun-21 A	[Gantt chart bar from 12-May to 16-Jun]																													
DDA - Further information required by SO	0			17-Jun-21 A	20-Jul-21 A	[Gantt chart bar from 17-Jun to 20-Jul]																													
DDA - 6th Sub	0				20-Jul-21 A	[Gantt chart bar from 20-Jul to 20-Jul]																													
DDA - SO Consent for Construction	0		08-Feb-21		27-Jul-21 A	[Gantt chart bar from 08-Feb to 27-Jul]																													
DDA - 6th Review by SO	0			21-Jul-21 A	27-Jul-21 A	[Gantt chart bar from 21-Jul to 27-Jul]																													
DDA WVB - Accommodation (SoA)	0	09-Apr-21	09-Apr-21	09-Mar-21 A	14-Aug-21	[Summary bar from 09-Apr to 14-Aug]																													
DDA - Further information required by SO	0			09-Mar-21 A	12-Jul-21 A	[Gantt chart bar from 09-Mar to 12-Jul]																													
DDA - 3rd Sub	0				12-Jul-21 A	[Gantt chart bar from 12-Jul to 12-Jul]																													
DDA - SO Consent for Construction	0		09-Apr-21		14-Aug-21	[Gantt chart bar from 09-Apr to 14-Aug]																													
DDA - 3rd Review by SO	0			13-Jul-21 A	14-Aug-21	[Gantt chart bar from 13-Jul to 14-Aug]																													
DDA WVB - Permanent Structure	58	08-Apr-21	17-Jun-21	20-Mar-21 A	17-Jul-21 A	[Summary bar from 08-Apr to 17-Jul]																													
DDA - Further information required by SO	30	08-Apr-21	13-May-21	20-Mar-21 A	13-May-21 A	[Gantt chart bar from 08-Apr to 13-May]																													
DDA - 2nd Sub	0		13-May-21		13-May-21 A	[Gantt chart bar from 13-May to 13-May]																													
DDA - SO Consent for Construction	0		17-Jun-21		17-Jul-21 A	[Gantt chart bar from 17-Jun to 17-Jul]																													
DDA - 2nd Review by SO	35	14-May-21	17-Jun-21	14-May-21 A	17-Jul-21 A	[Gantt chart bar from 14-May to 17-Jul]																													
DDA WVB - ABWF	121	11-Mar-21	07-Aug-21	14-May-21 A	15-Nov-21	[Summary bar from 11-Mar to 15-Nov]																													
DDA - Draft - Preparation by Designer	45	11-Mar-21	07-May-21	14-May-21 A	14-Aug-21	[Gantt chart bar from 11-Mar to 14-Aug]																													
DDA - Draft - Final Review and prepare for 1st Sub	24	08-May-21	05-Jun-21	16-Aug-21	11-Sep-21	[Gantt chart bar from 08-May to 11-Sep]																													

Page 3 of 23
 Data Date: 31-Jul-21


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

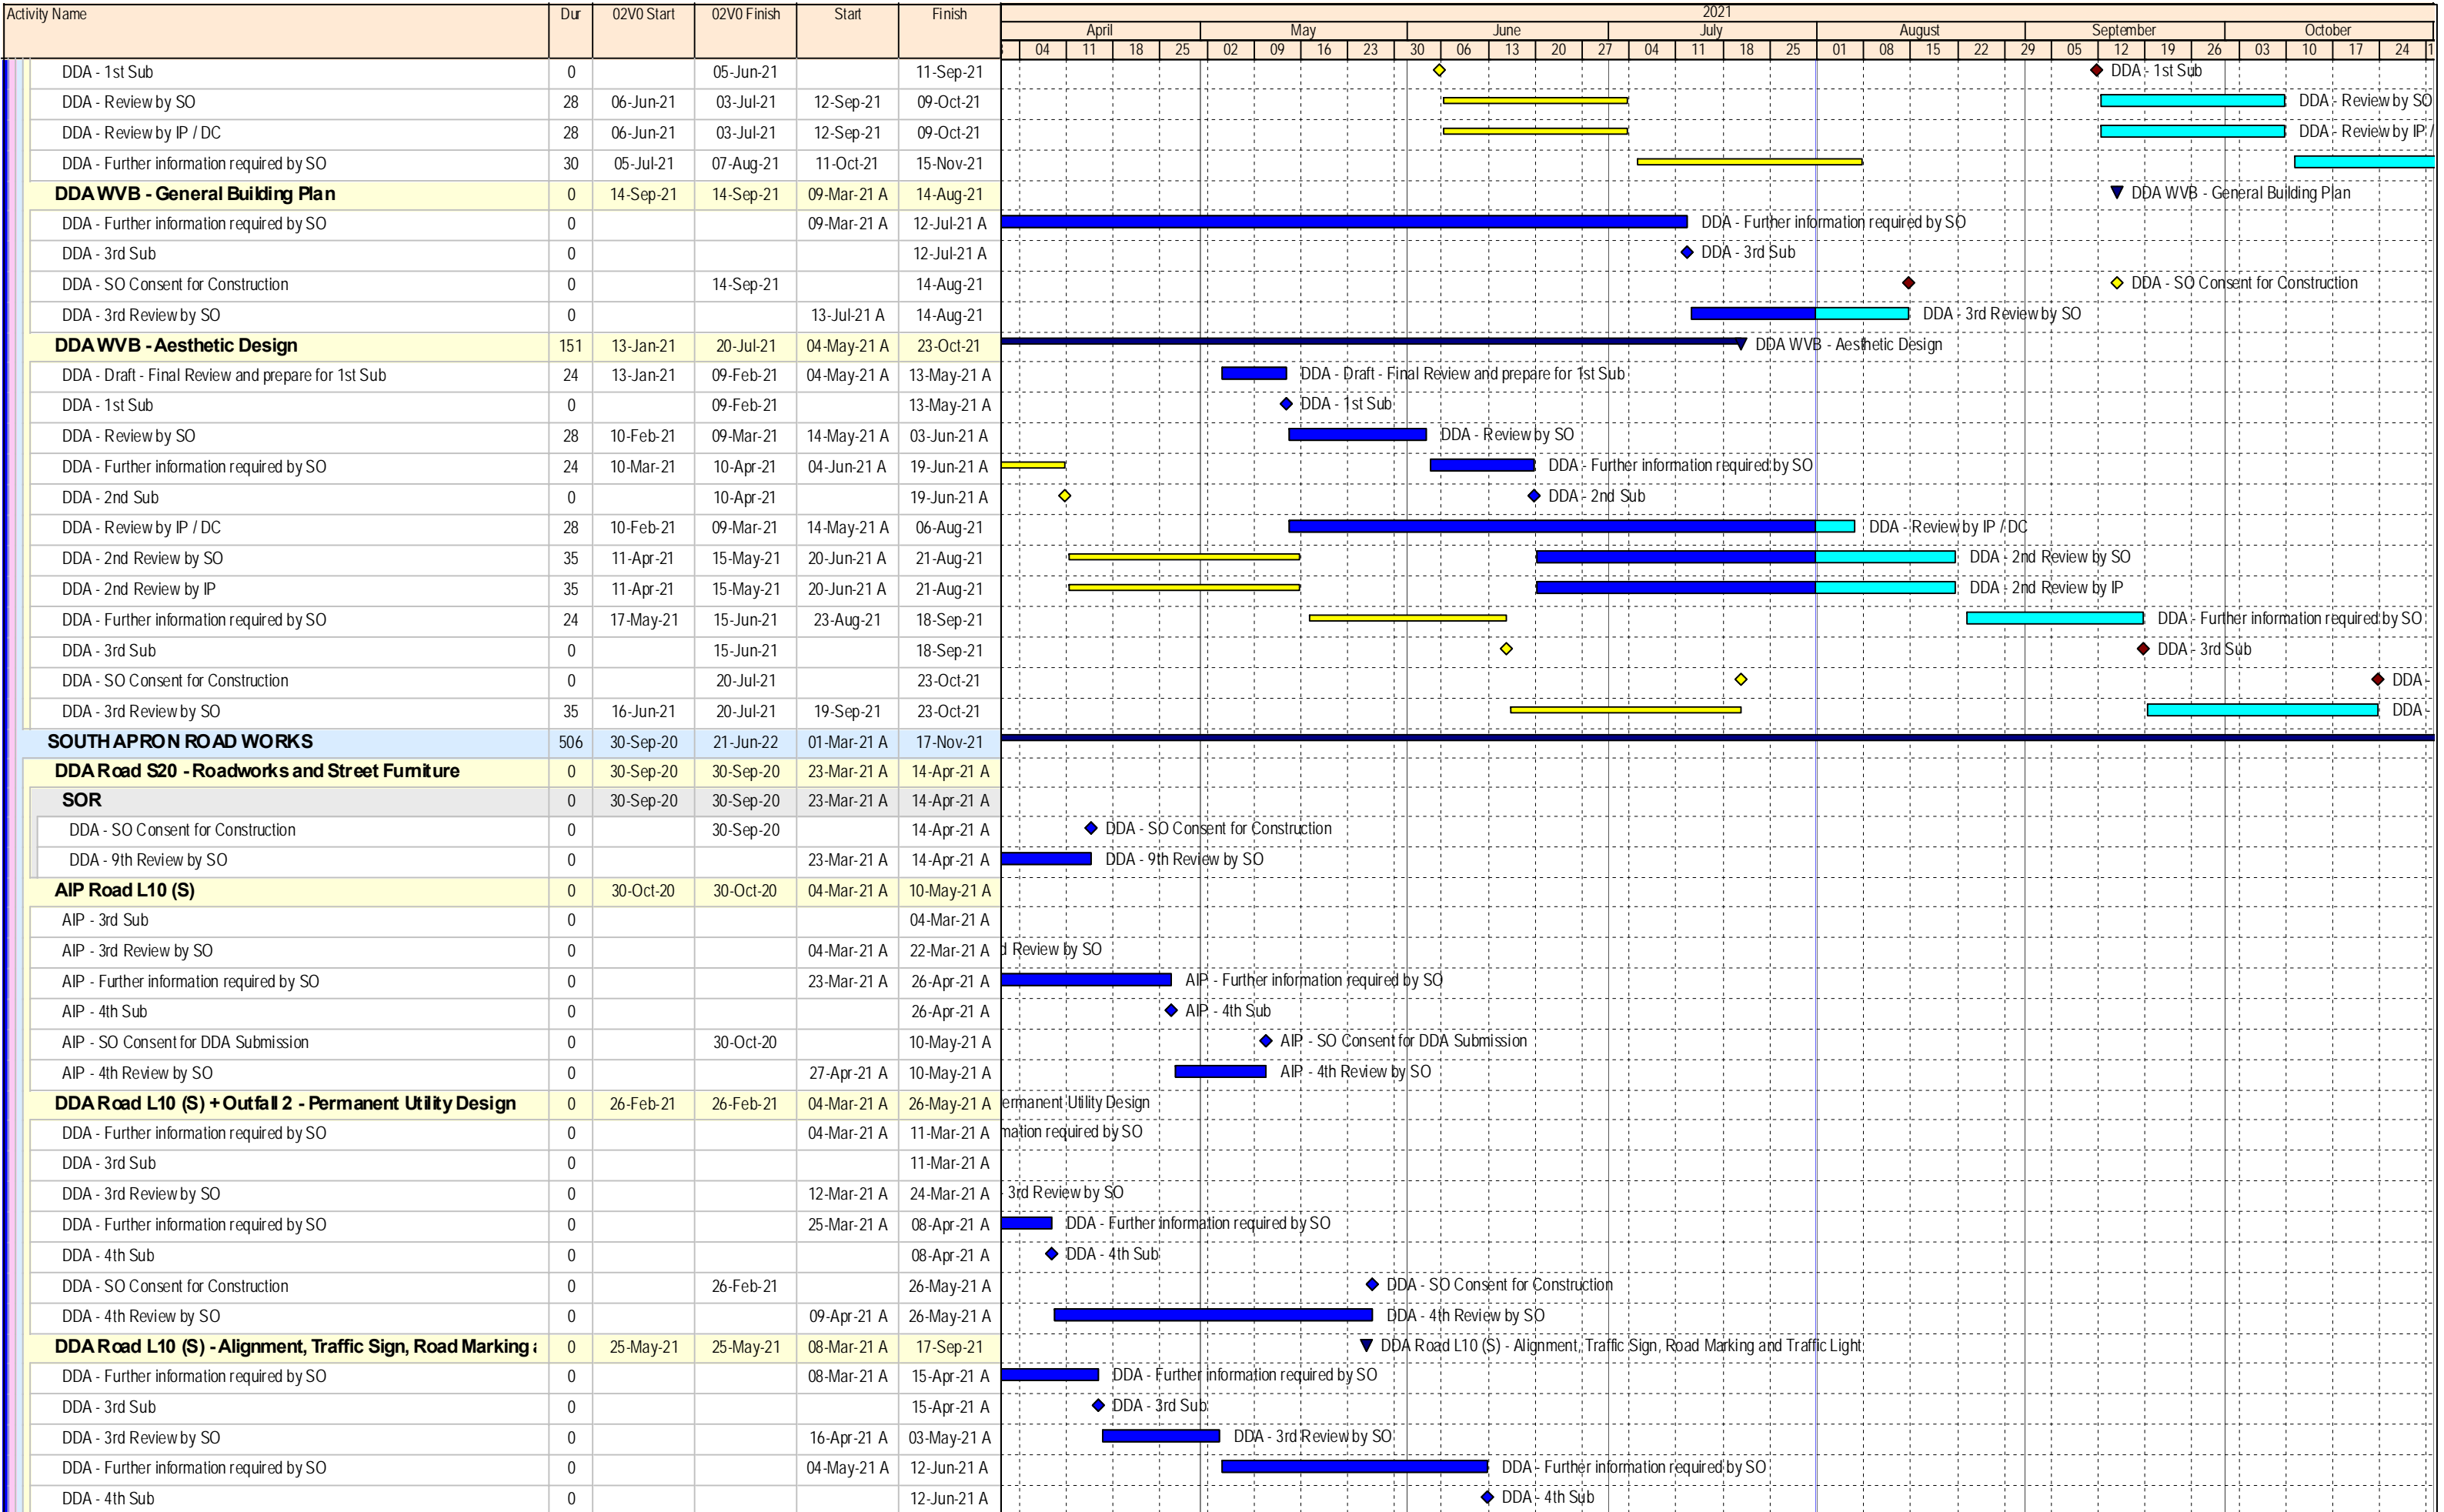


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu


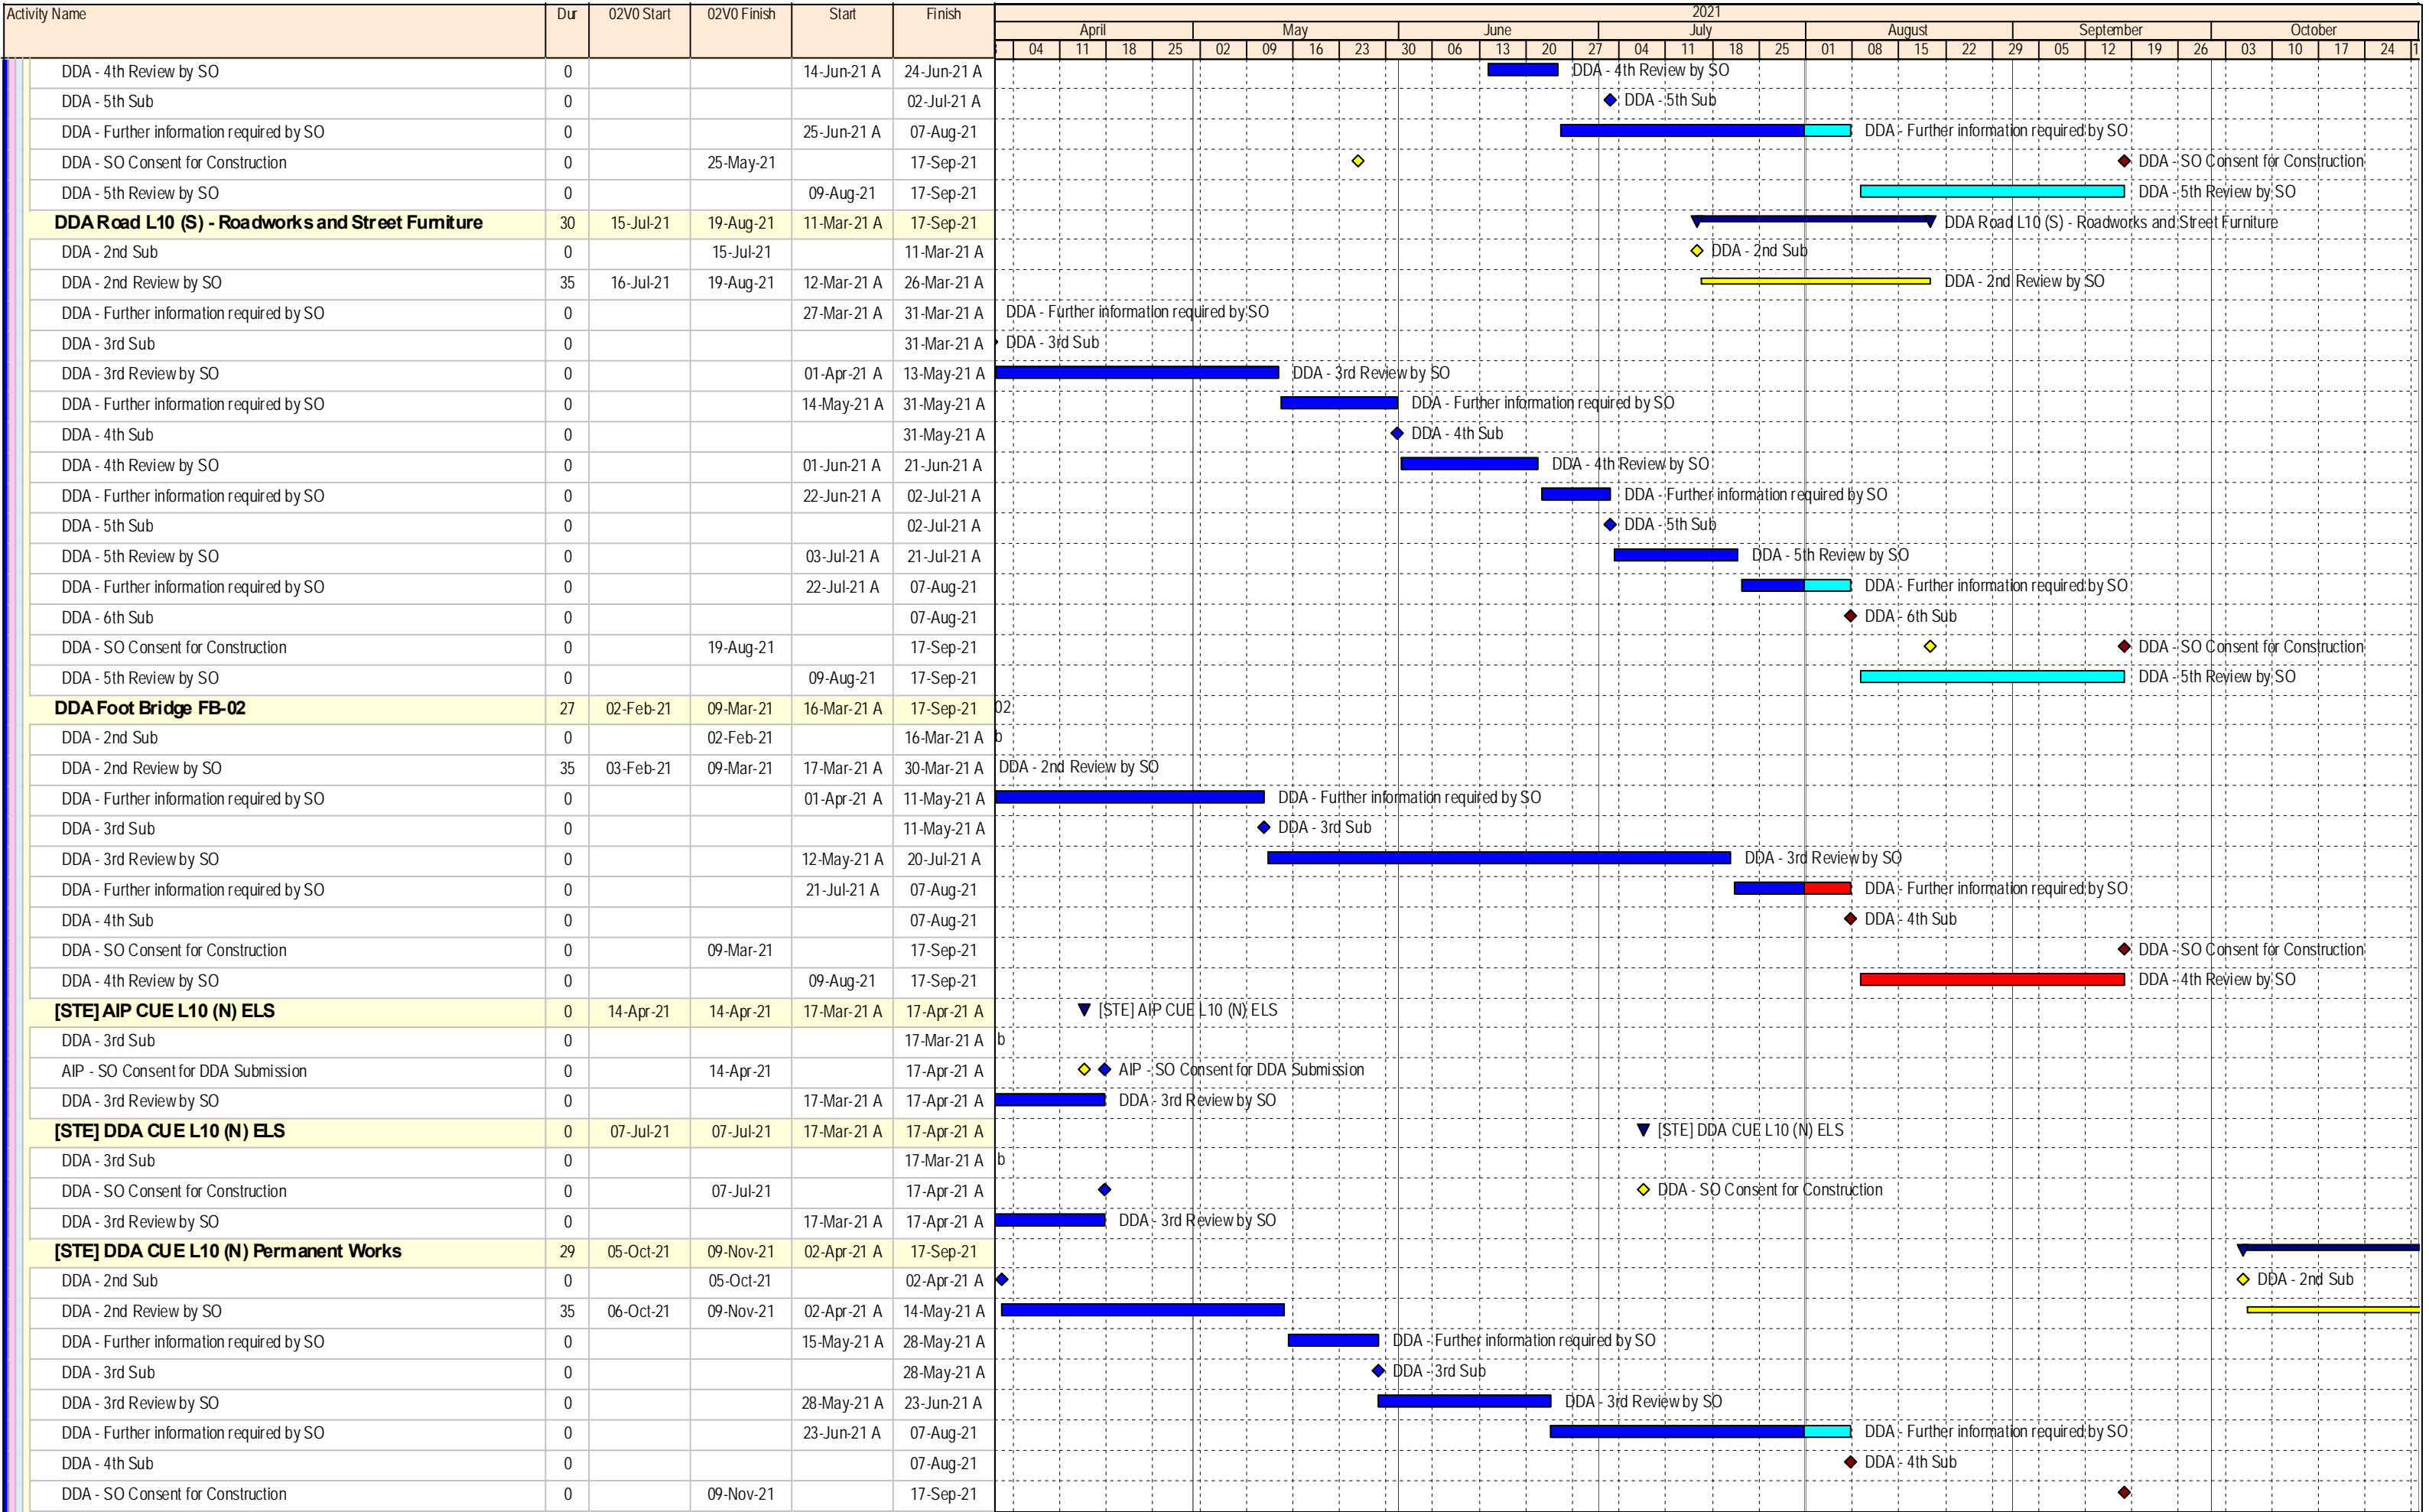


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

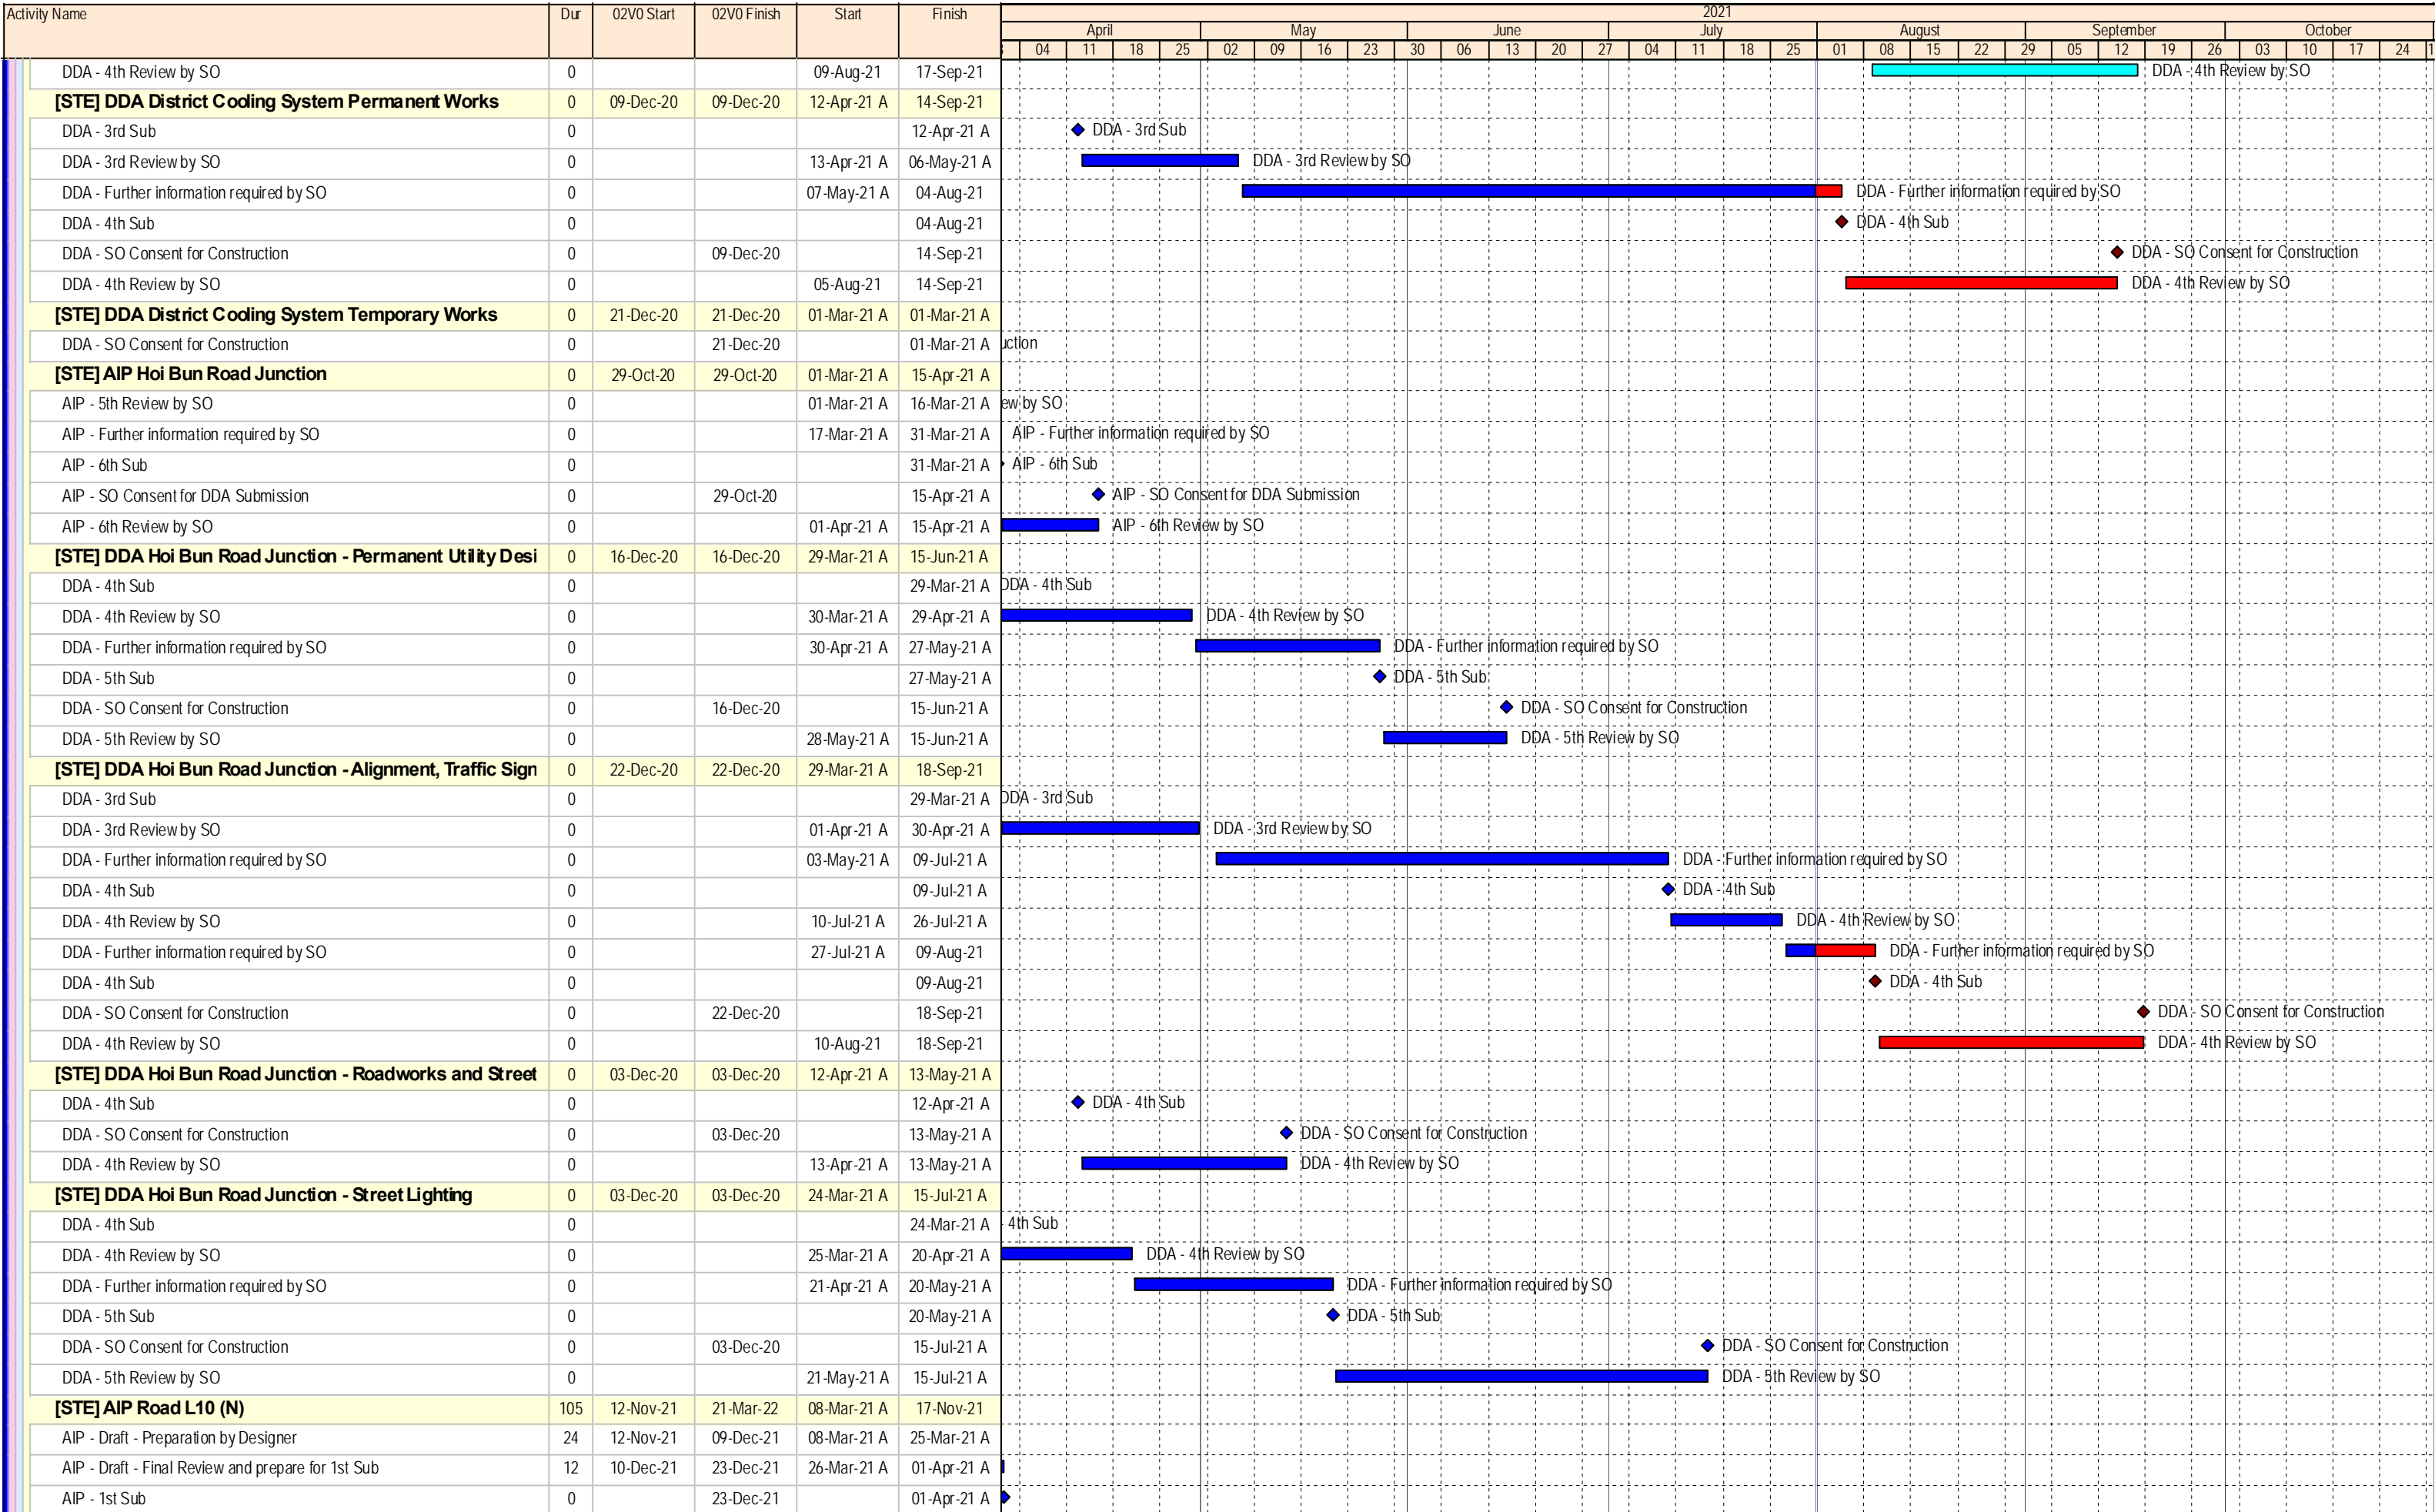


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

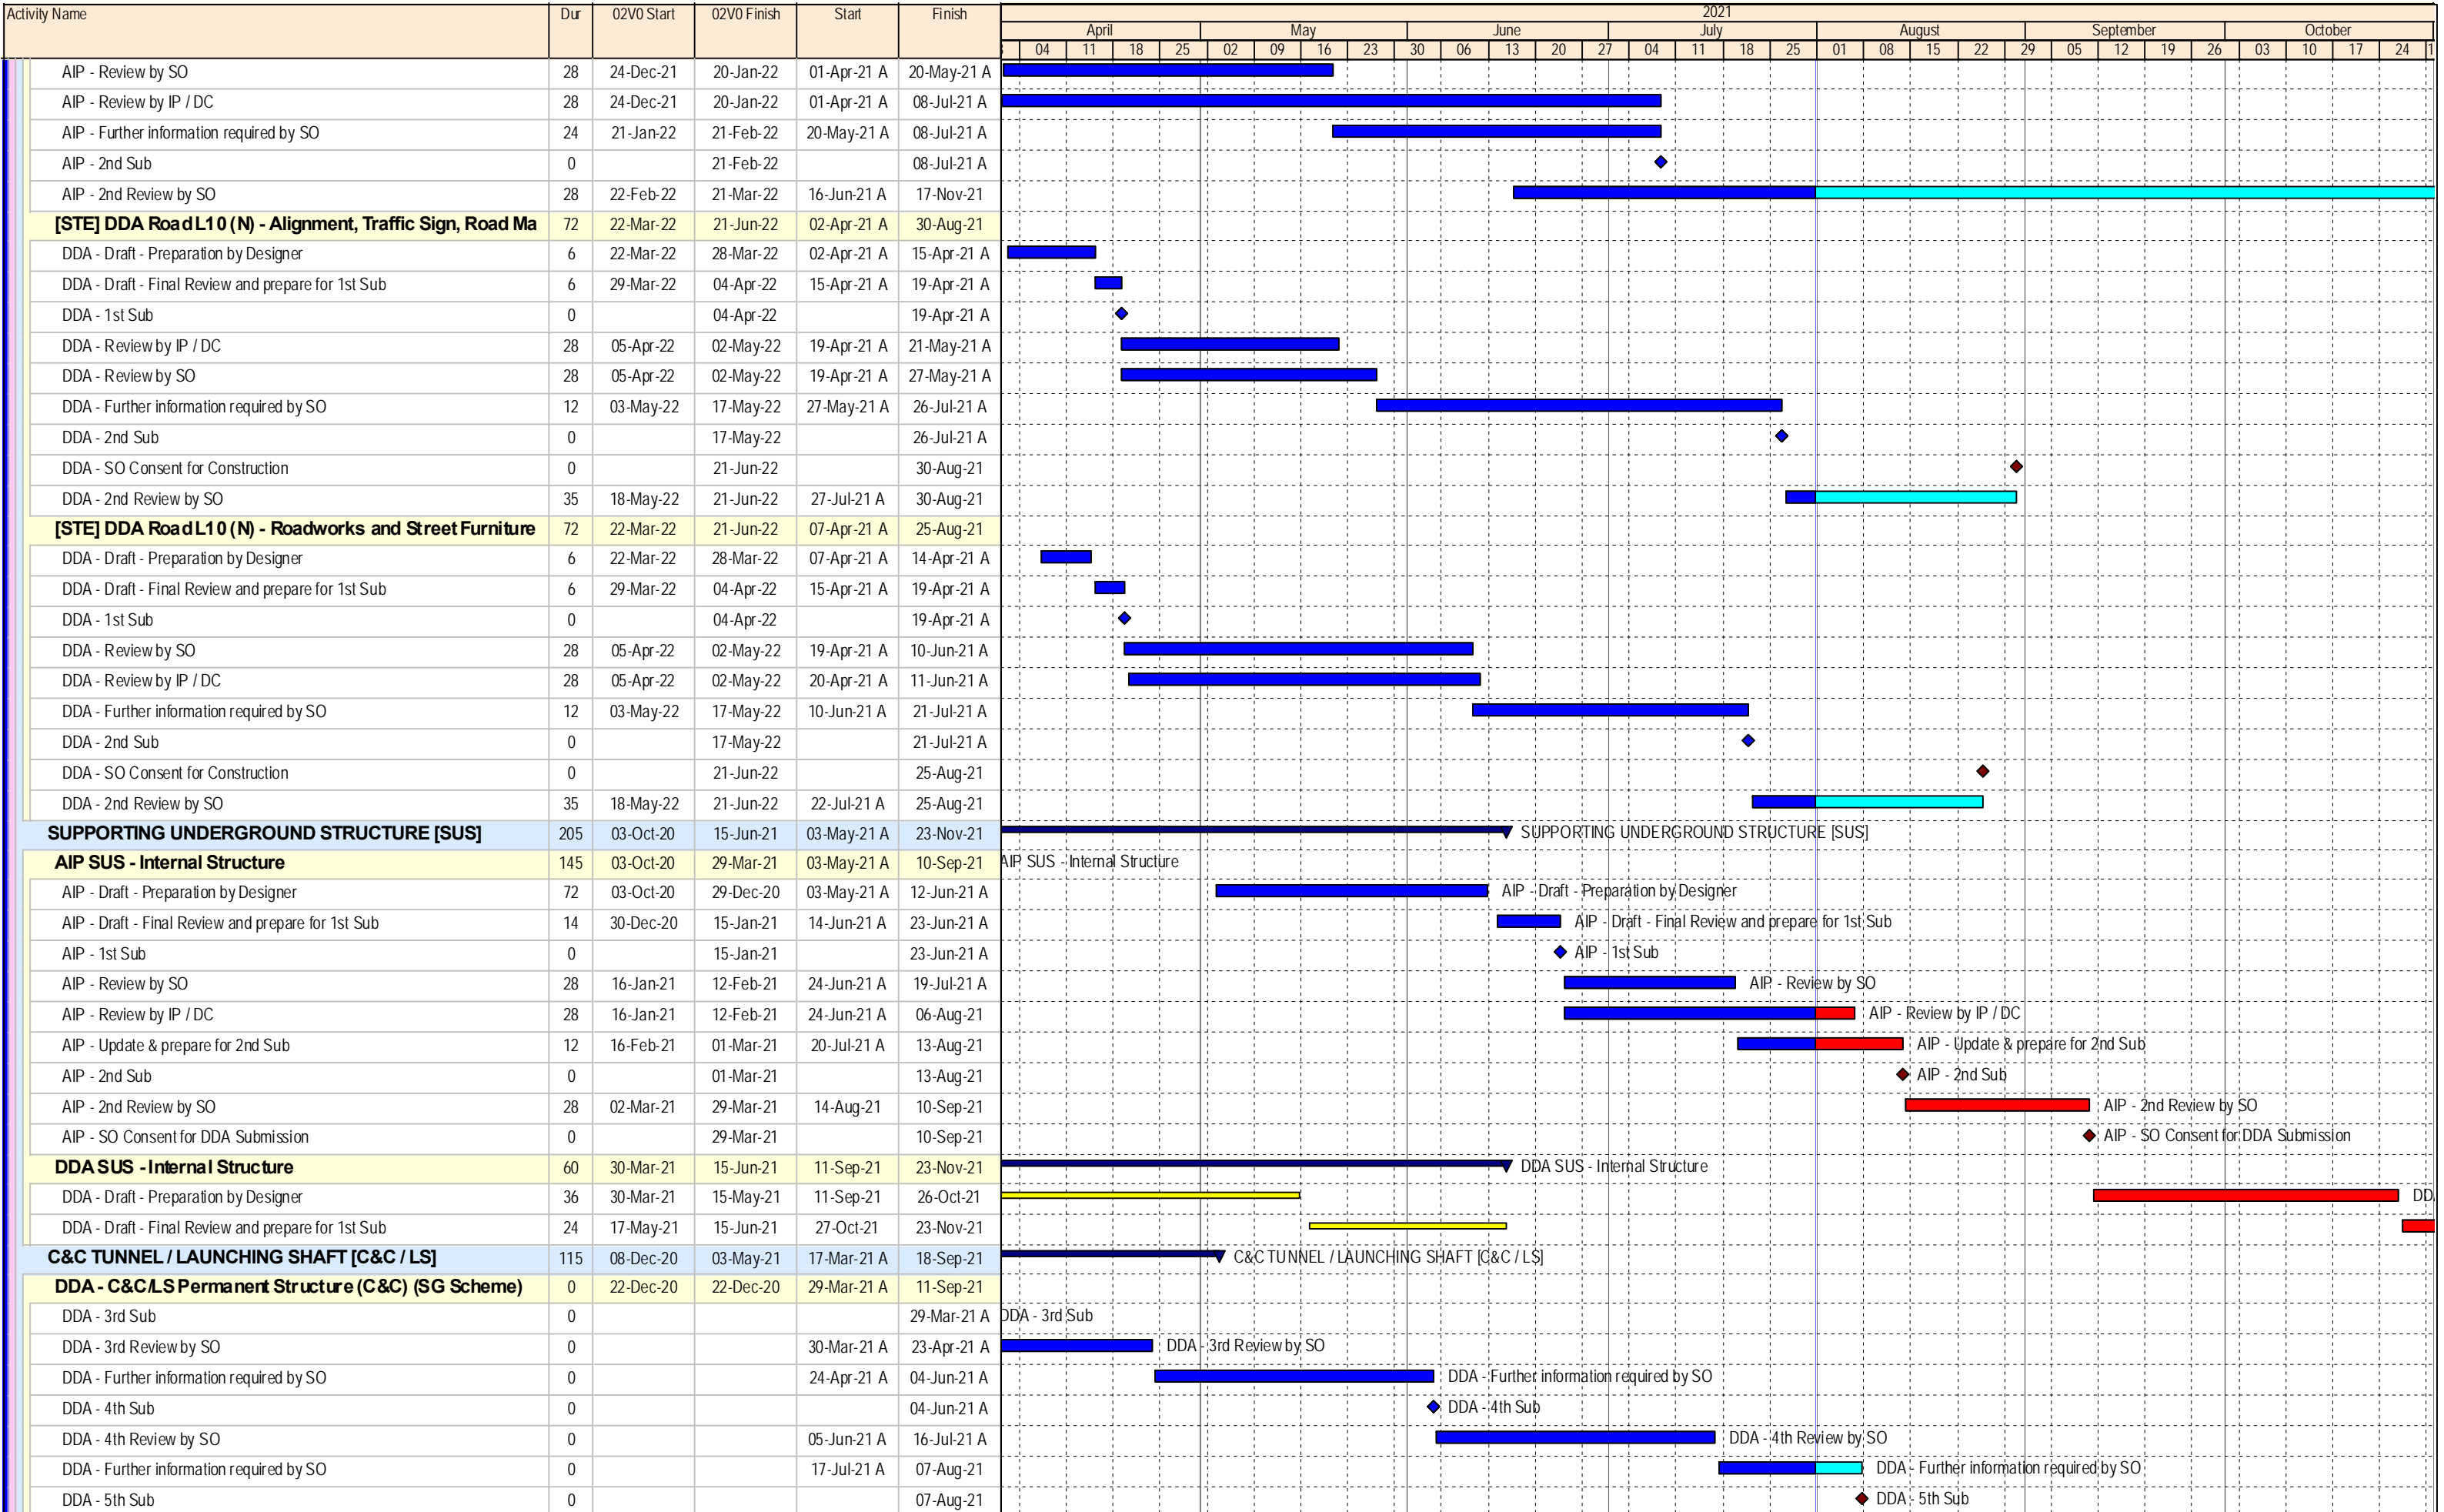


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

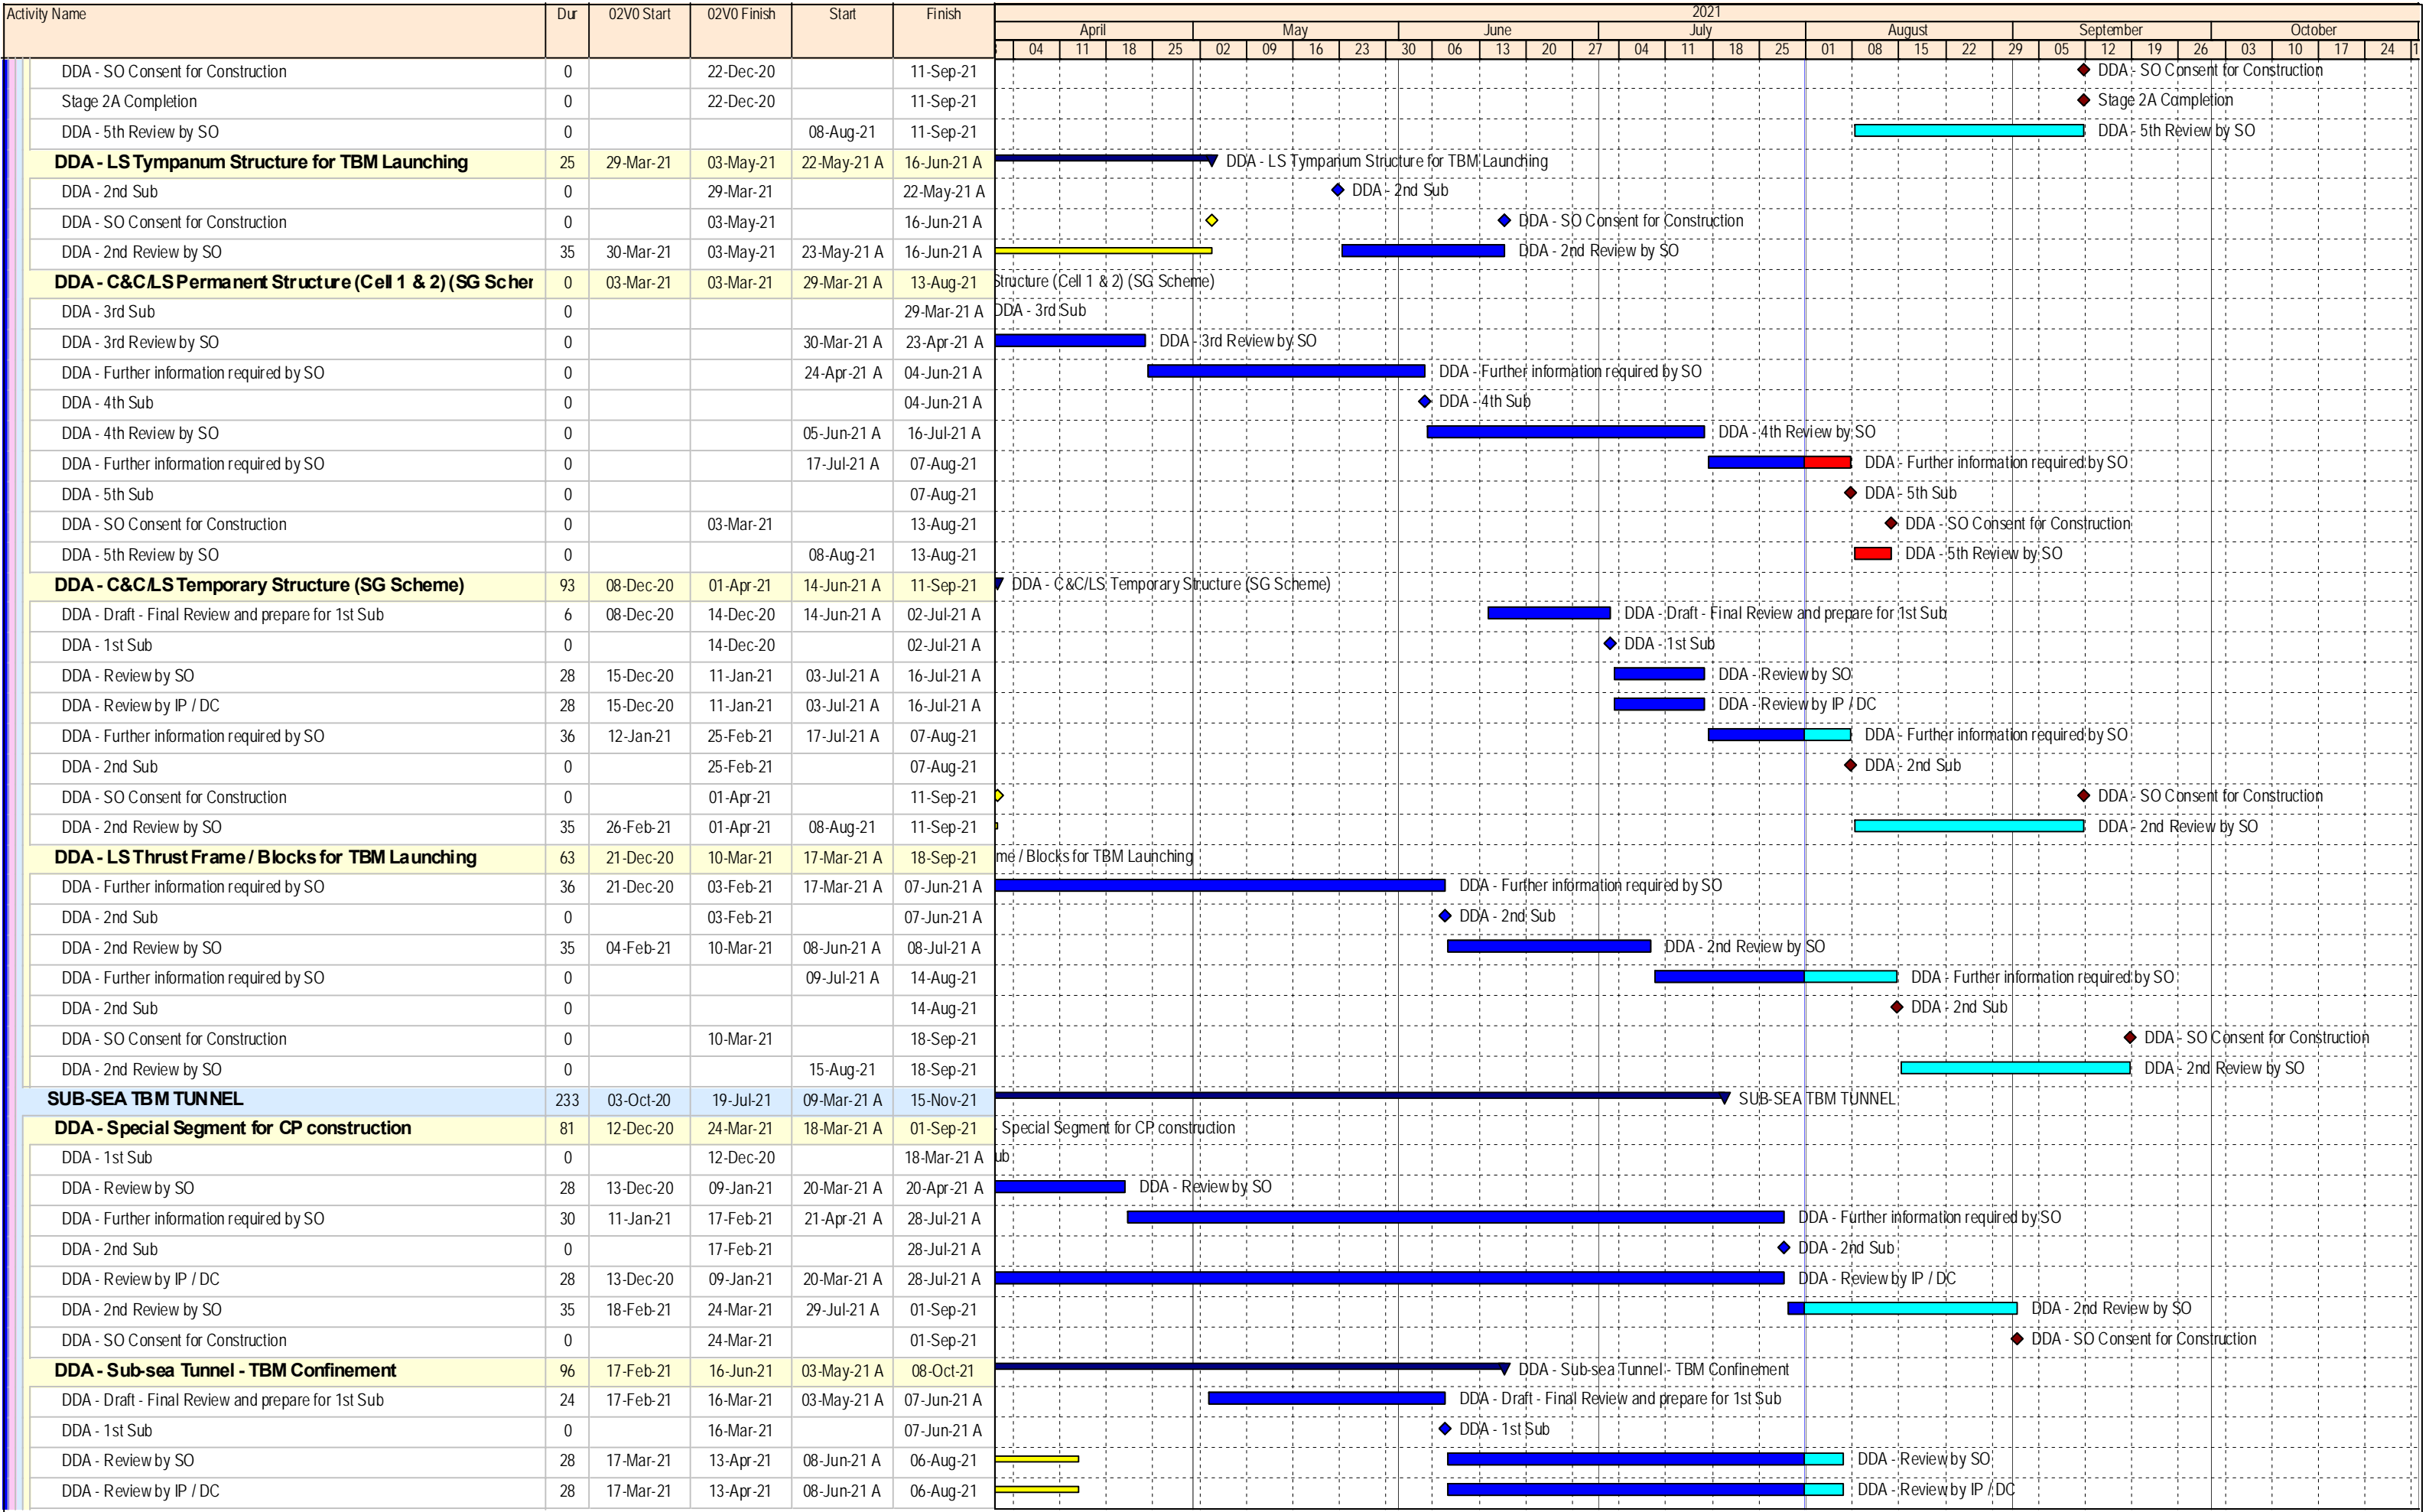


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

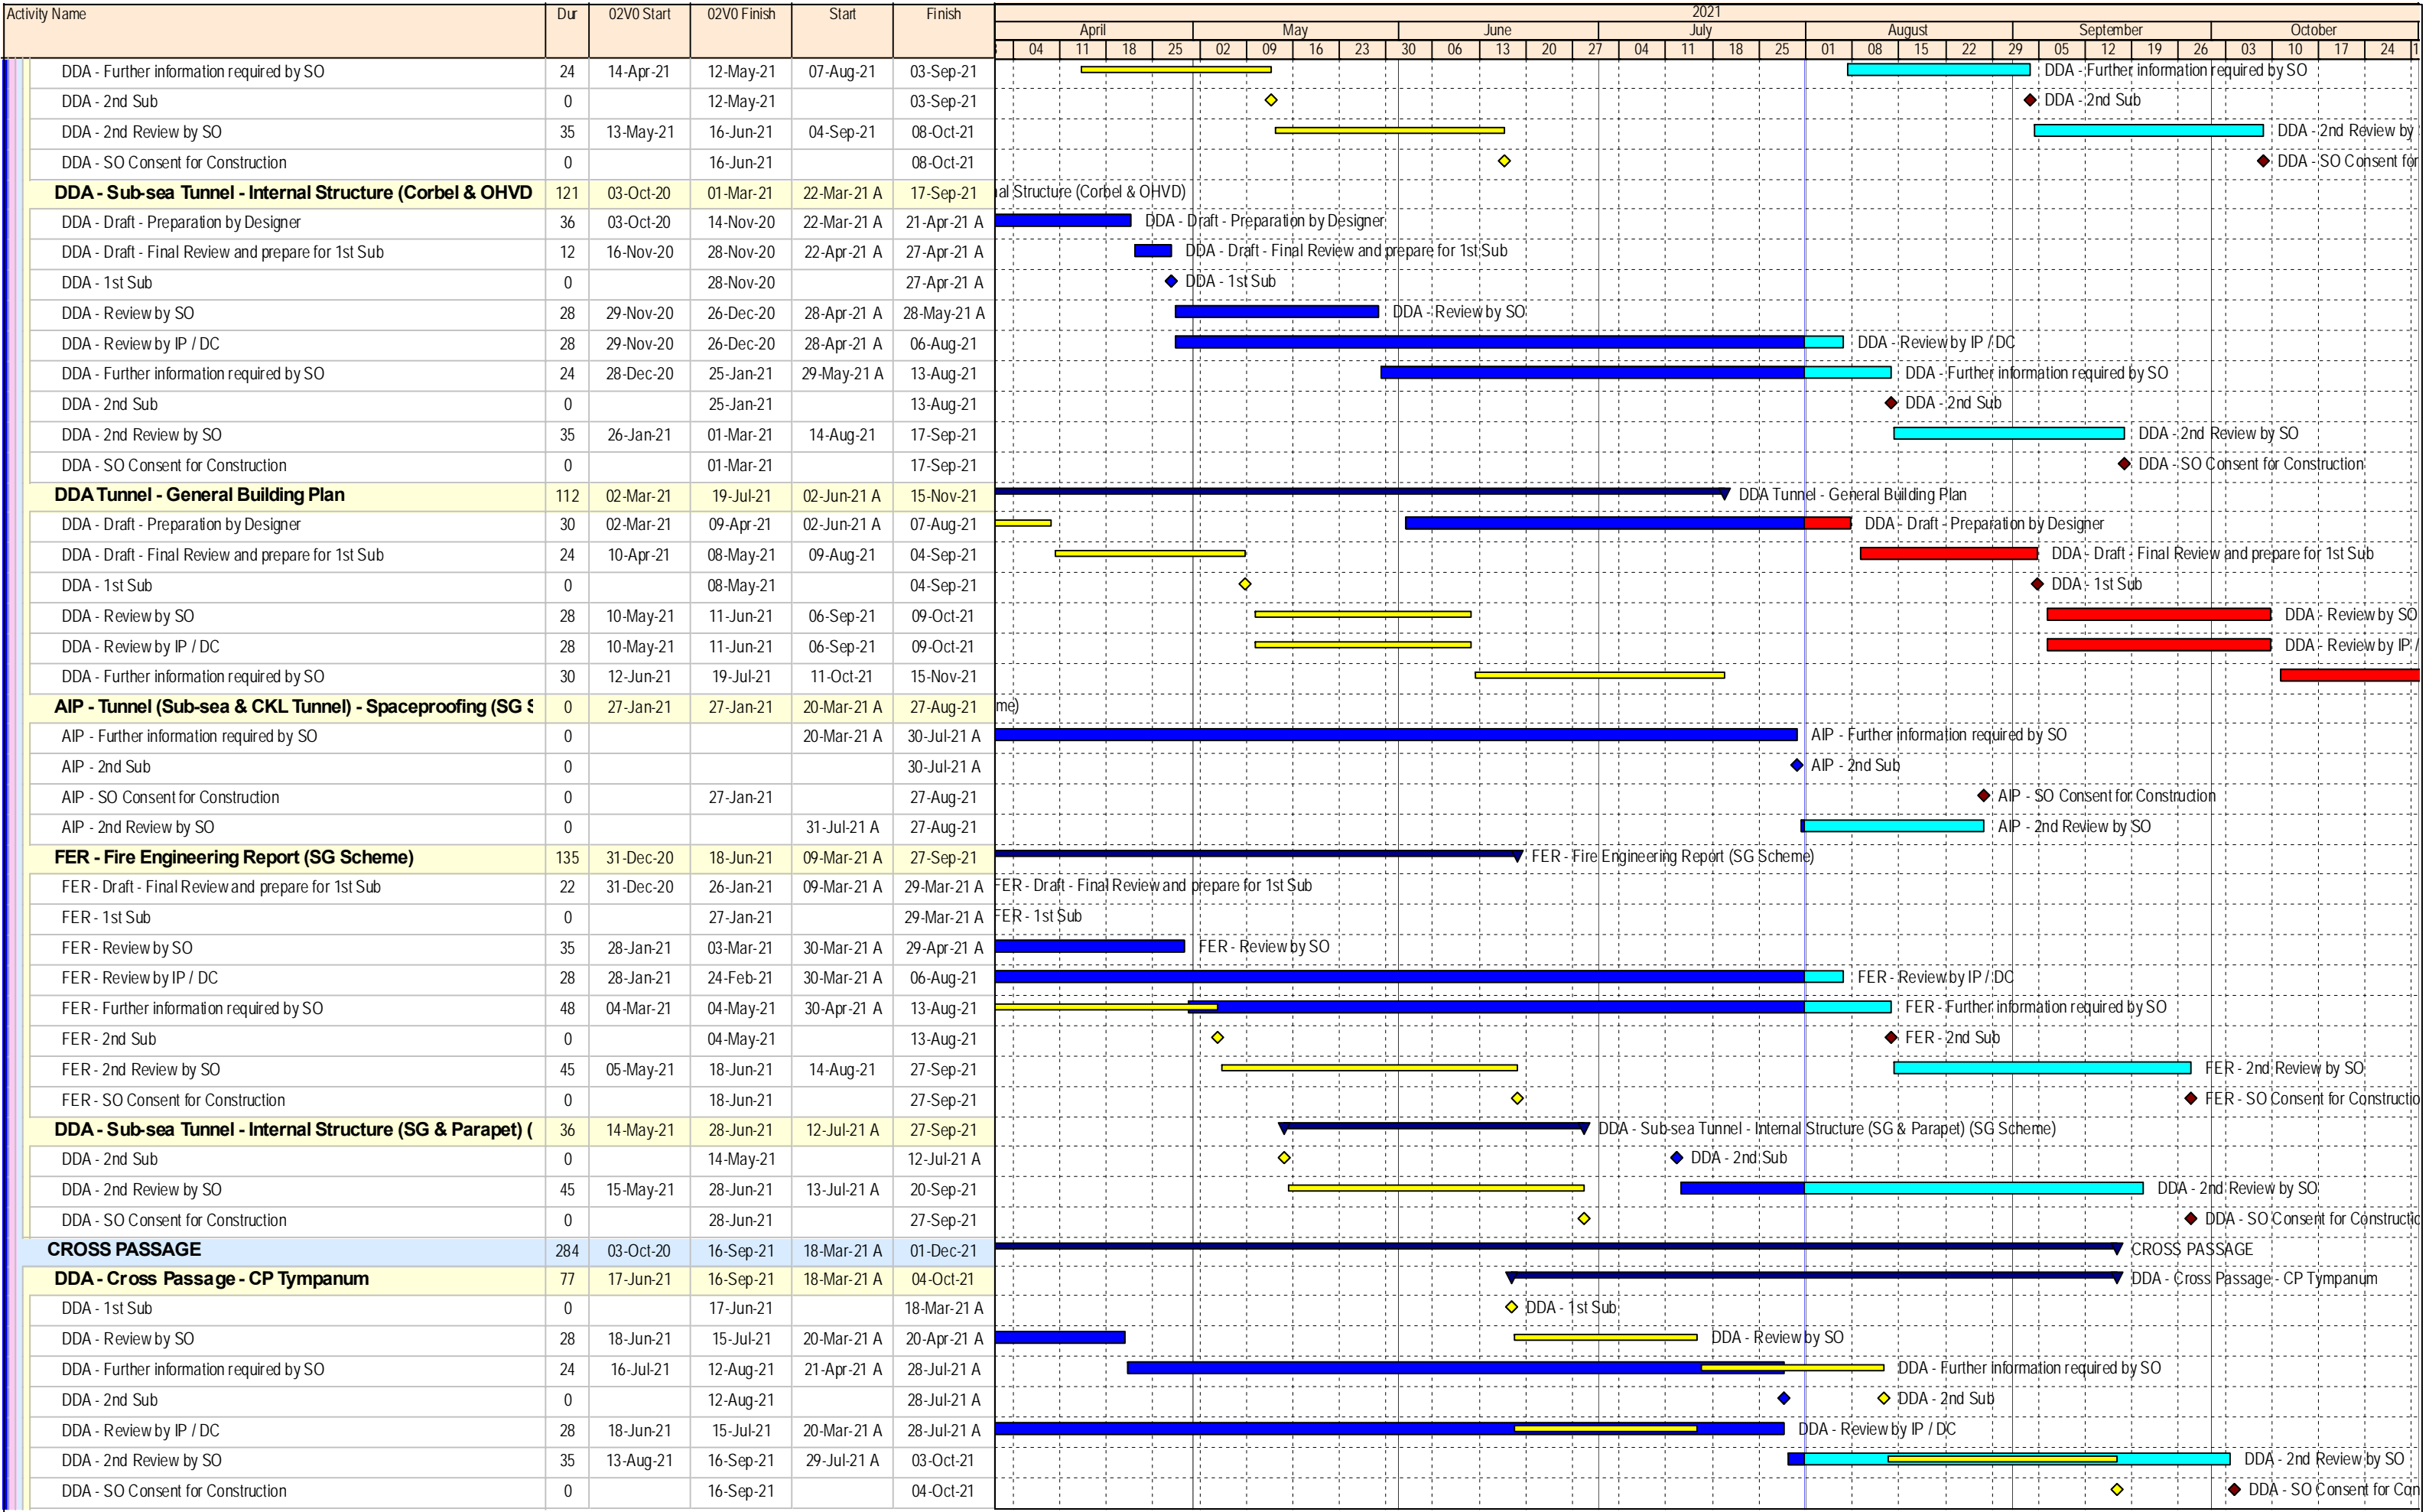

Page 9 of 23
Data Date: 31-Jul-21


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

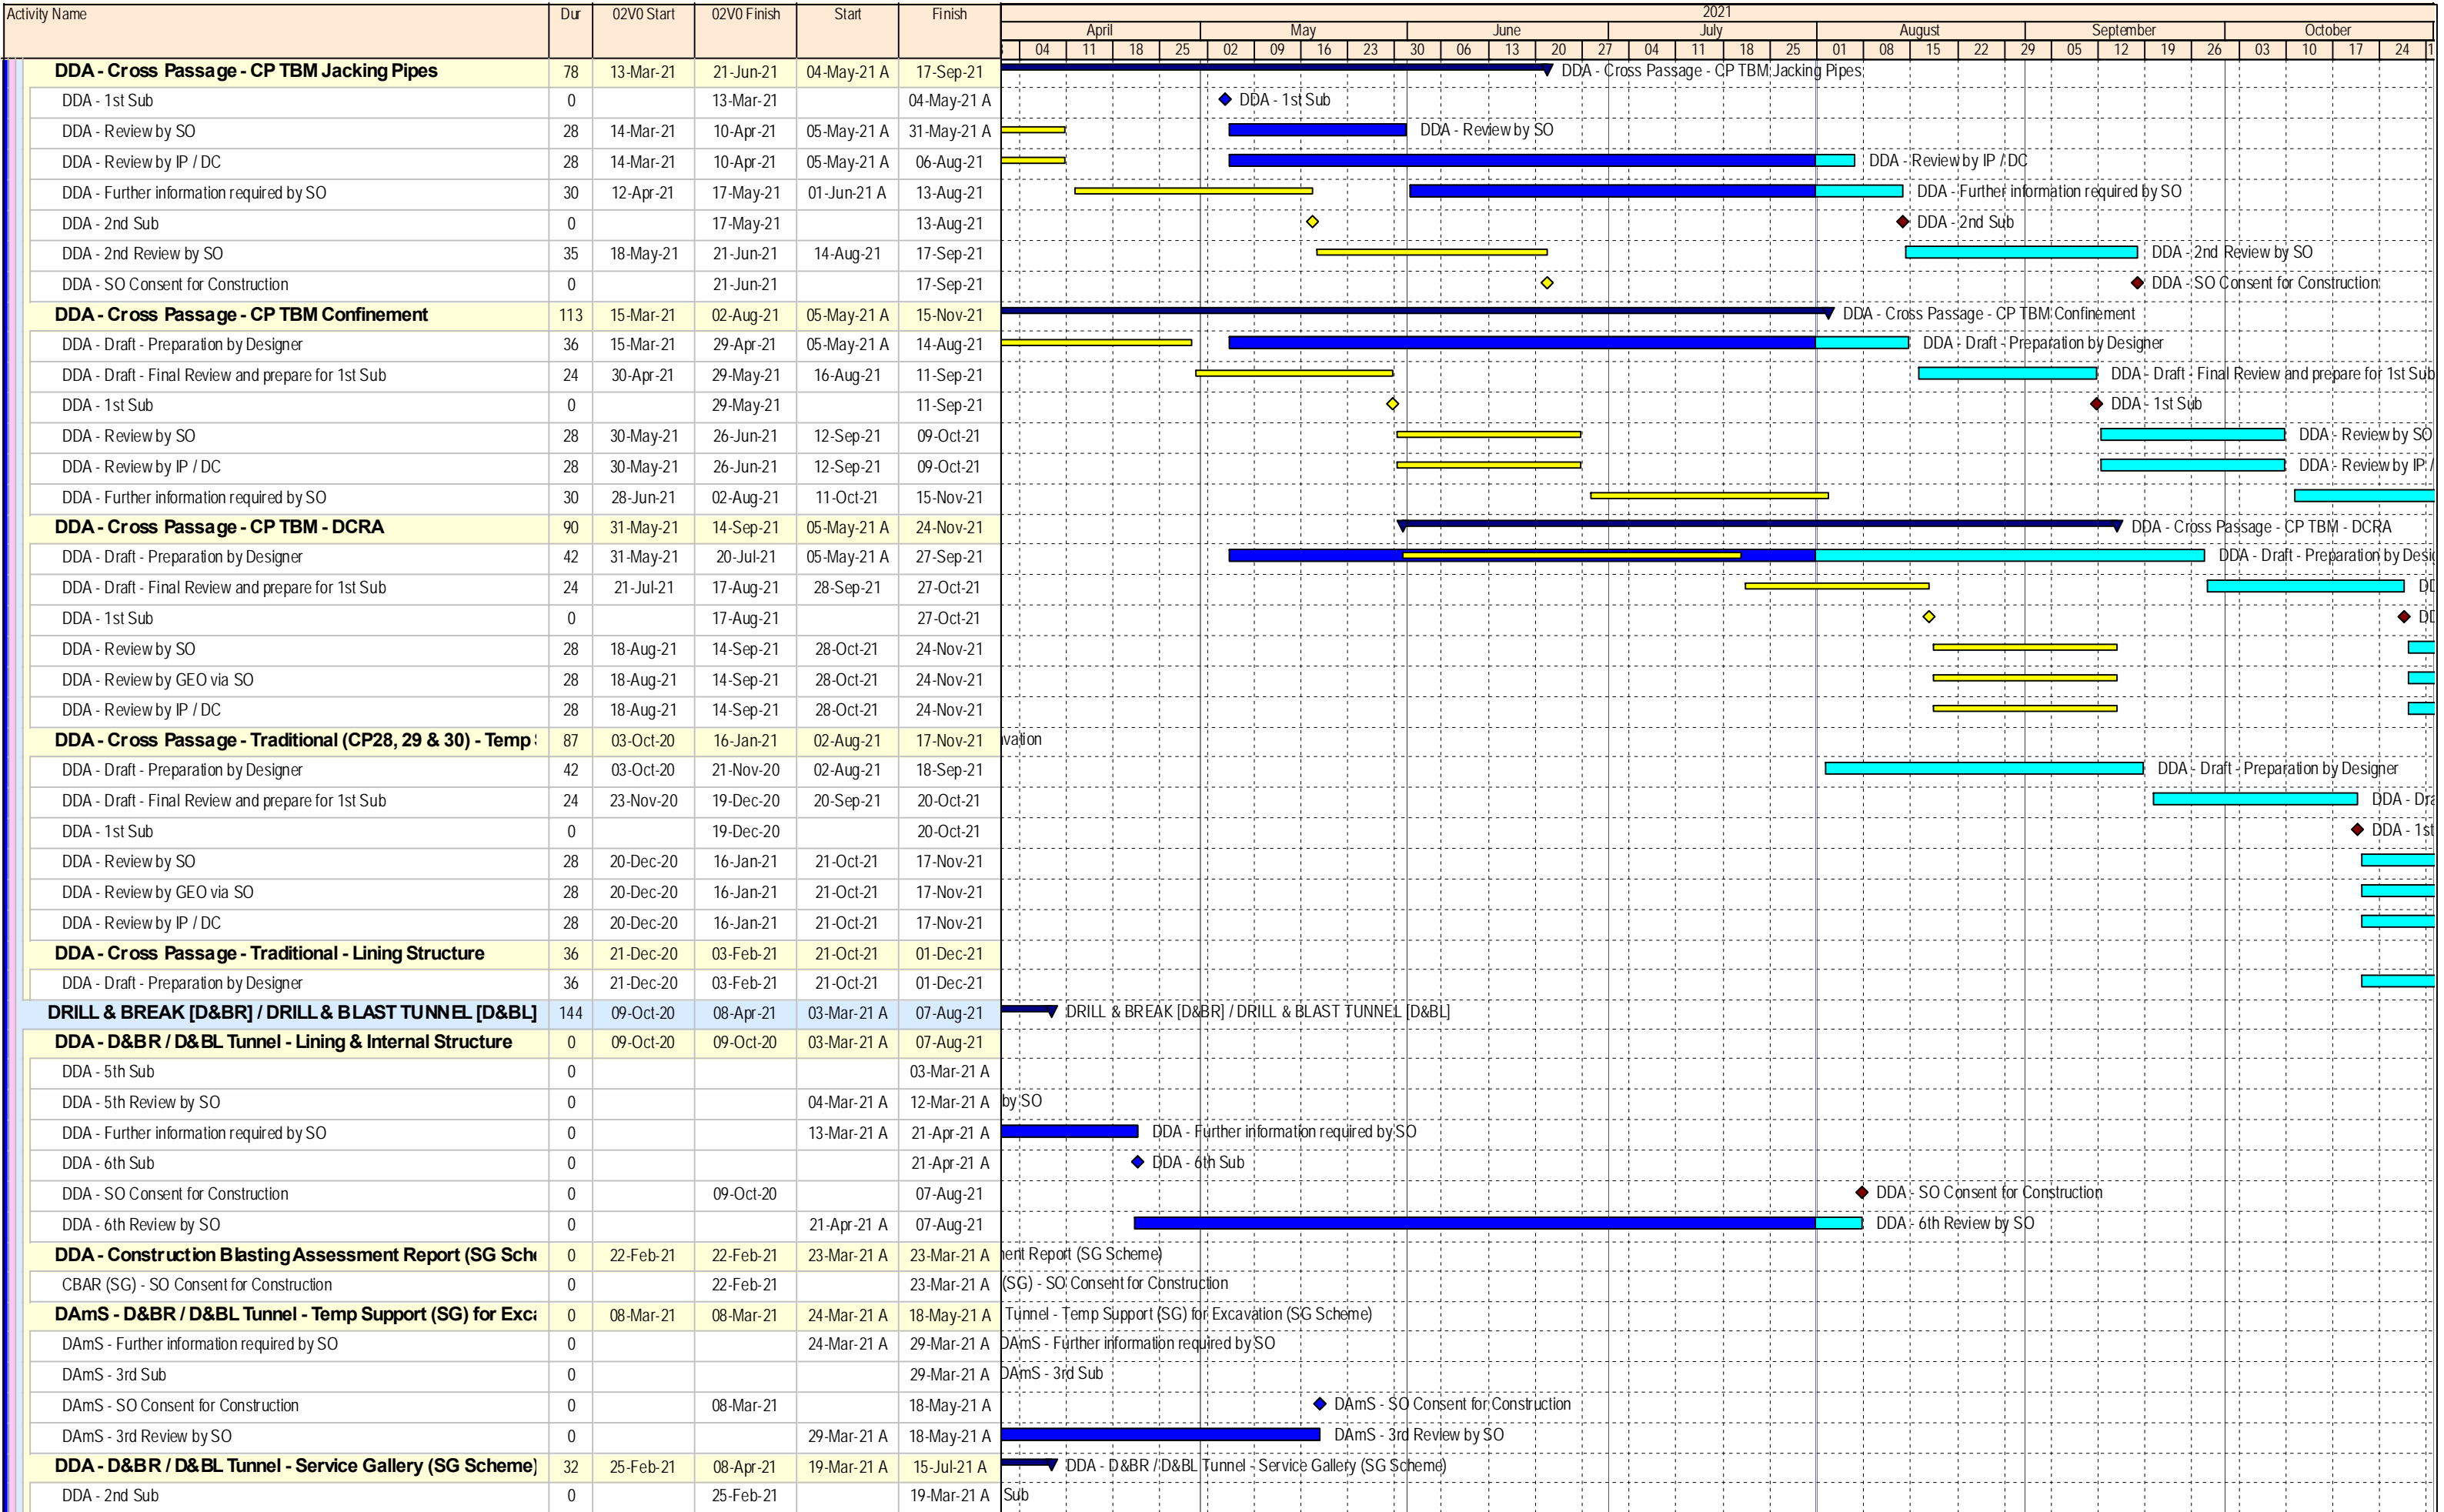


- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- ◆ Summary
- Planned Bar
- Critical Activity
- Actual Work
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

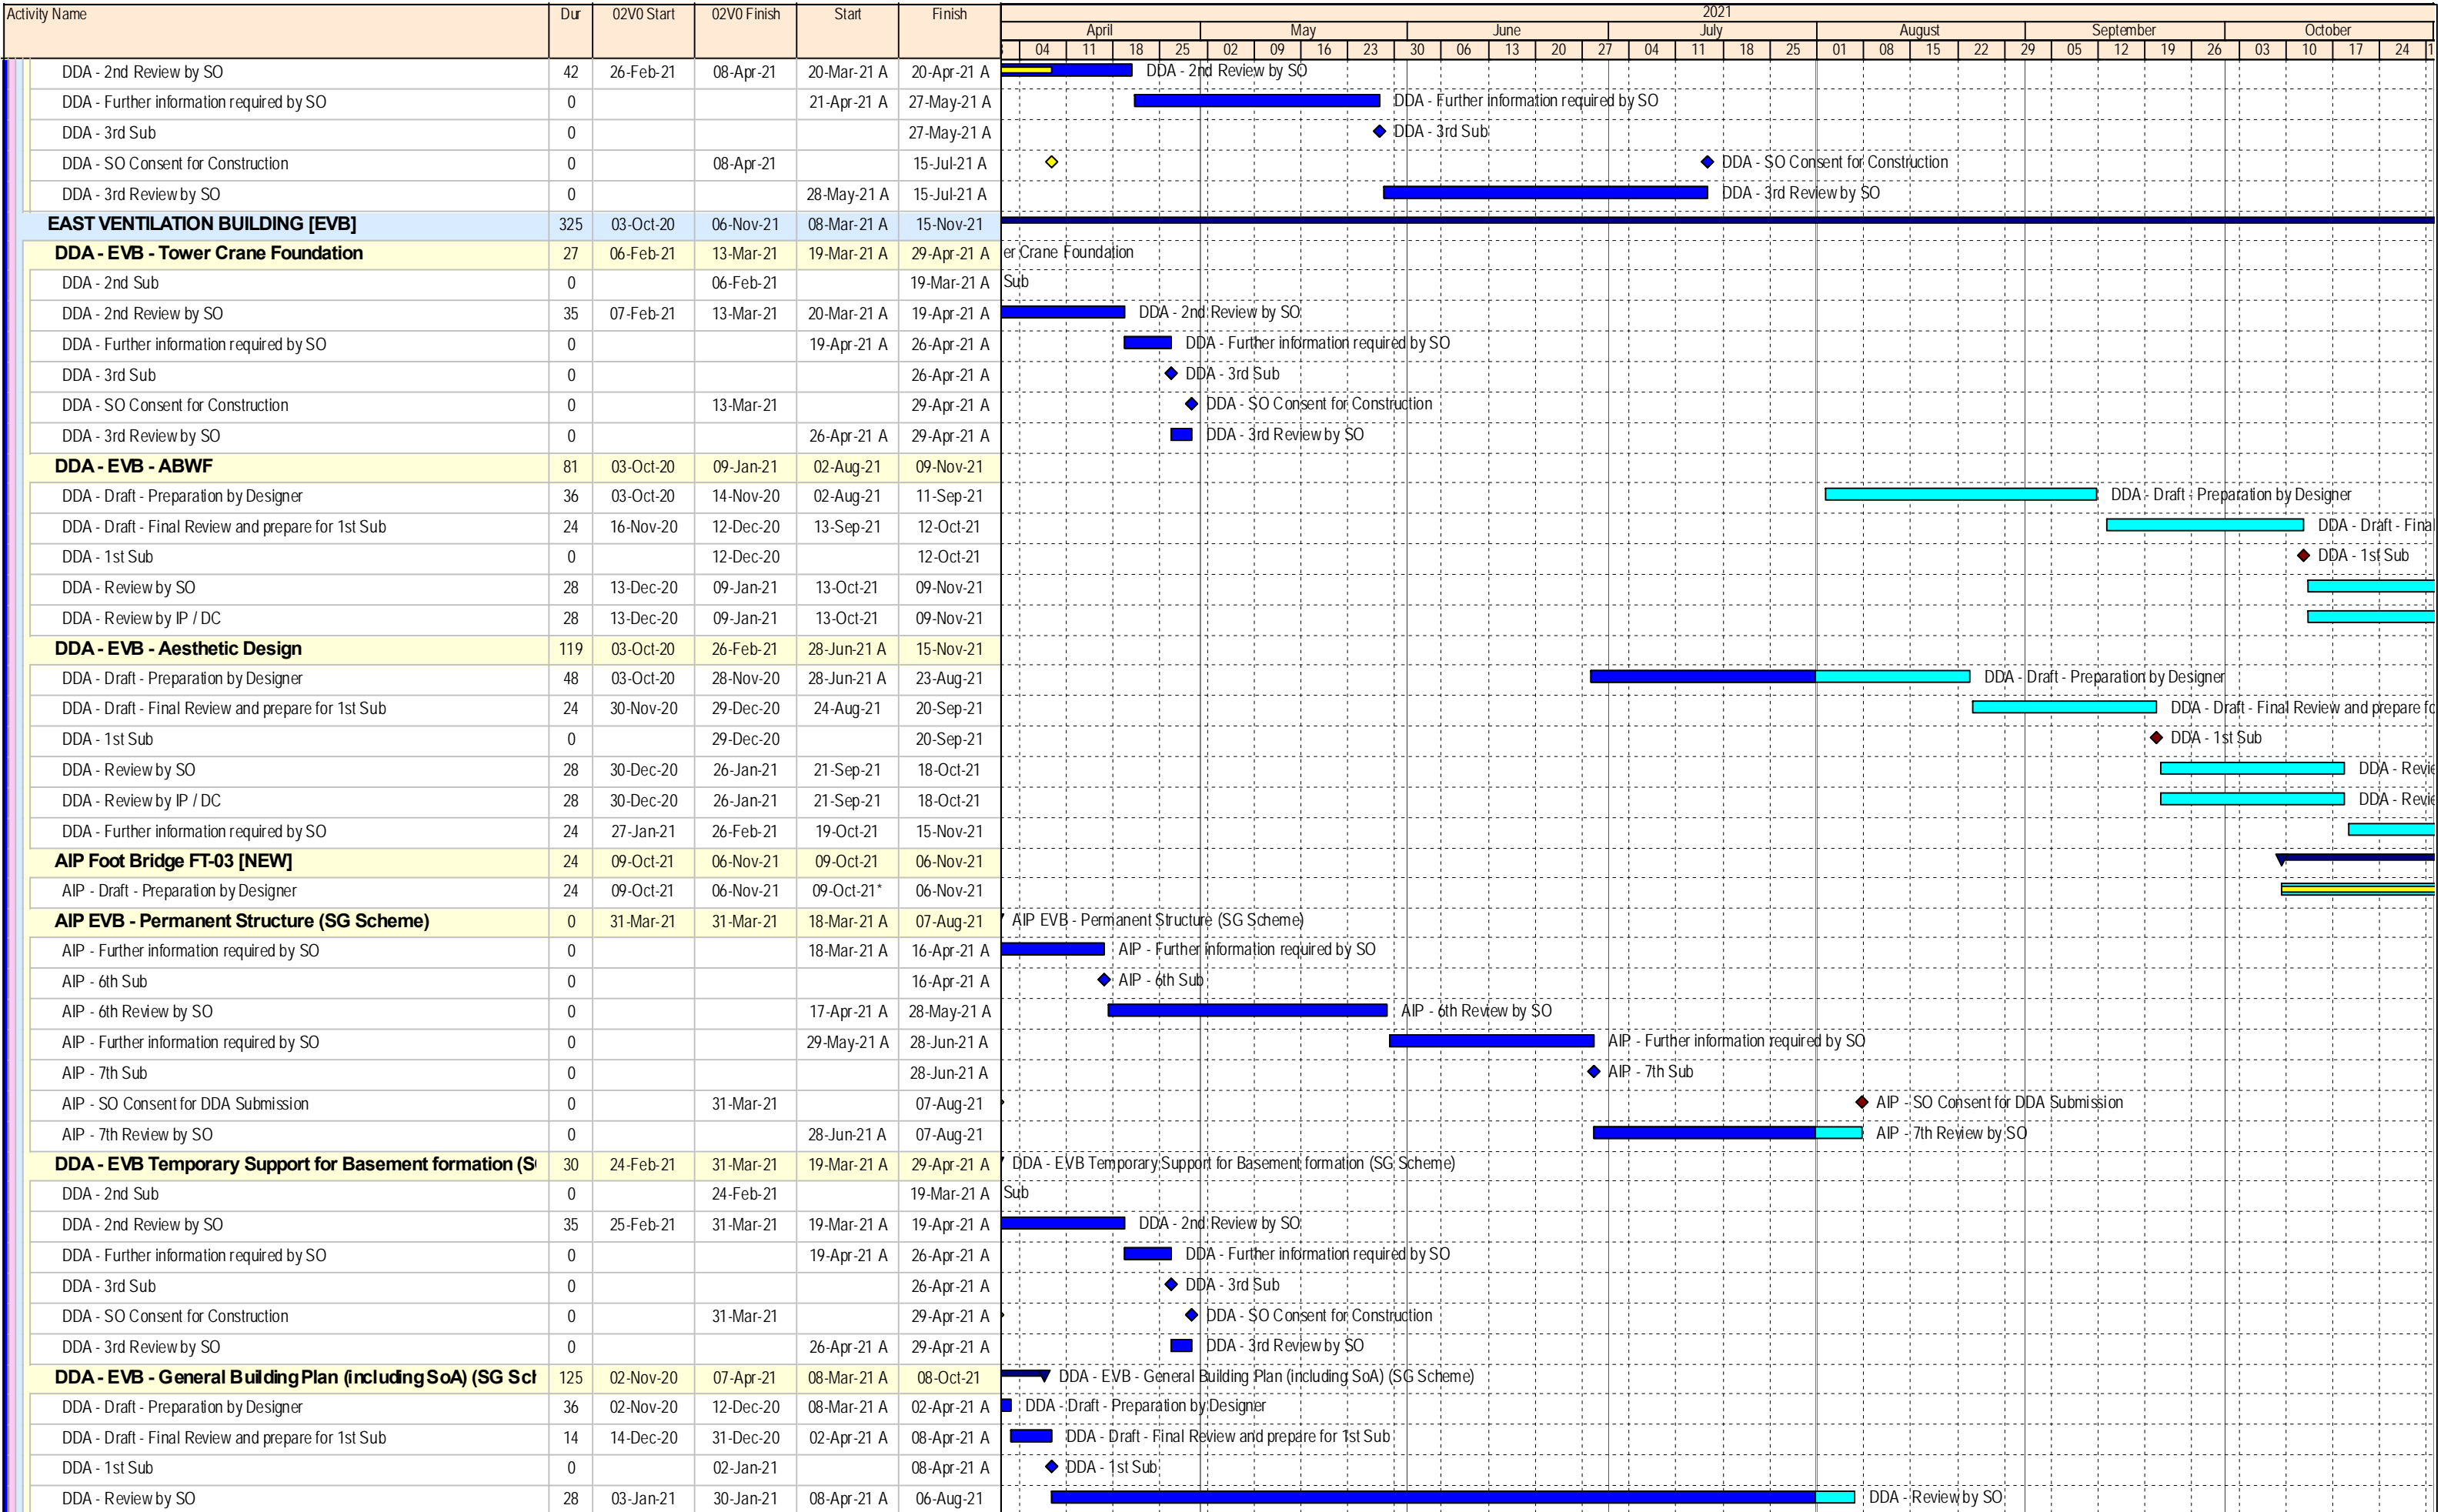


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

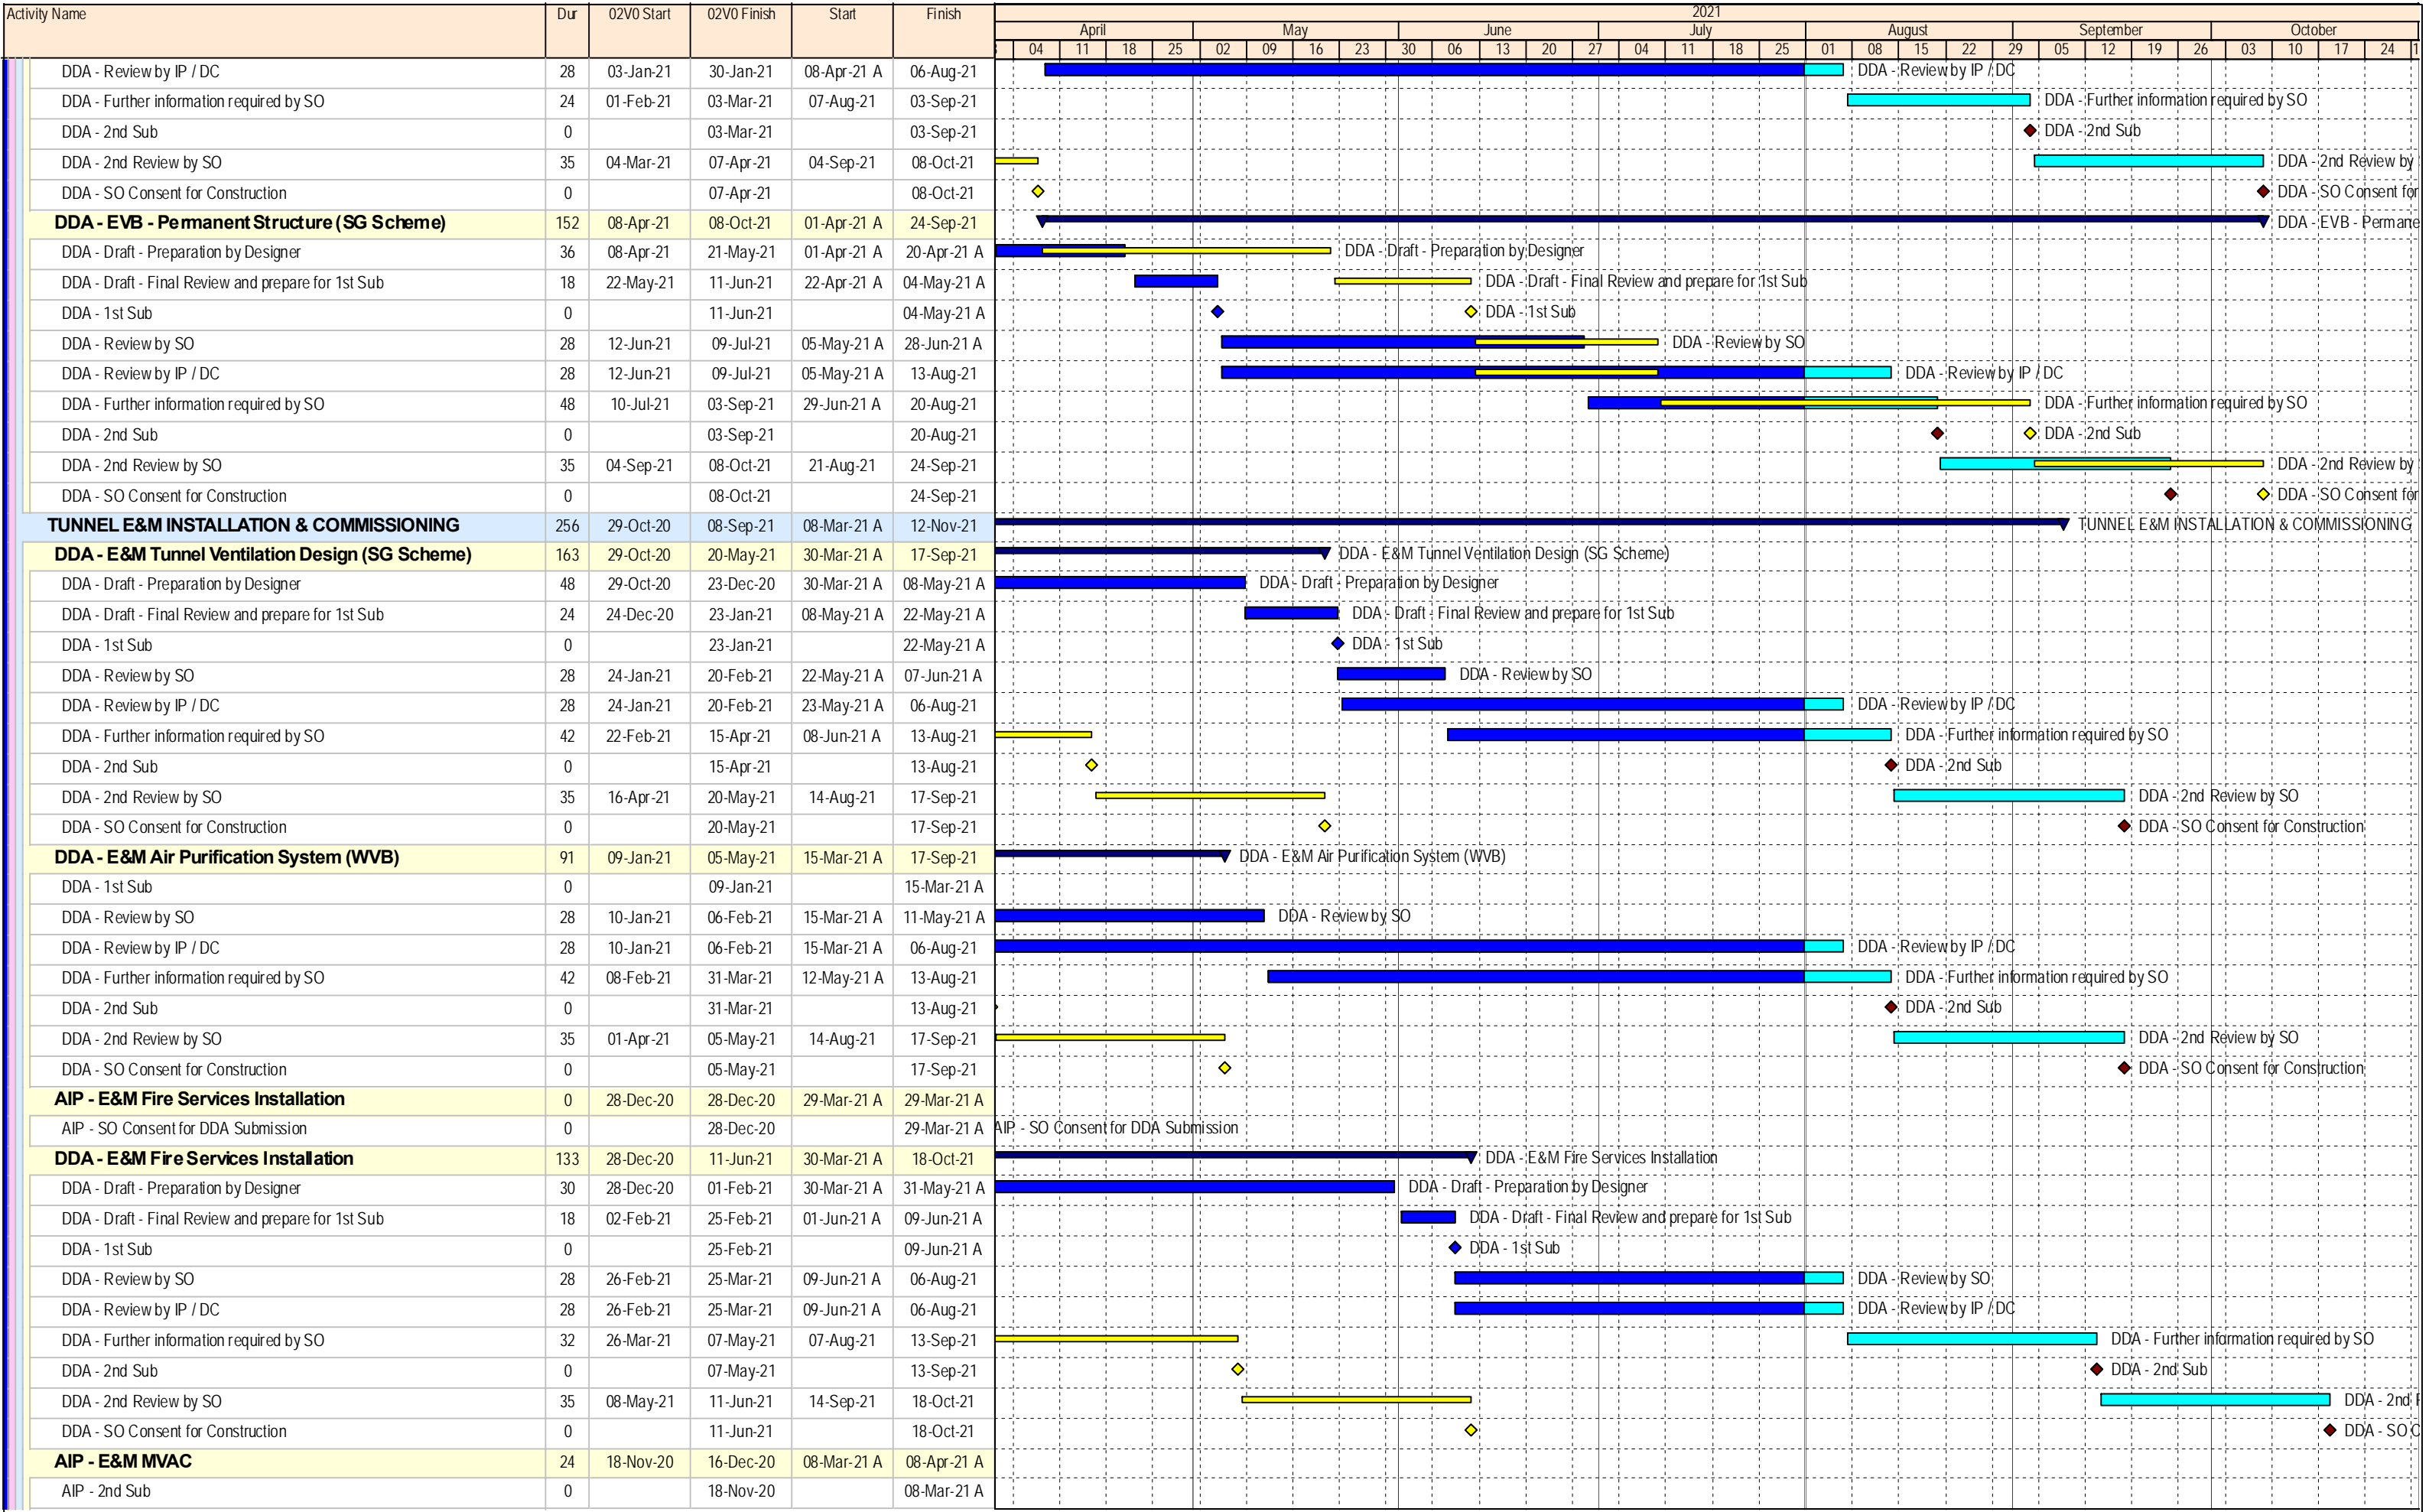


- Milestone
- Summary
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

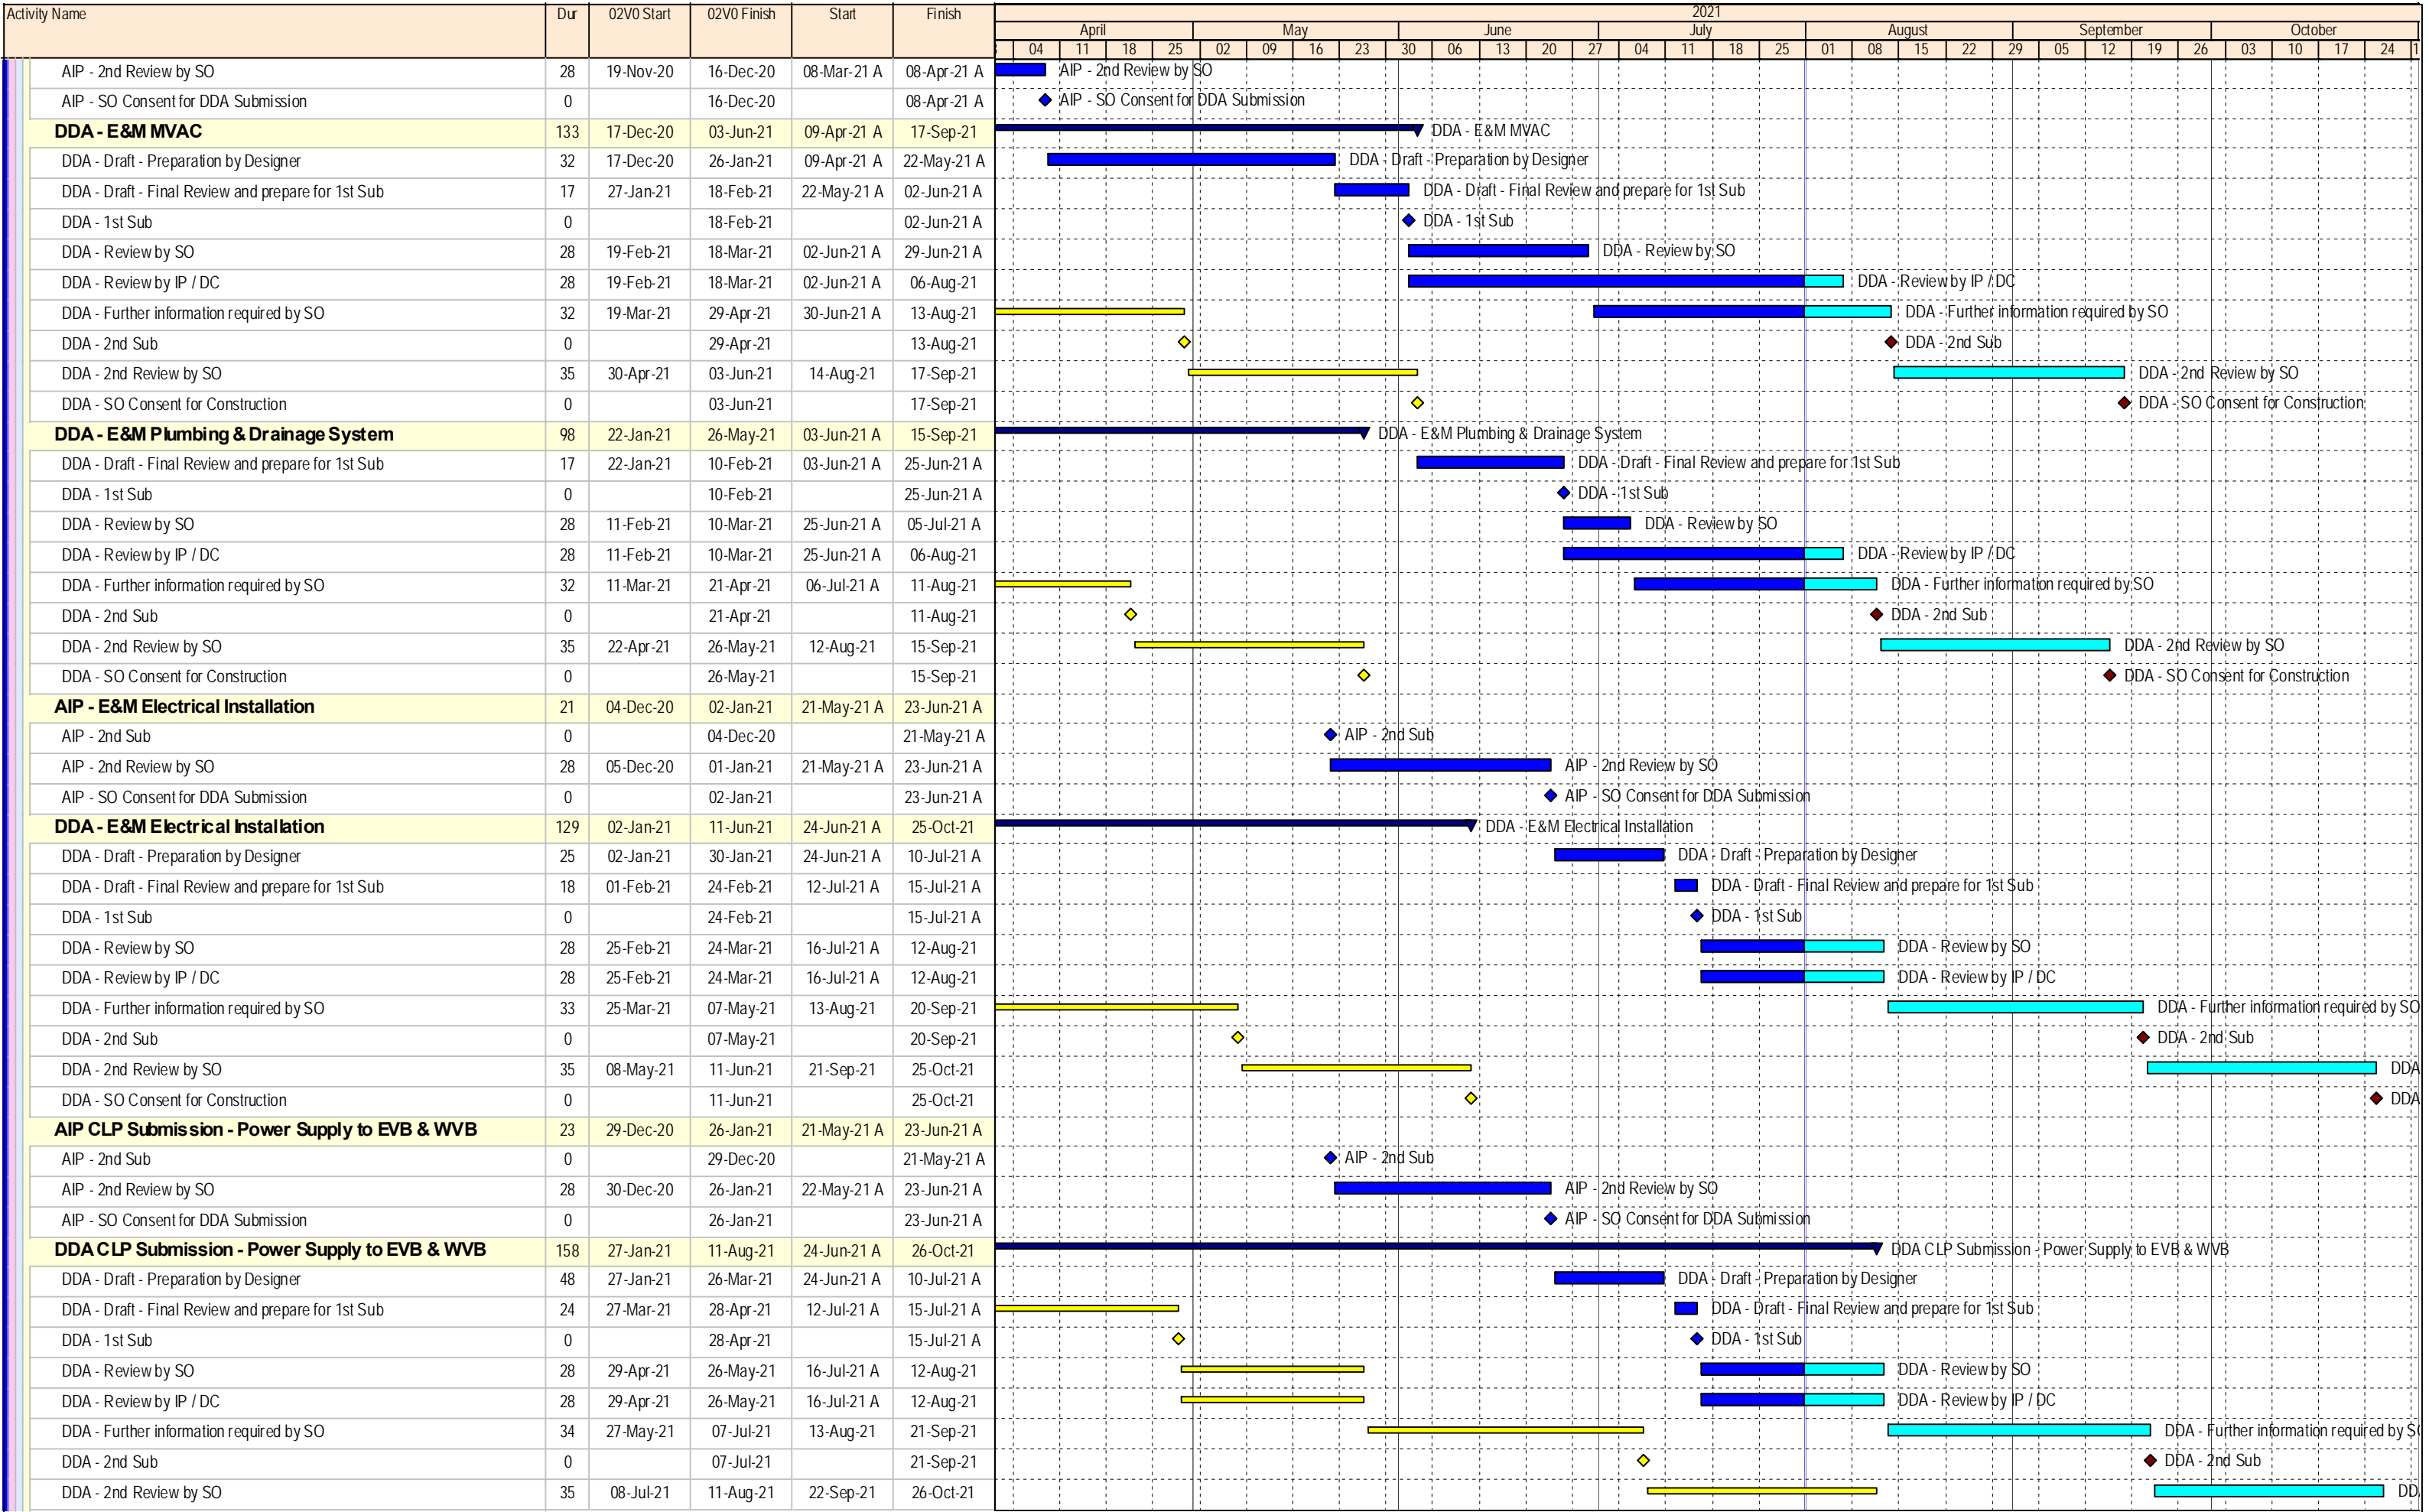


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

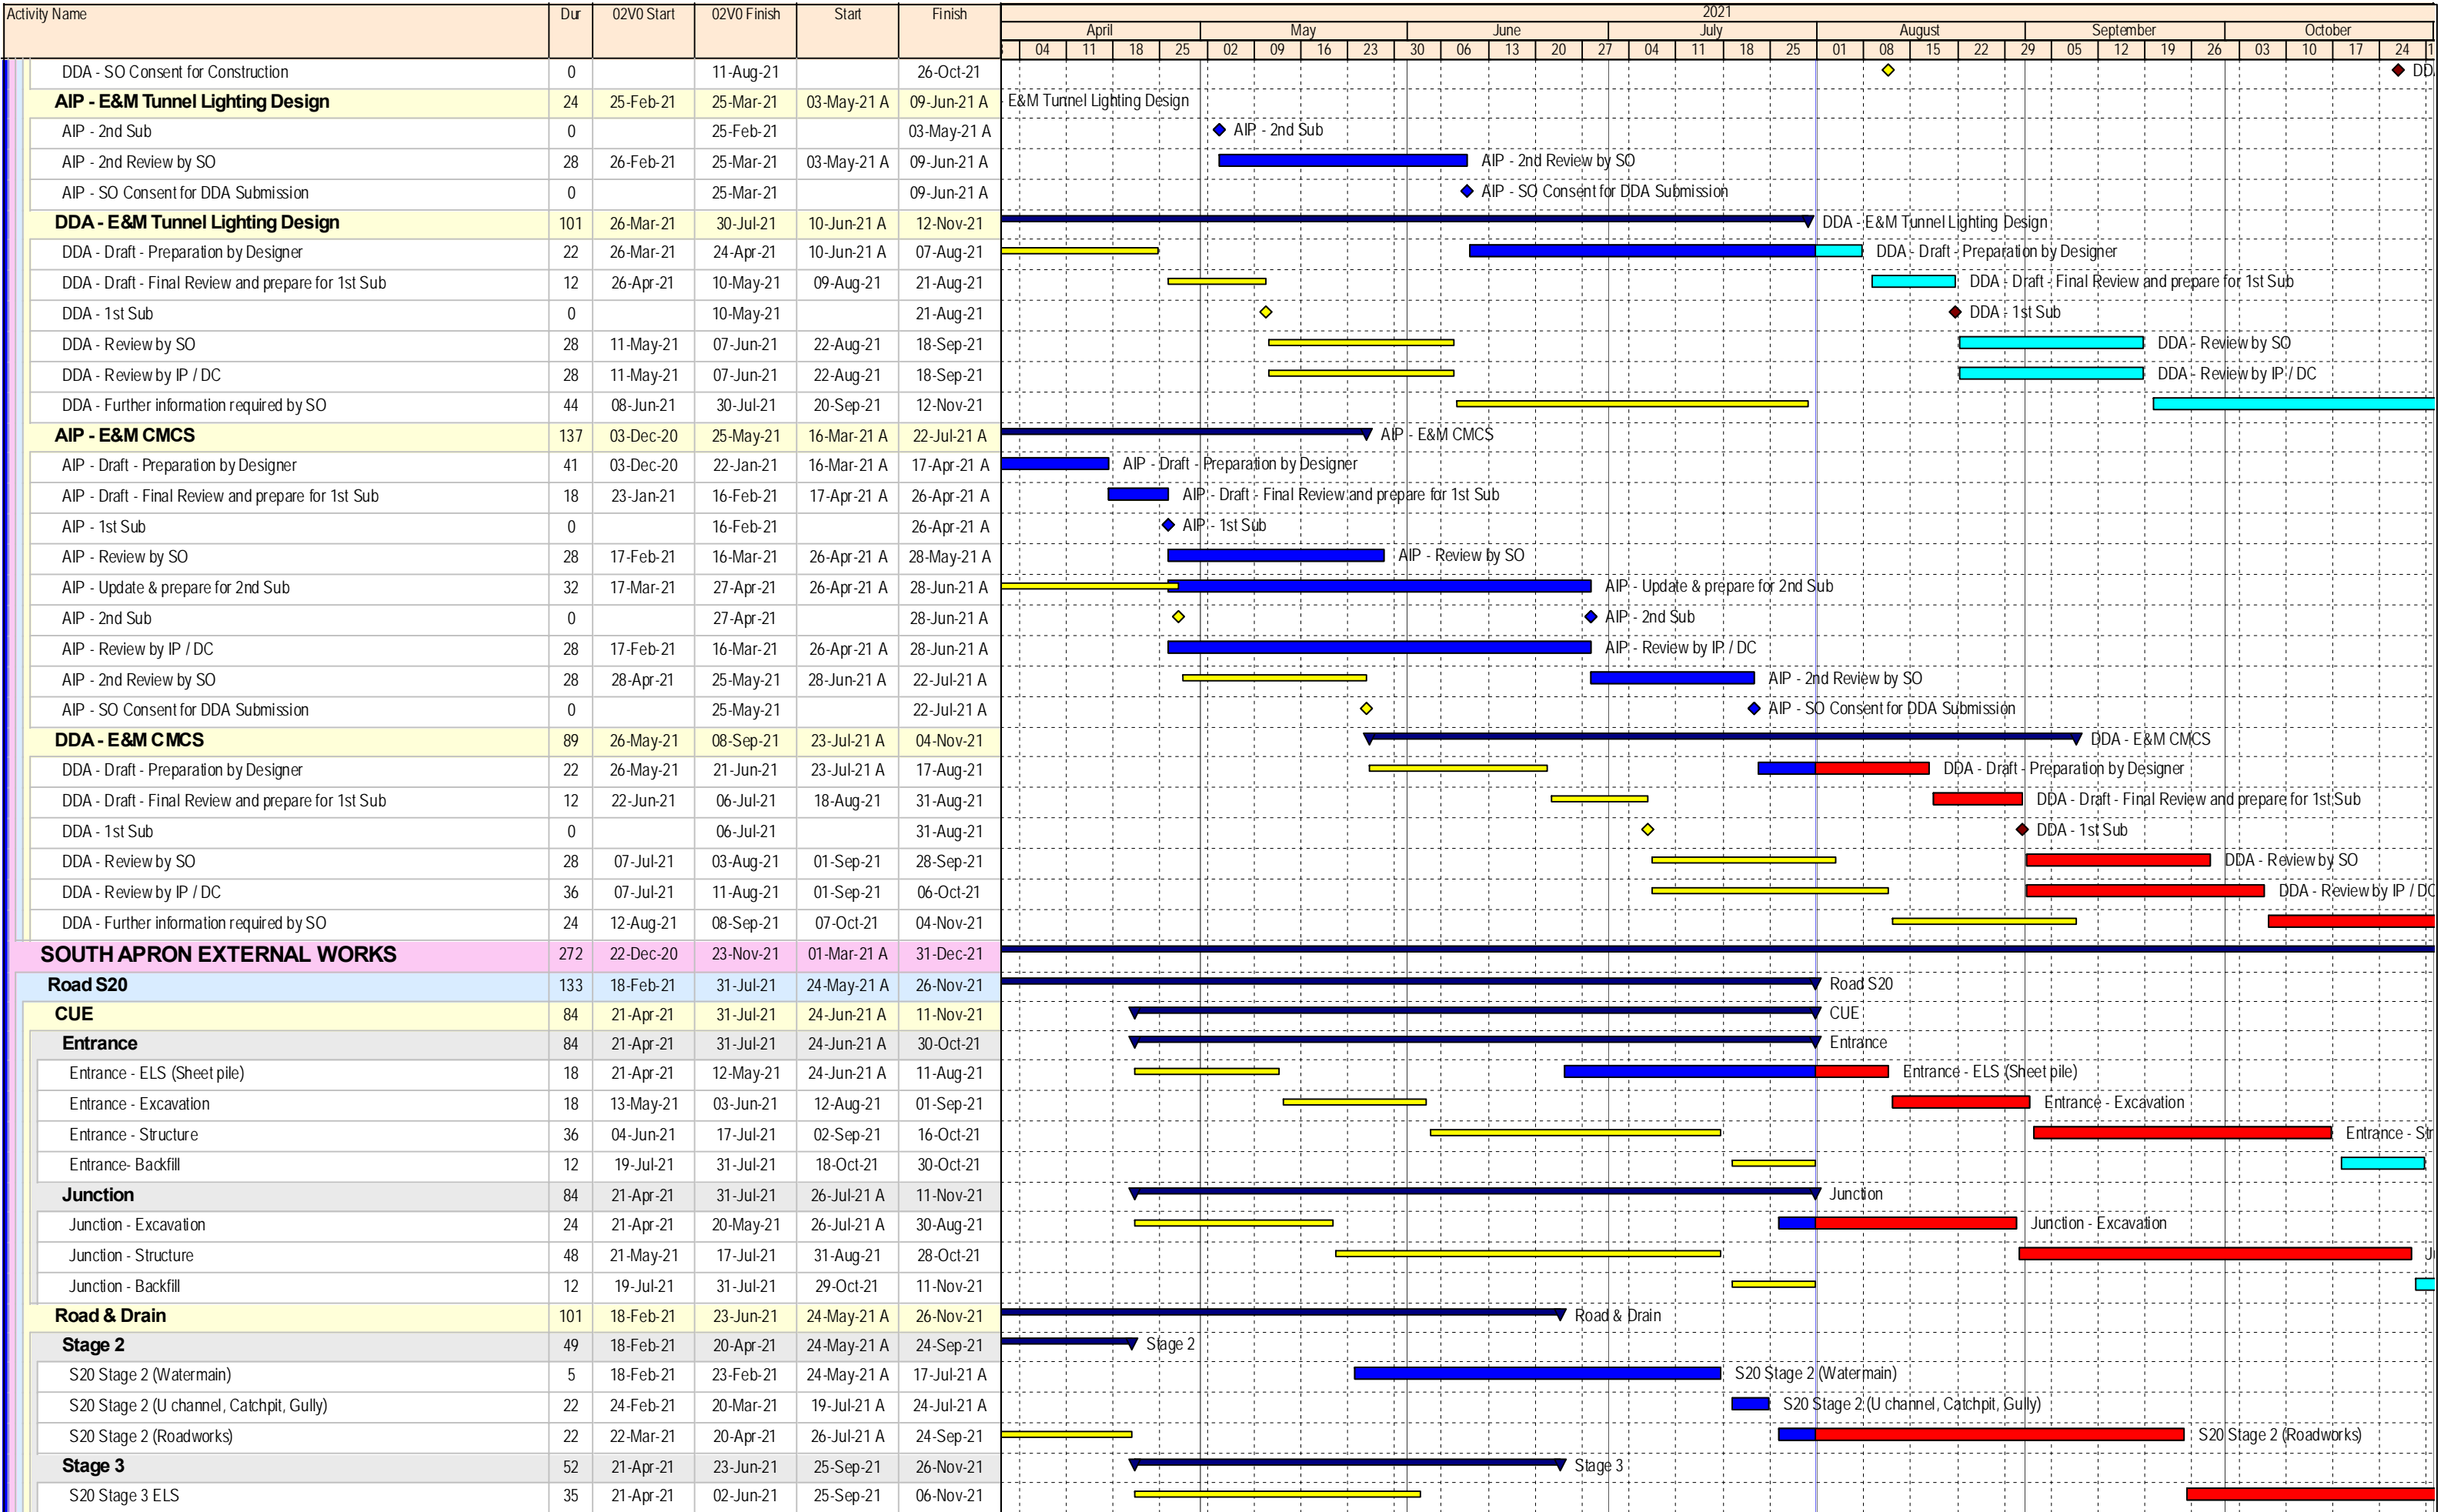


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬▬▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

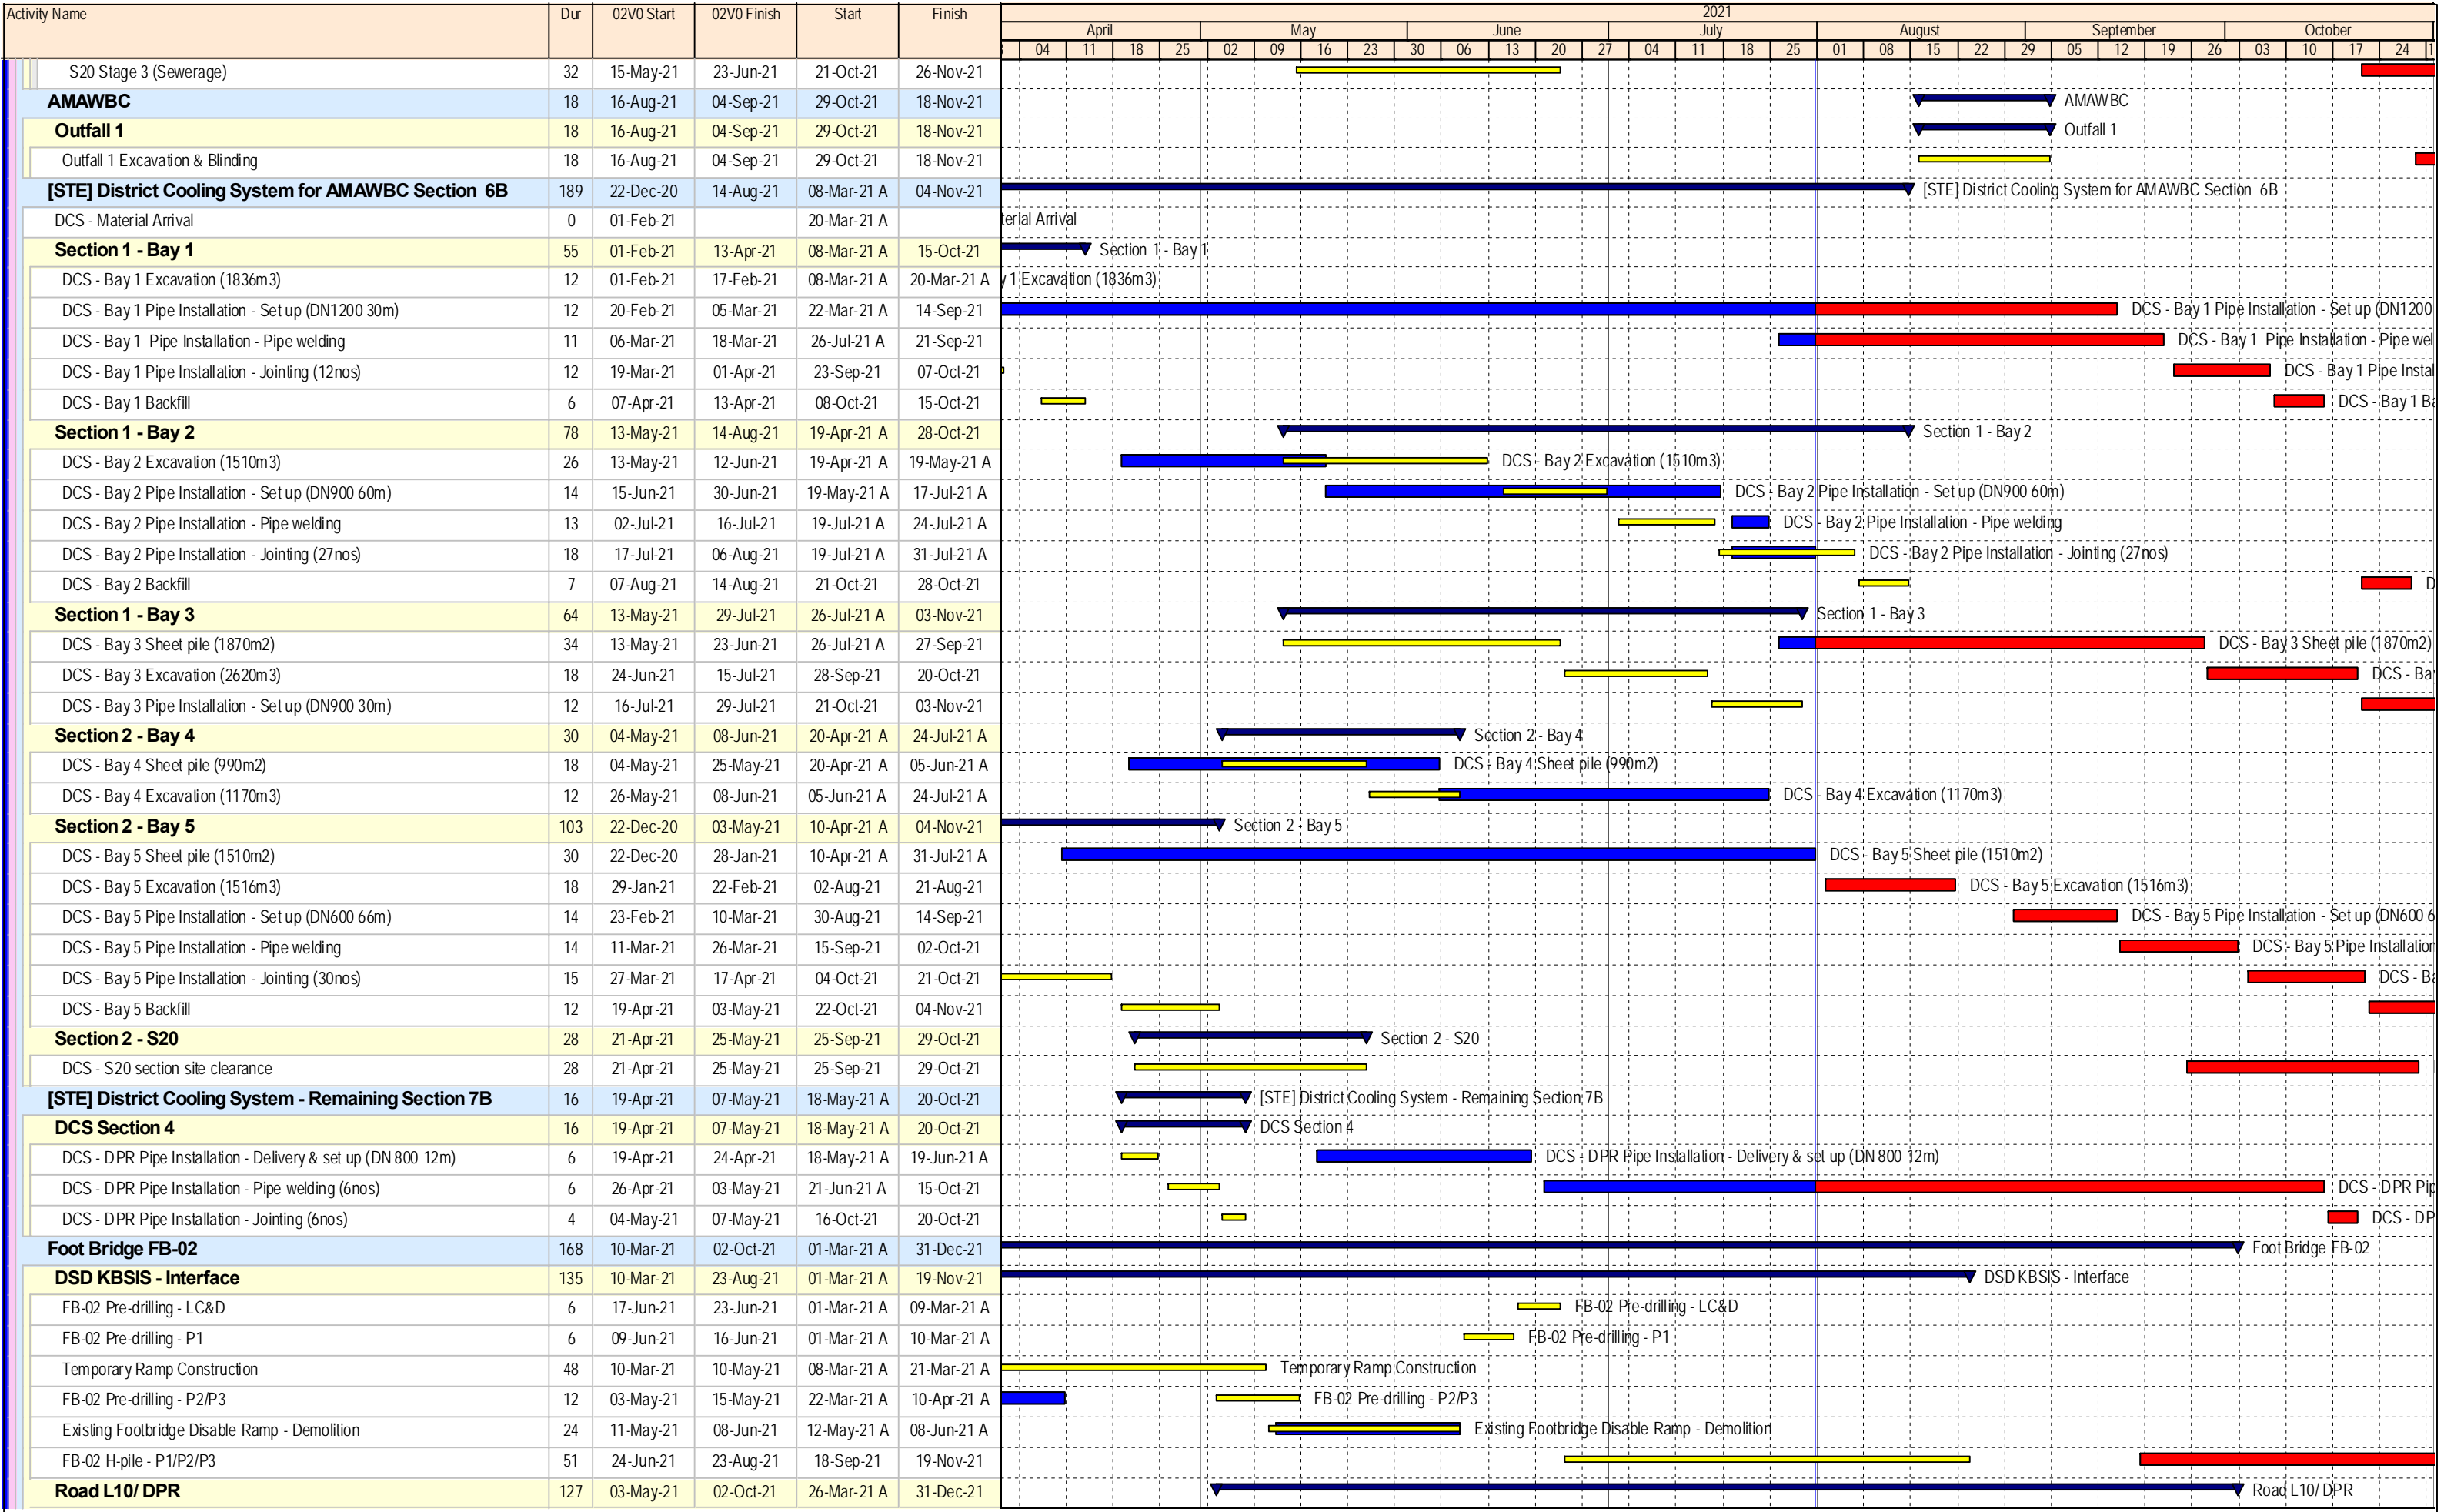


- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- Planned Bar
- Critical Activity
- Actual Work
- Baseline Bar
- ▶ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	WYu
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

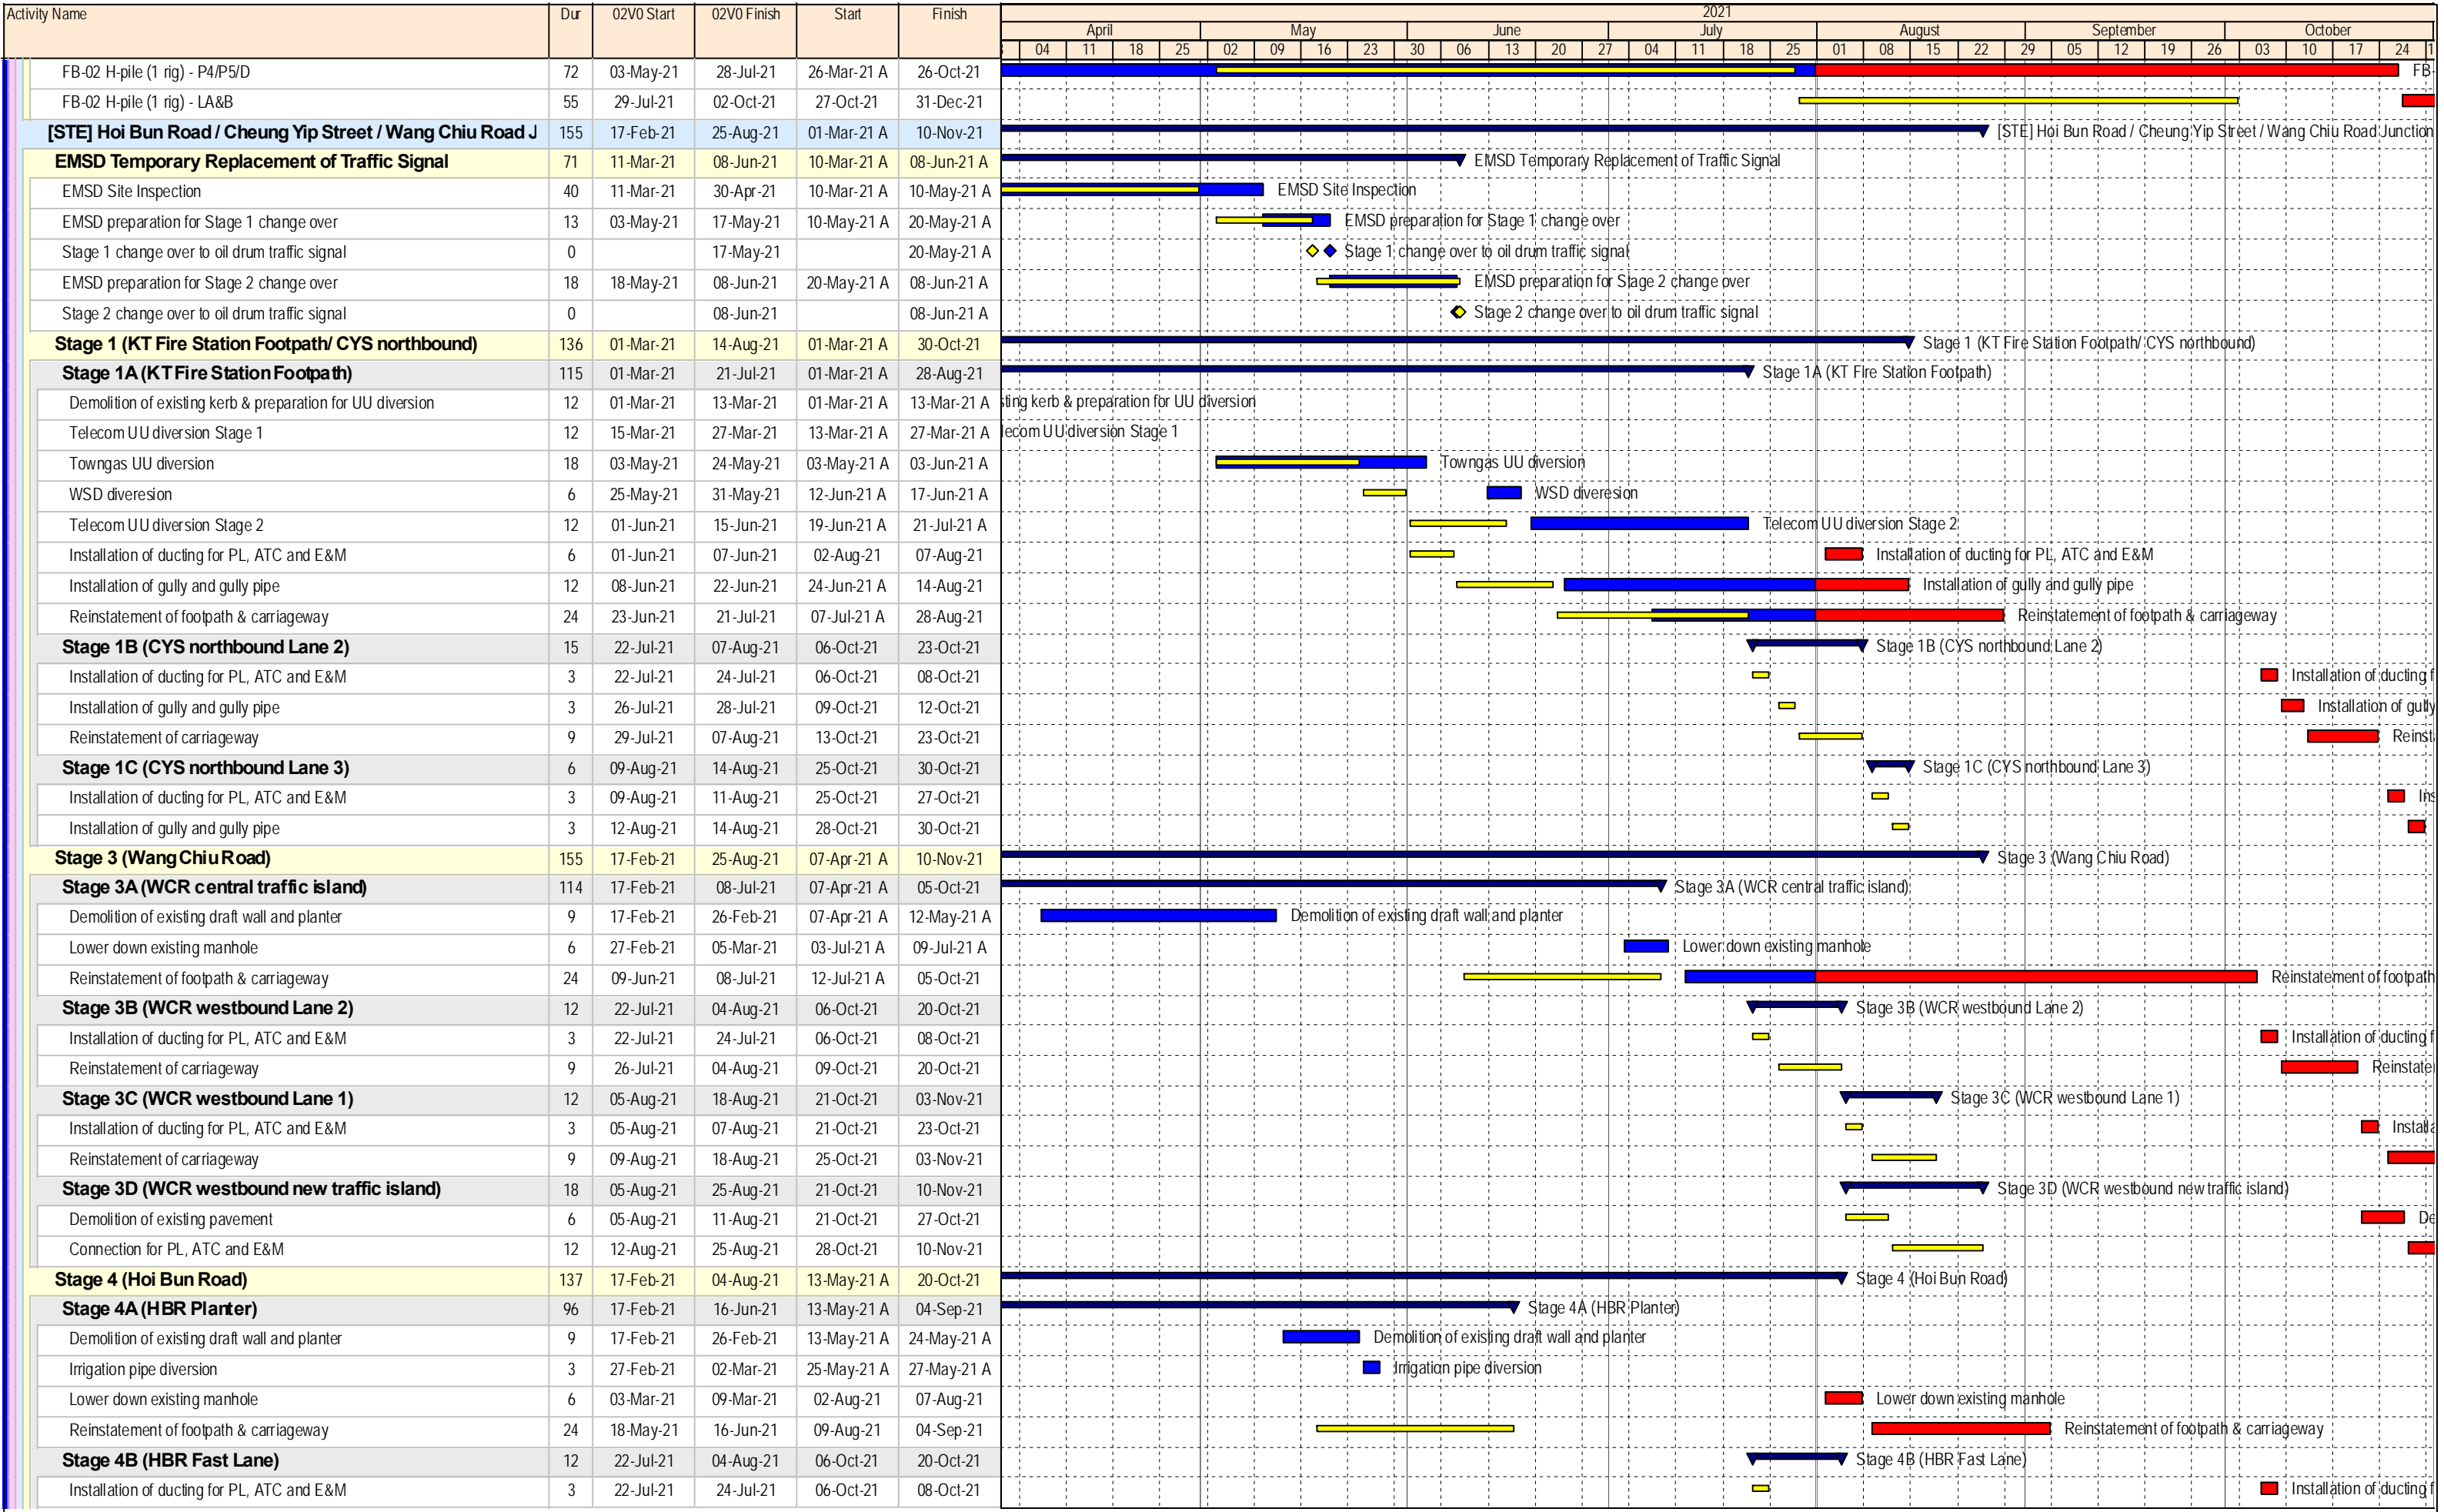


- ◆ Milestone
- ◆ Actual Milestone
- ◆ Baseline Milestone
- Planned Bar
- Critical Activity
- Actual Work
- Baseline Bar
- ▶ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)




Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

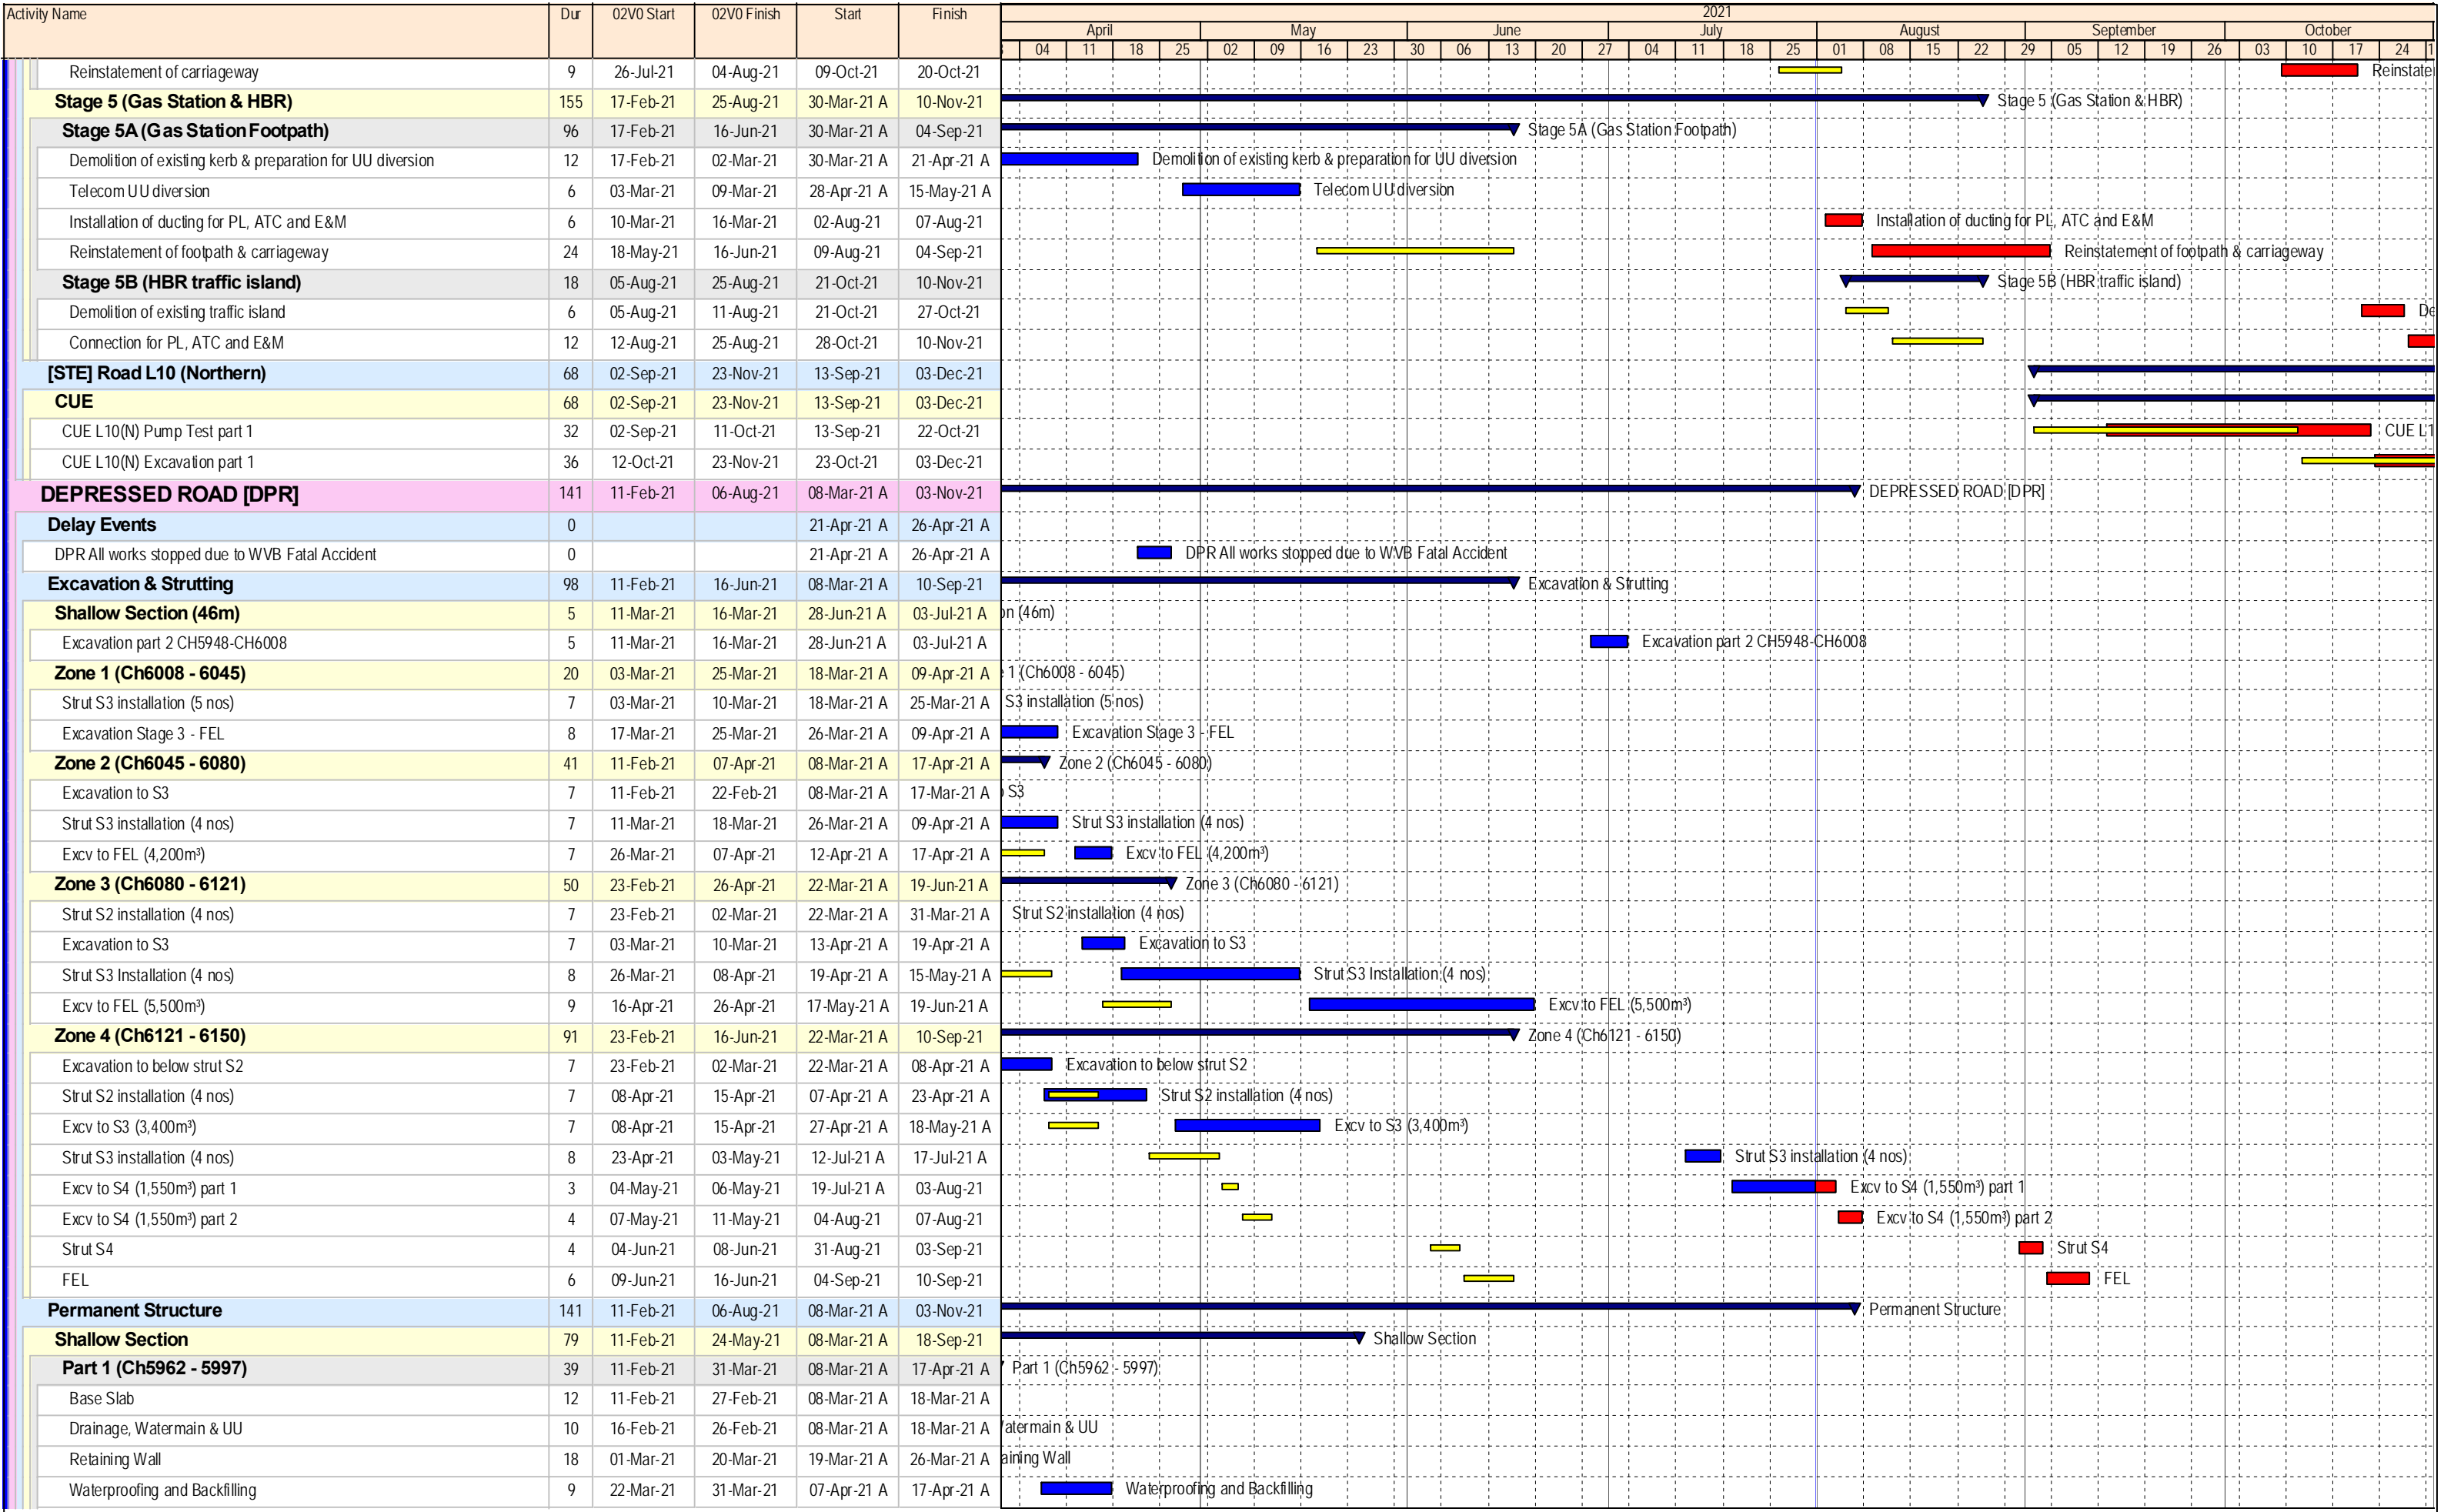


	Milestone		Summary
	Planned Bar		
	Critical Activity		
	Actual Milestone		
	Actual Work		
	Baseline Milestone		
	Baseline Bar		

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPaLLo	WYu
09-Apr-20	01V1	SPaLLo	WYu
17-Jul-20	01V2	SPaLLo	WYu
09-Oct-20	01V3	SPaLLo	WYu
02-Jul-21	02V0	SPaLLo	WYu

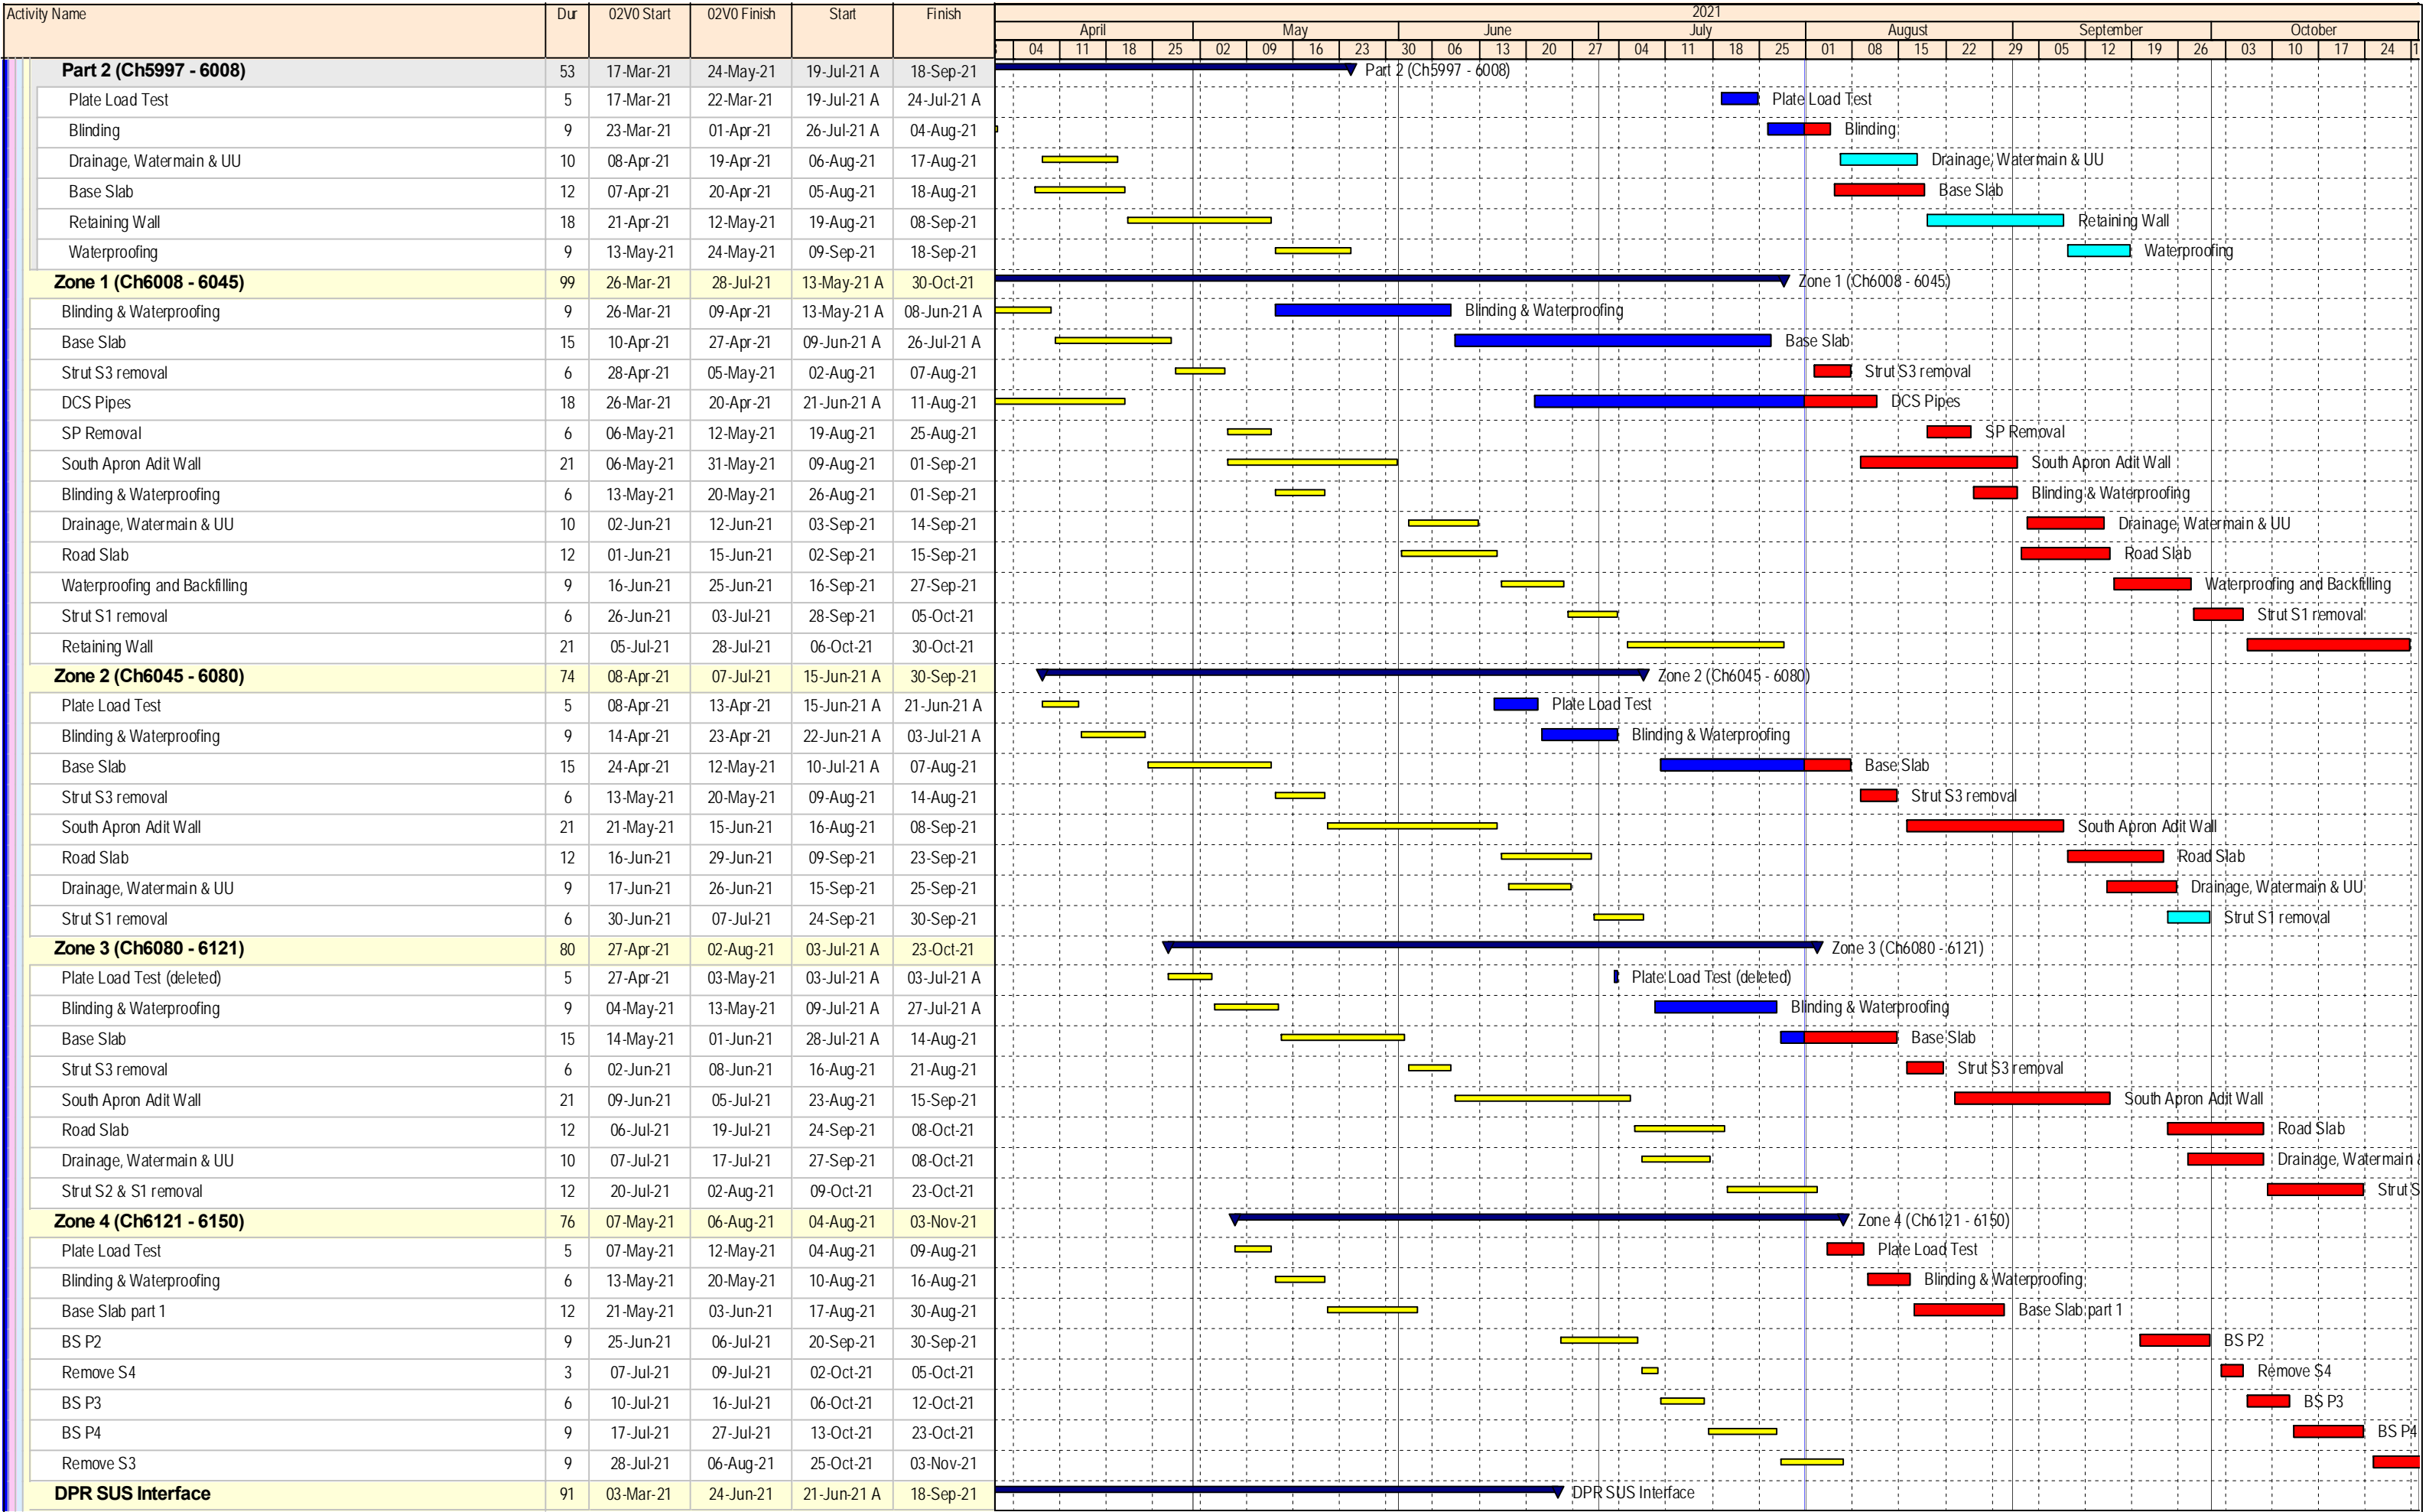


- Milestone
- Planned Bar
- Critical Activity
- Actual Milestone
- Actual Work
- Baseline Milestone
- Baseline Bar
- Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

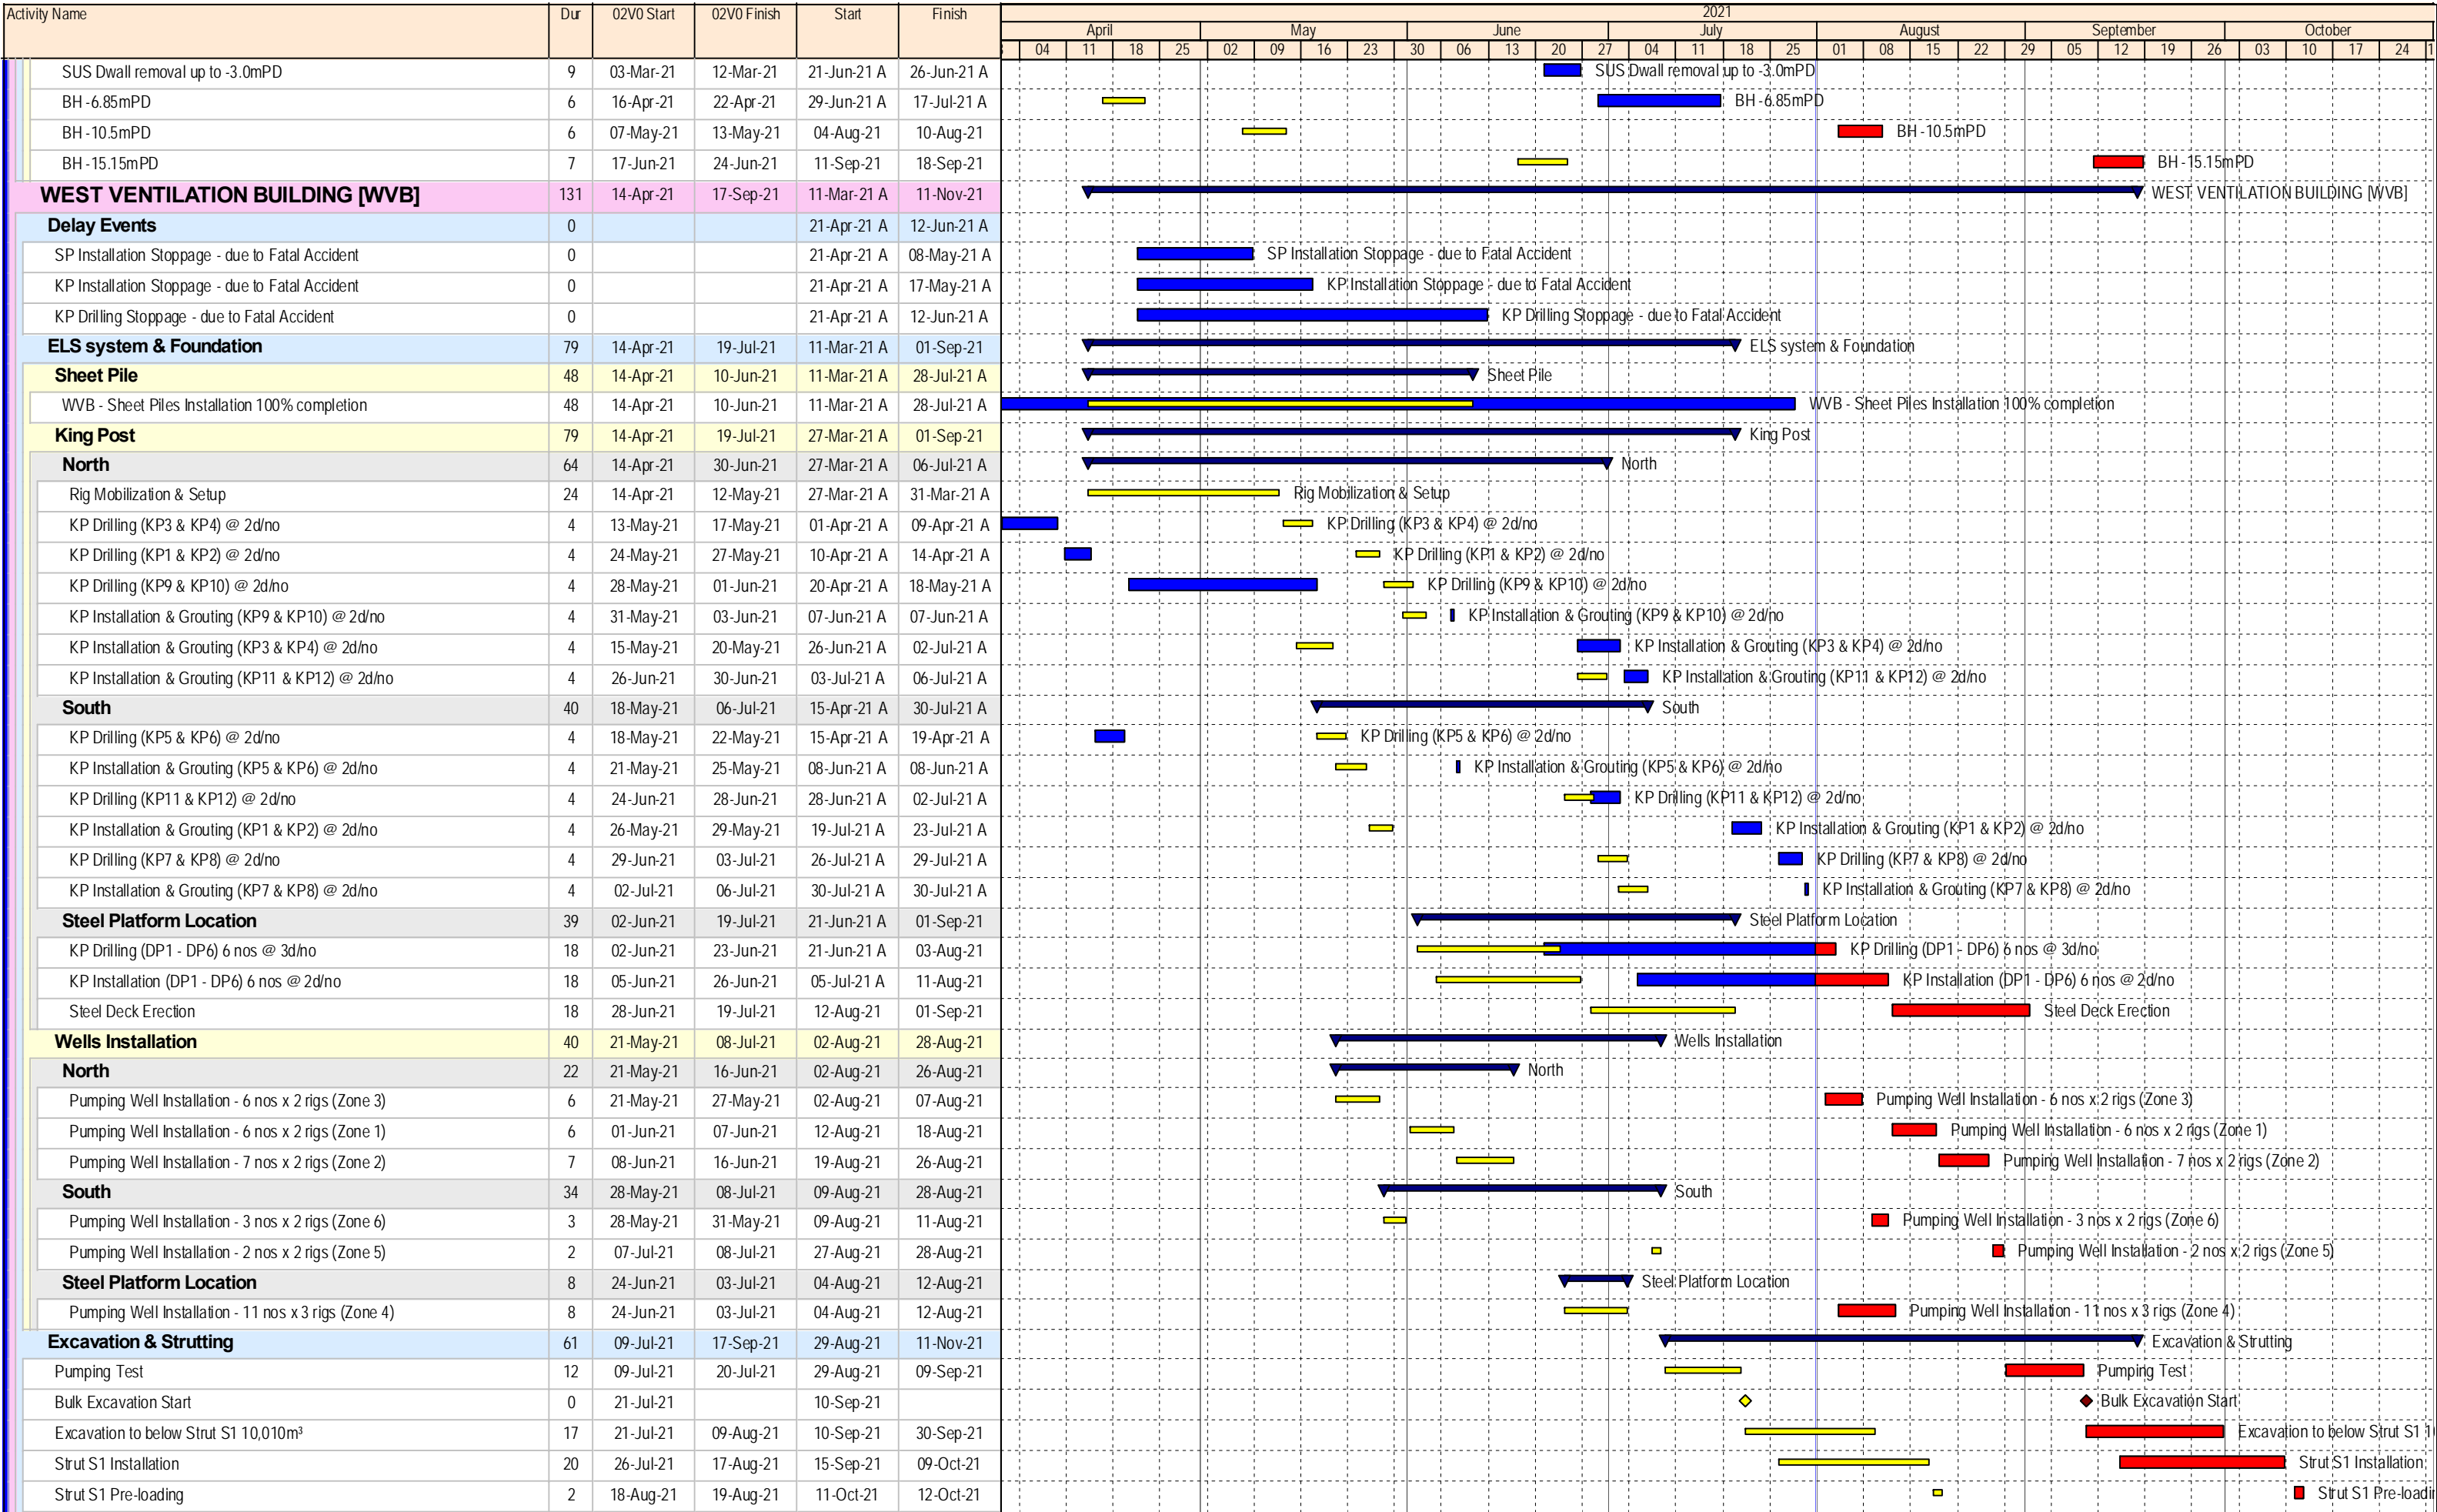


◆ Milestone	◆ Summary
▬ Planned Bar	
▬ Critical Activity	
◆ Actual Milestone	
▬ Actual Work	
◆ Baseline Milestone	
▬ Baseline Bar	


ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/Lo	WYu
09-Apr-20	01V1	SPa/Lo	WYu
17-Jul-20	01V2	SPa/Lo	WYu
09-Oct-20	01V3	SPa/Lo	WYu
02-Jul-21	02V0	SPa/Lo	WYu

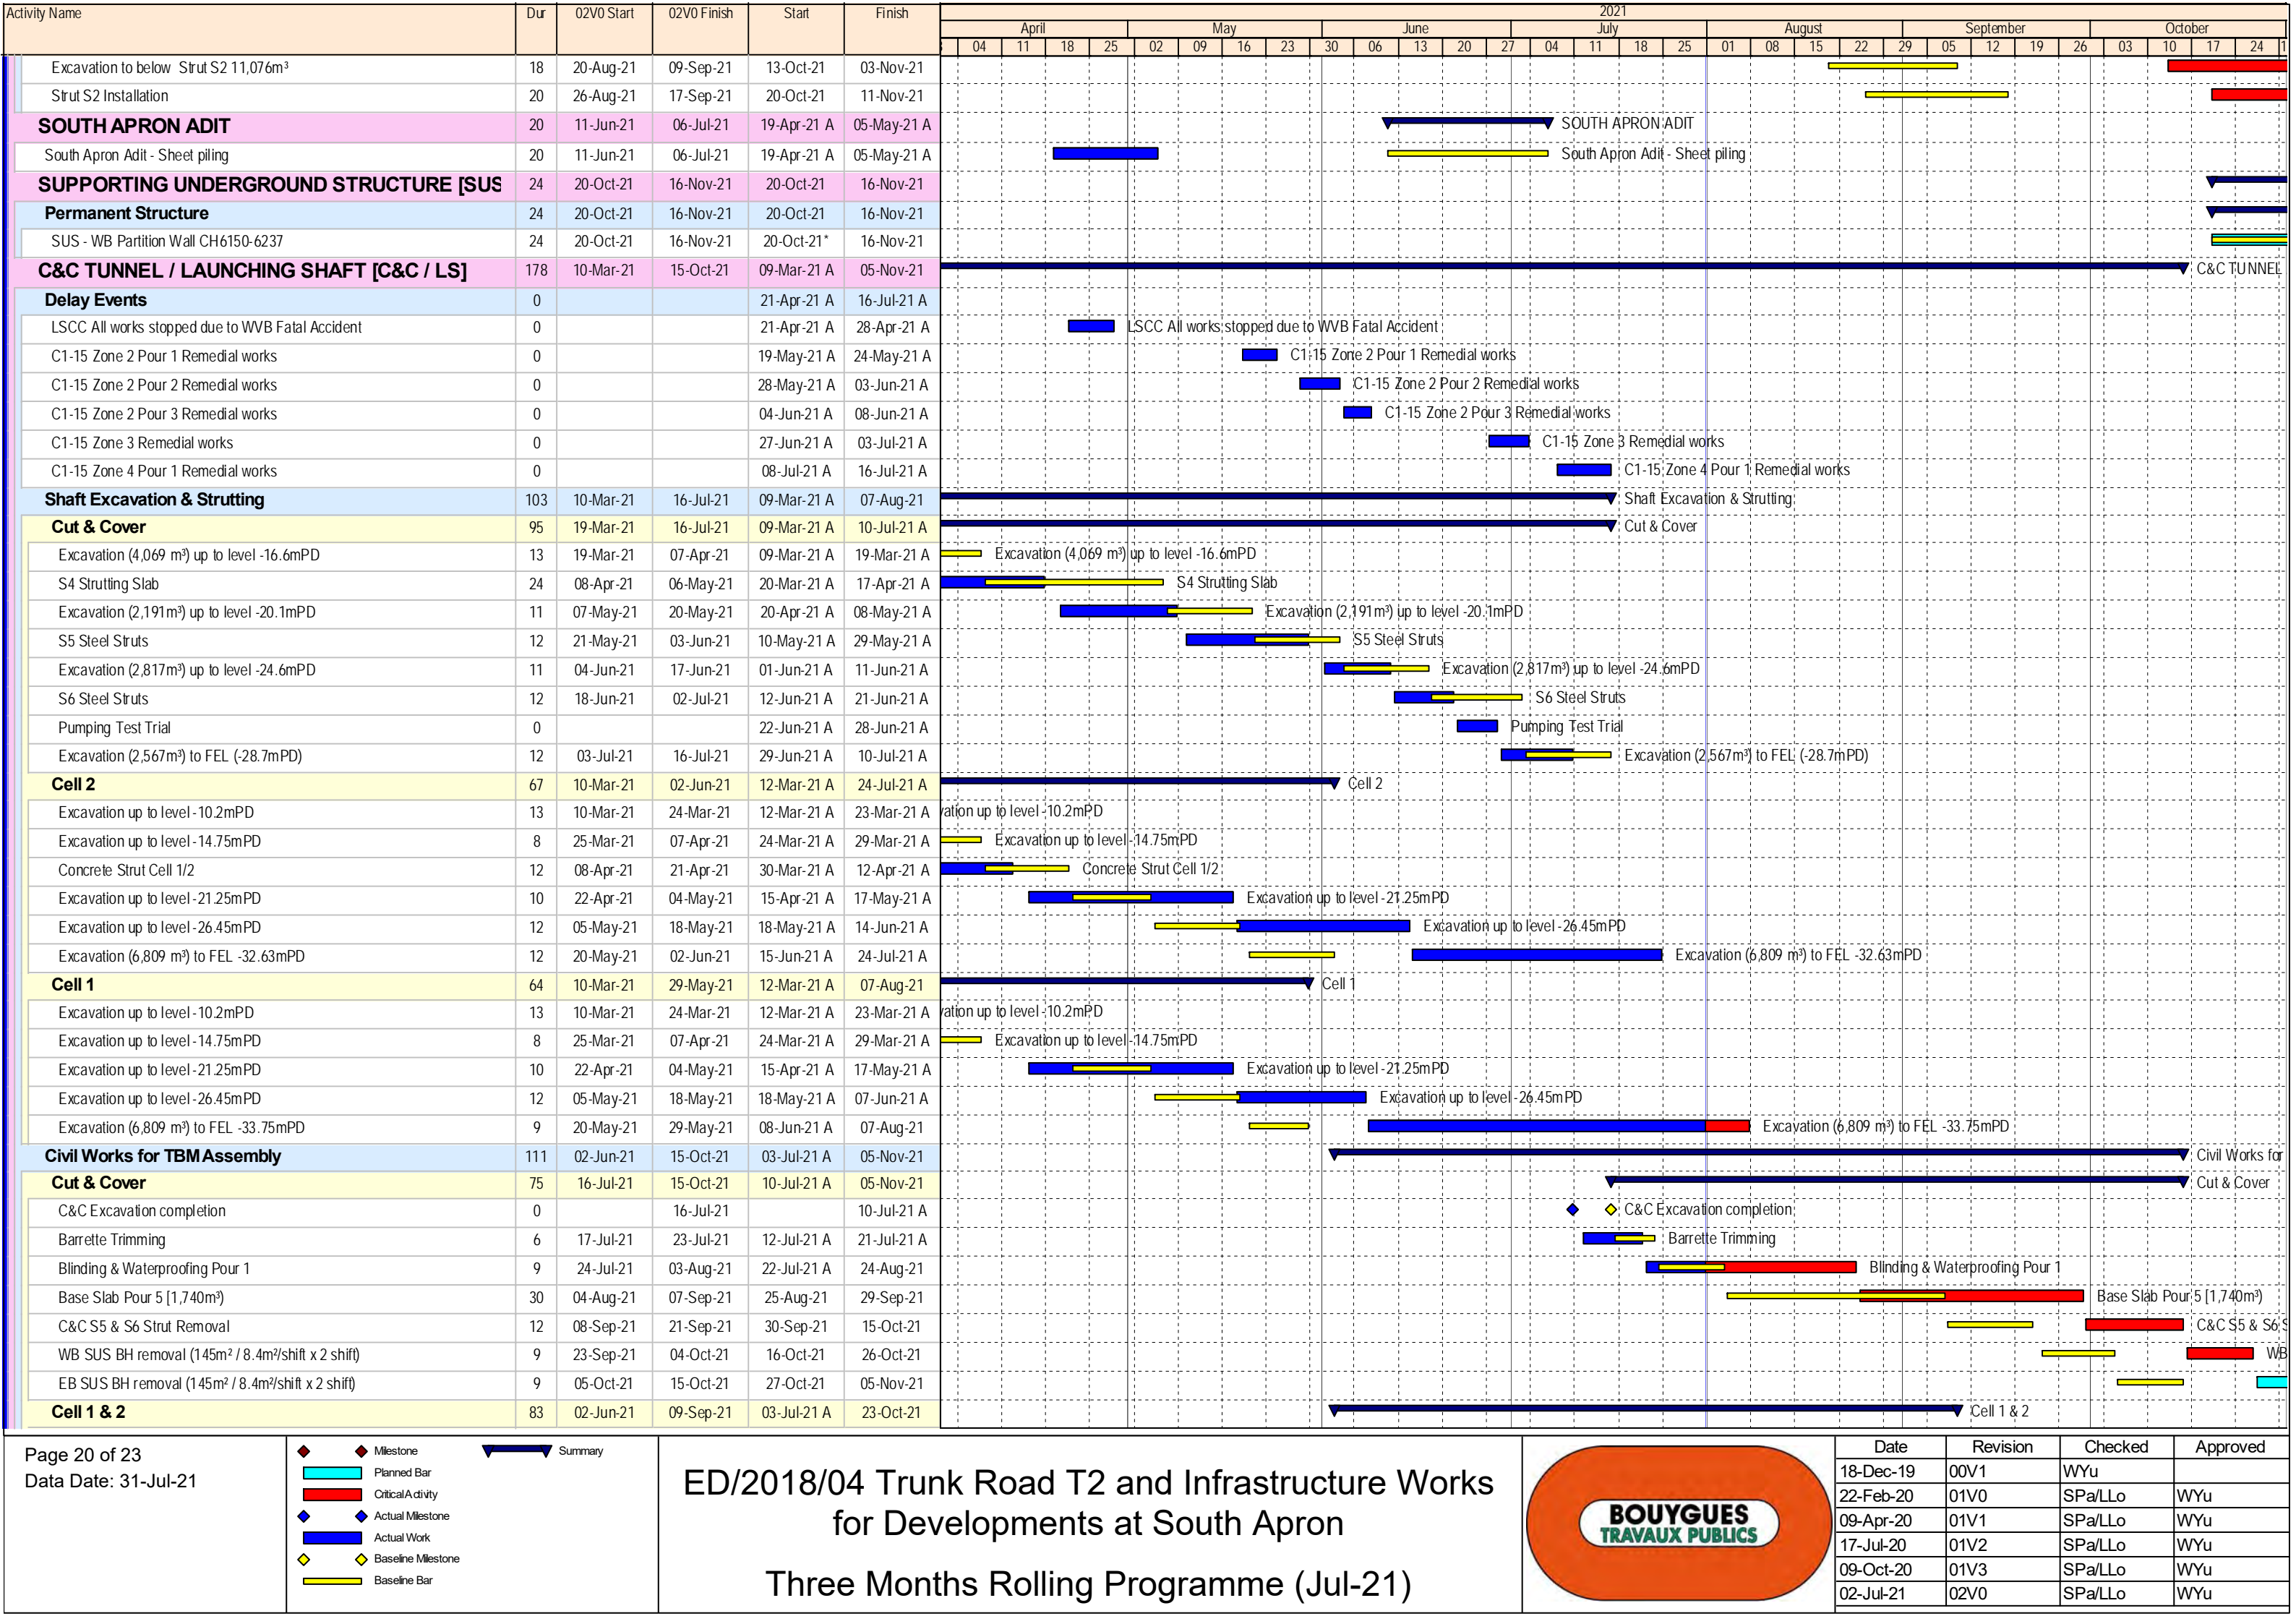

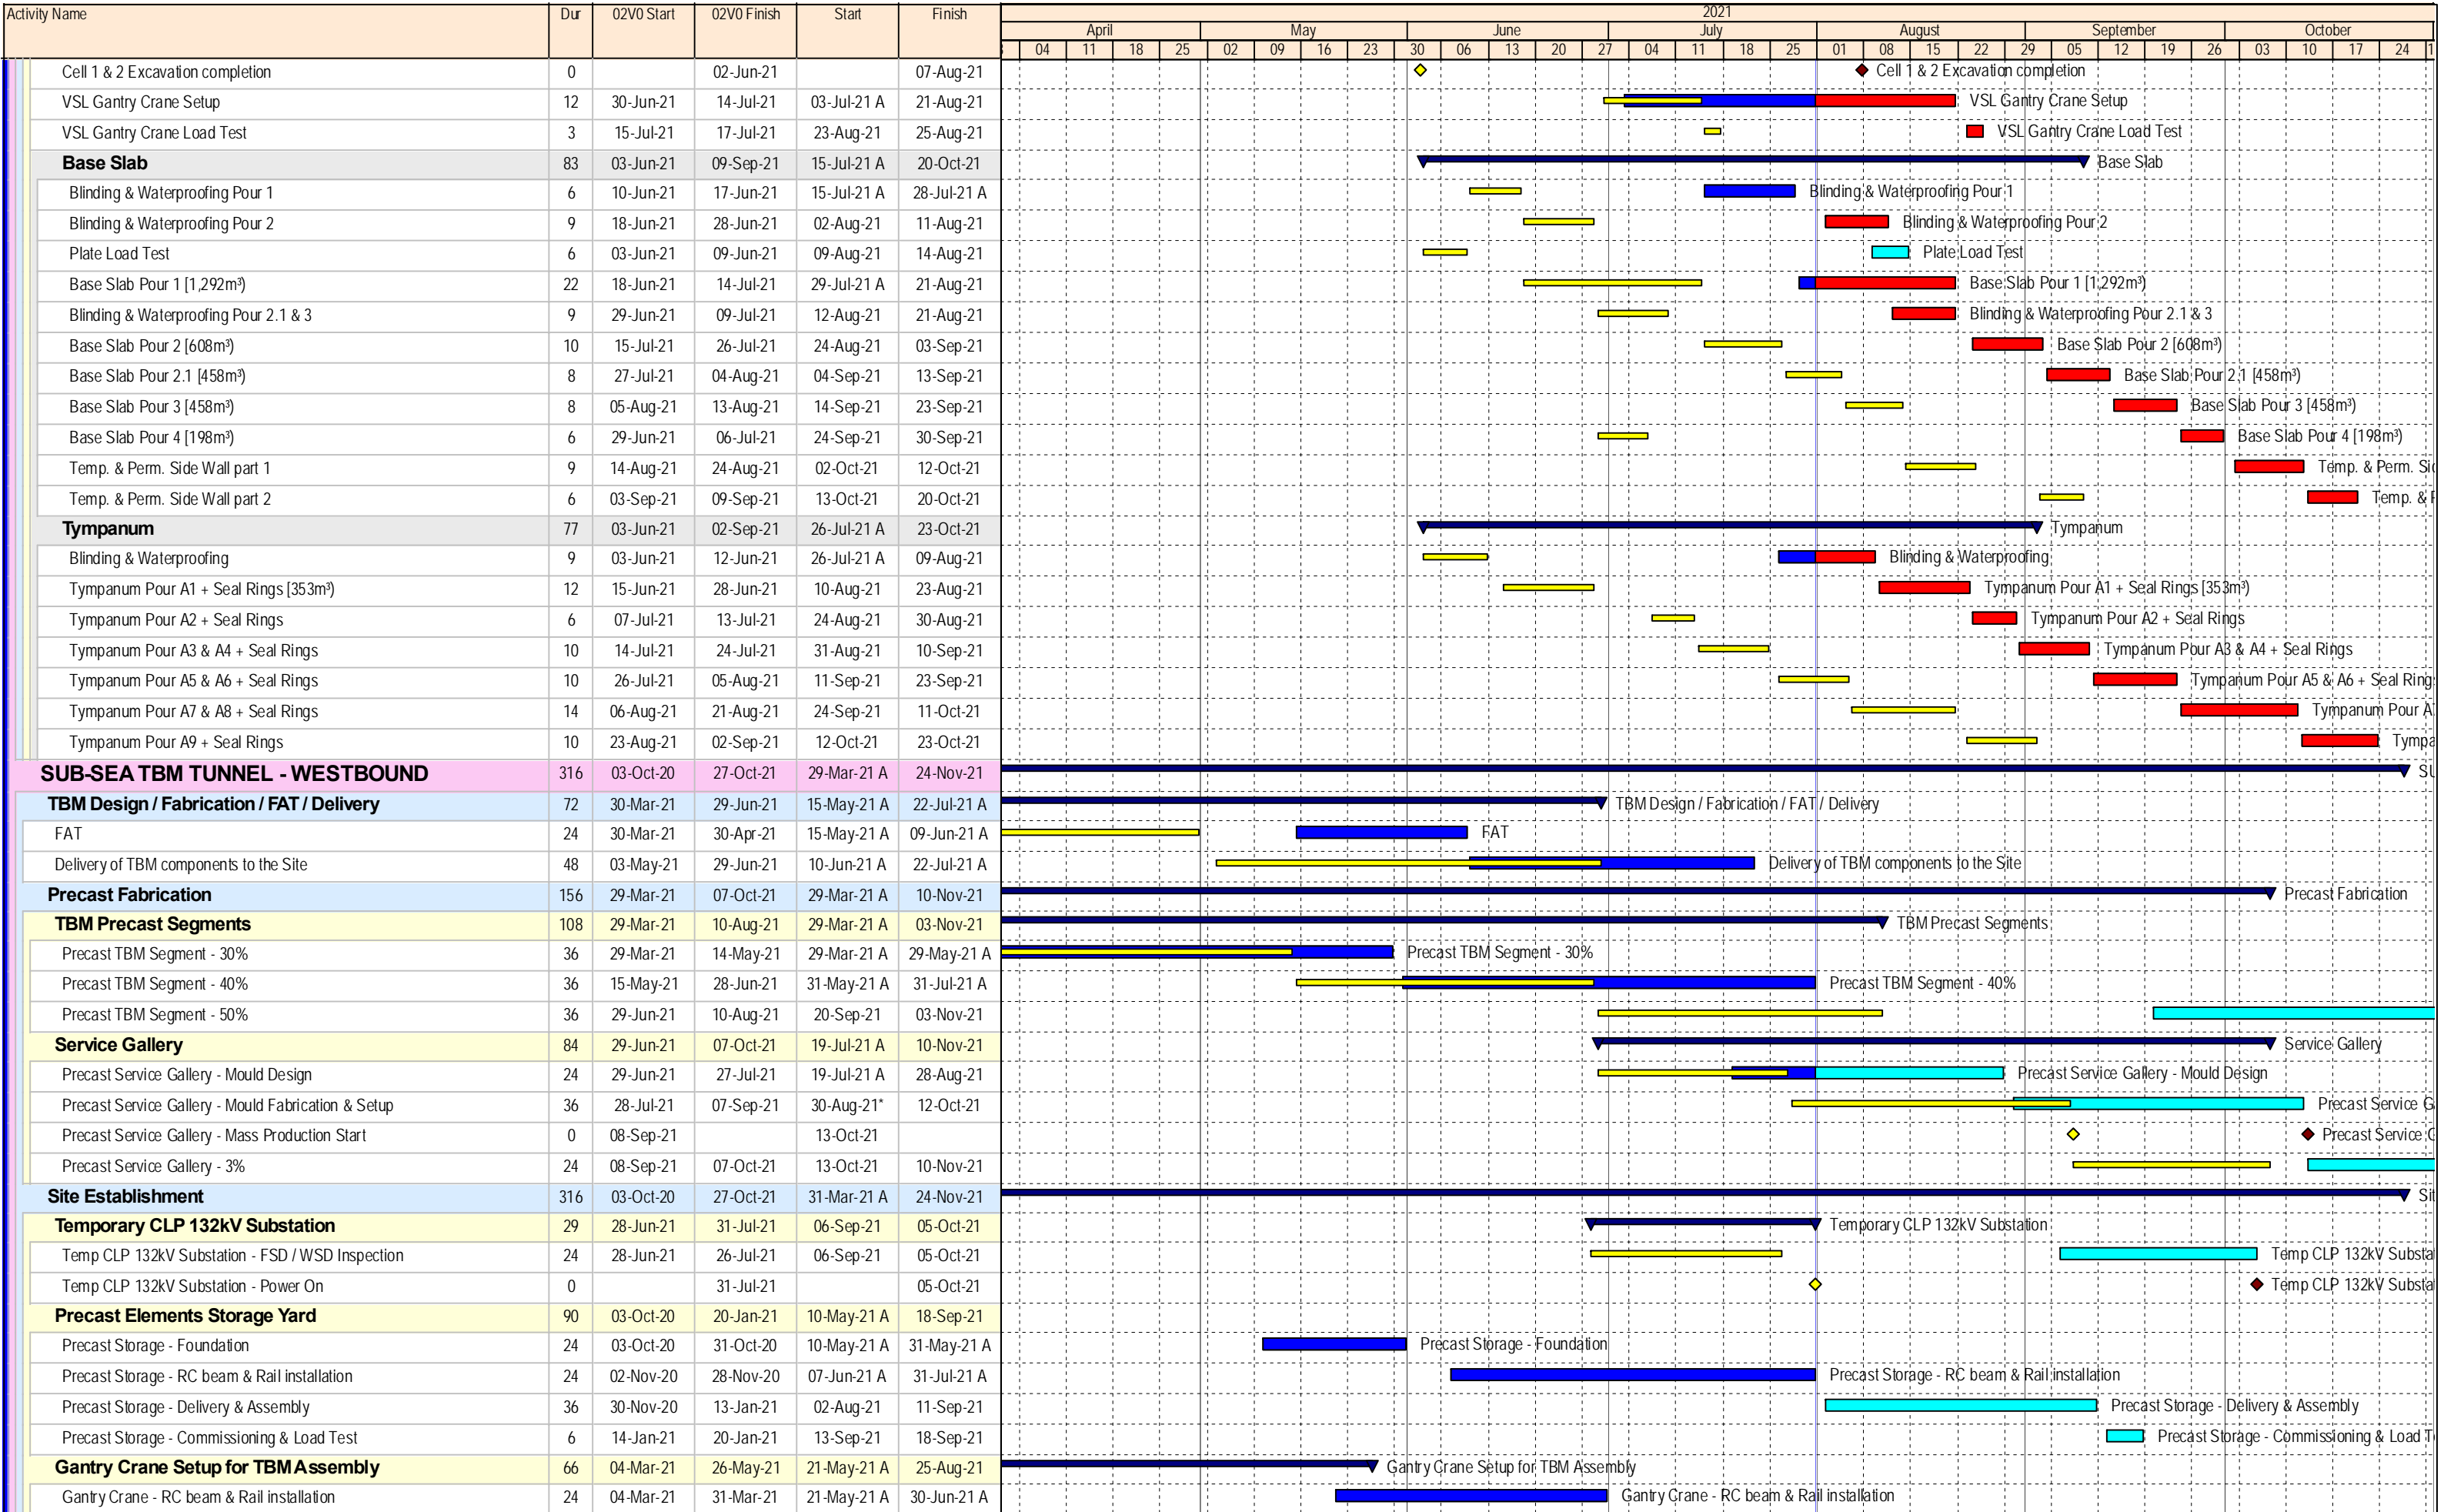


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬▬▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

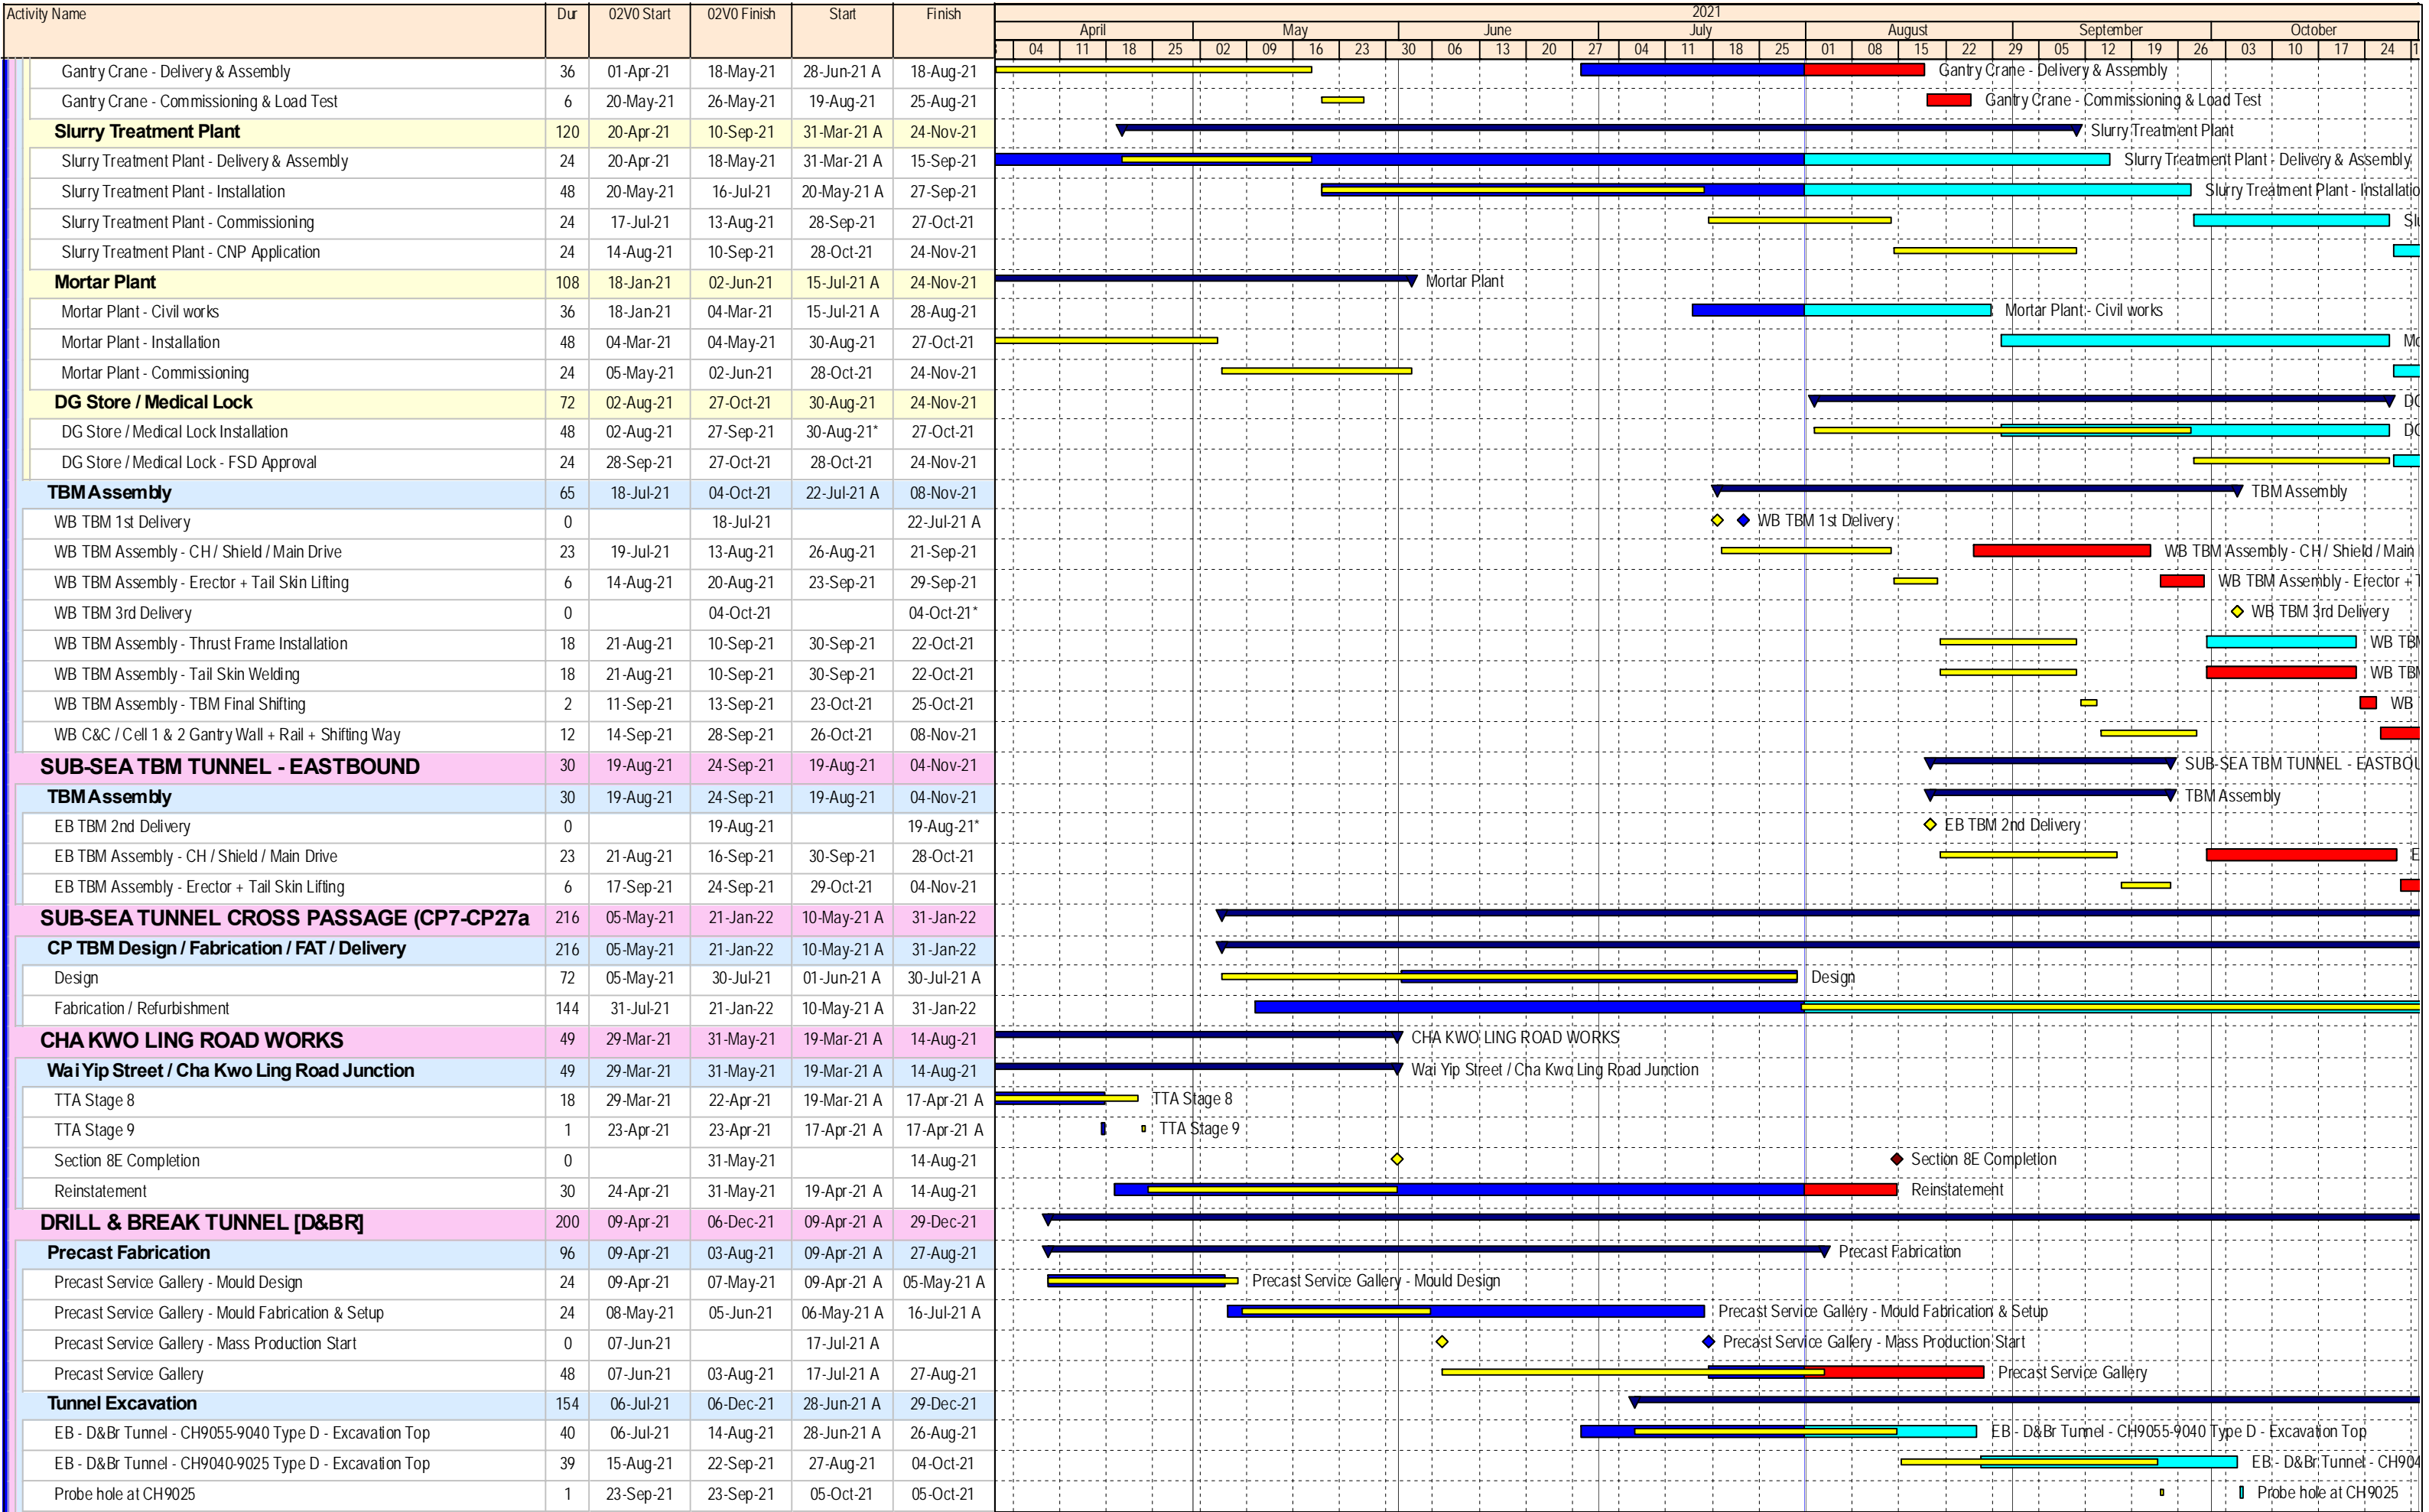


- ◆ Milestone
- ▬ Planned Bar
- ▬ Critical Activity
- ◆ Actual Milestone
- ▬ Actual Work
- ◆ Baseline Milestone
- ▬ Baseline Bar
- ▬ Summary

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu

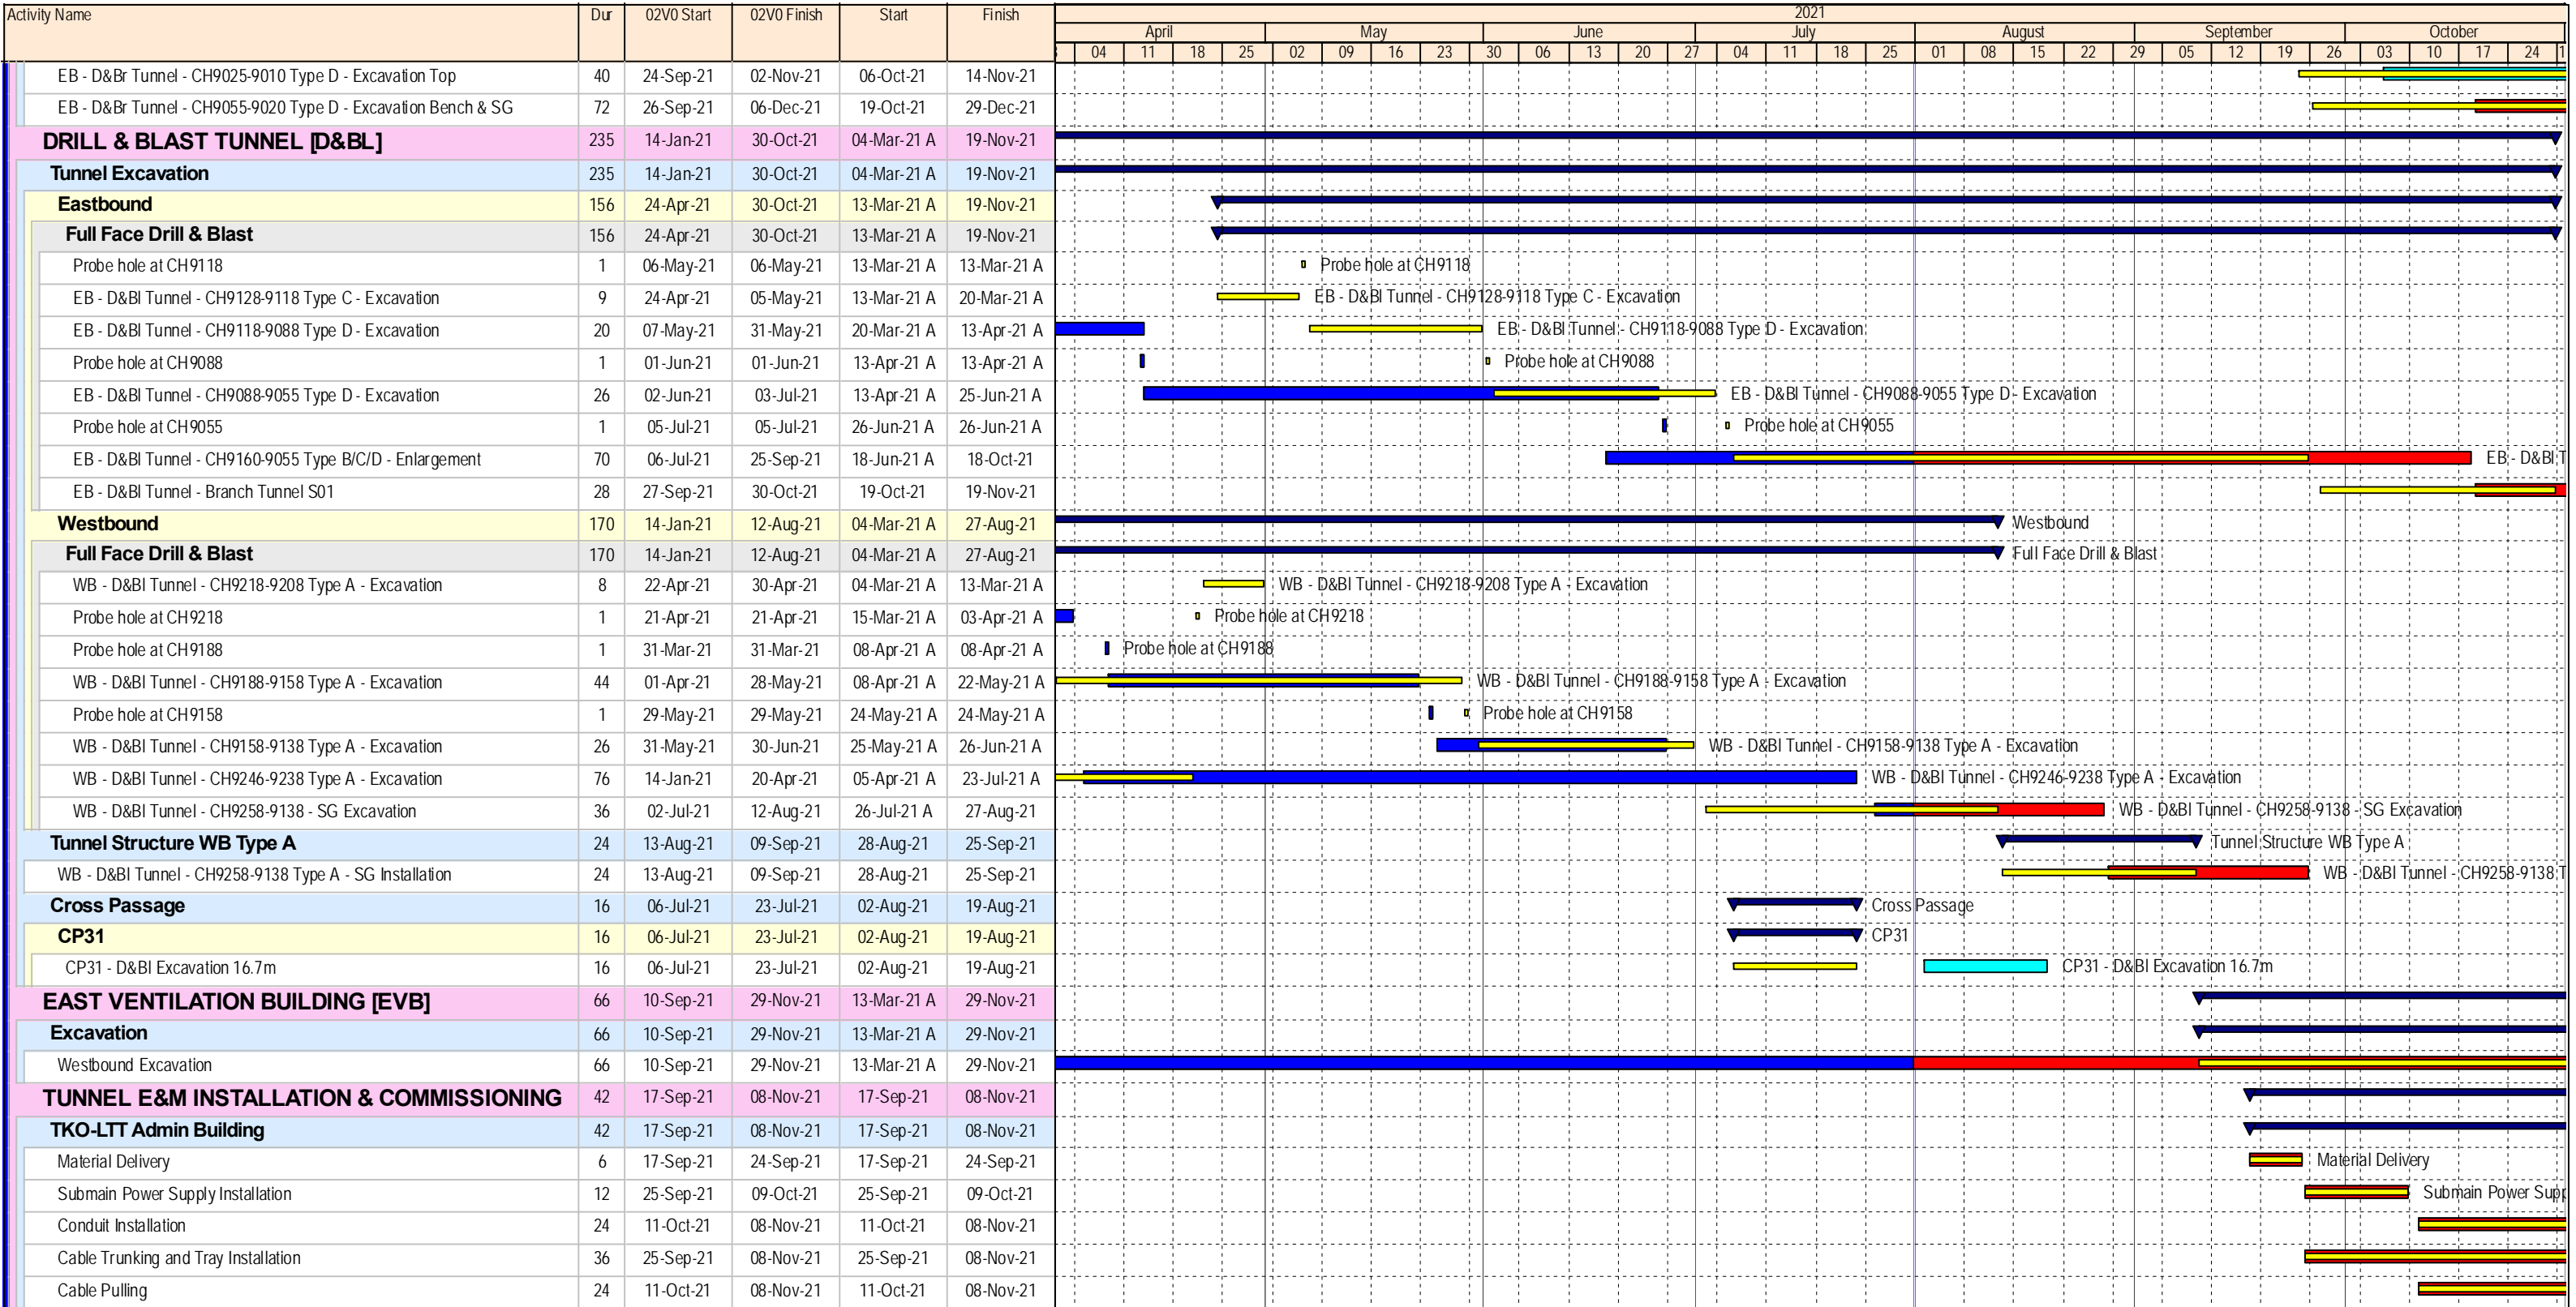

ED/2018/04 Trunk Road T2 and Infrastructure Works for Developments at South Apron

Three Months Rolling Programme (Jul-21)



Date	Revision	Checked	Approved
18-Dec-19	00V1	WYu	
22-Feb-20	01V0	SPa/LLo	WYu
09-Apr-20	01V1	SPa/LLo	WYu
17-Jul-20	01V2	SPa/LLo	WYu
09-Oct-20	01V3	SPa/LLo	WYu
02-Jul-21	02V0	SPa/LLo	WYu
