
































Activity ID	Activity Name	Dur	Start	Finish	2026		
					Feb	Mar	Apr
HKT2 Revised Accelerated Programme DD 31Jan26							
Construction							
Trunk Road T2							
02 At-Grade Road - AGR							
Kiosk							
AGR1090	Kiosk - E&M + T&C	31	13-Jan-26 A	12-Feb-26	Kiosk - E&M + T&C		
AGR1100	Kiosk - TCSS	30	13-Feb-26	14-Mar-26	Kiosk - TCSS		
AGR1110	Kiosk - Reday for FSI	6	15-Mar-26	20-Mar-26*	Kiosk - Reday for FSI		
AGR - Road & Drainage works							
AGR1170	AGR - Remaining Works after Breakthrough	30	15-Feb-26	16-Mar-26	AGR - Remaining Works after Breakthrough		
03 Depressed Road - DPR							
DPR - Road Works							
Rising Main							
A229450170	DPR - Civil - Perm civil provision (sump pit)	124	01-Oct-25 A	01-Feb-26	DPR - Civil - Perm civil provision (sump pit)		
A229426391	DPR - E&M - Sump pit pumps and watermain installation (remainir	129	24-Nov-25 A	02-Apr-26	DPR - E&M - Sump pit pumps and watermain installation (remainir		
A229450390	DPR - Civil - Remaining Civil Works	30	02-Apr-26	02-May-26			
06 Launching Shaft & C&C Tunnel - LSCC							
LSCC - Backfilling & Dwall Dismantling							
A229447780	D-wall dismantling at LCS side (from +1.0mPD to +4.0mPD) TBC	45	15-Feb-26	31-Mar-26	D-wall dismantling at LCS side (from +1.0mPD to +4.0mPD) TBC		
A229447781	D-wall dismantling (from +1.0mPD to +4.0mPD) ~3050 m3 TBC	38	01-Apr-26	08-May-26			
07 Tunnel Sub-sea (TSS)							
TSS - TBM Excavation from Kai Tak							
Eastbound - TBM S1282							
TBM2 Tunneling							
CP26-30							
EBTBM1320	EB TBM Tunnelling Cavern section CH8900-8977 (Pilot tunnel sec	30	16-Jan-26 A	14-Feb-26	EB TBM Tunnelling Cavern section CH8900-8977 (Pilot tunnel section) (77m; 8.5R/wk)		
TA010	EB TSS - TBM Tunneling Break-out	0		14-Feb-26	EB TSS - TBM Tunneling Break-out		
TBM2 Rescue							
Seawall Reinstatement							
A229450950	Phase 1 (Bay 11 to Bay 13) Seawall Reinstatement	106	25-Oct-25 A	08-Feb-26	Phase 1 (Bay 11 to Bay 13) Seawall Reinstatement		
A229450960	Phase 2 (Bay 9 to Bay 10) Seawall Reinstatement	128	17-Nov-25 A	24-Mar-26	Phase 2 (Bay 9 to Bay 10) Seawall Reinstatement		
A229450970	Phase 3 (Bay 6 to Bay 8) Seawall Reinstatement	68	16-Jan-26 A	24-Mar-26	Phase 3 (Bay 6 to Bay 8) Seawall Reinstatement		
A229451010	Phase 4 (Bay 1 to Bay 3) Seawall Reinstatement	53	15-Feb-26*	08-Apr-26	Phase 4 (Bay 1 to Bay 3) Seawall Reinstatement		
A229451020	Phase 5 (Bay 4 to Bay 5) Seawall Reinstatement	53	17-Mar-26*	08-May-26			
A229451030	Final Works	158	17-Mar-26*	21-Aug-26			
TBM2 Dismantling							
TBM2 Dismantling Summary							
TSS							
TA040	EB TBM dismantling - TSS side	69	15-Feb-26	24-Apr-26	EB TBM dismantling - TSS side		
TA1601	EB Resume Service Gallery Installation	58	15-Feb-26	13-Apr-26	EB Resume Service Gallery Installation		
CKL							
TA1231	Summary - EB TBM dismantling - CKL side	108	15-Feb-26	02-Jun-26			
TSS side							
TA020	EB TBM - Last 6 Rings Installation	6	15-Feb-26	20-Feb-26	EB TBM - Last 6 Rings Installation		
TA1661	Last ring securing + Tailskin Cutting + Erector Prep	7	21-Feb-26	27-Feb-26	Last ring securing + Tailskin Cutting + Erector Prep		
TSS side - breakdown							
Backup Gantries							
TA1671	Gantry 4 Dismantling	13	21-Feb-26	05-Mar-26	Gantry 4 Dismantling		
TA1681	G1 / Erector Disconnection + Gantries Pulling	2	06-Mar-26	07-Mar-26	G1 / Erector Disconnection + Gantries Pulling		
TA1711	Gantry 1-3 + Boggies Dismantling	30	08-Mar-26	06-Apr-26	Gantry 1-3 + Boggies Dismantling		



Activity ID	Activity Name	Dur	Start	Finish	2026		
					Feb	Mar	Apr
TA1721	Oxycut Platform Demobilisation	7	07-Apr-26	13-Apr-26			 Oxycut Platform Demobilisation
TA1901	Pulling Chair Demobilisation	6	14-Apr-26	19-Apr-26			 Pulling Chair Demobilisation
Erector / XB / MD		48	08-Mar-26	24-Apr-26			
TA1731	Concrete Slab + HAG System Erection	12	08-Mar-26	19-Mar-26		Concrete Slab + HAG System Erection	
TA1741	Erector Extraction	5	20-Mar-26	24-Mar-26		 Erector Extraction	
TA1751	Erector Dismantling	7	25-Mar-26	31-Mar-26		 Erector Dismantling	
TA1761	X Beam Extraction	6	25-Mar-26	30-Mar-26		 X Beam Extraction	
TA1771	X Beam Dismantling	18	31-Mar-26	17-Apr-26		 X Beam Dismantling	
TA1781	Main Drive Extraction	12	31-Mar-26	11-Apr-26		 Main Drive Extraction	
TA1791	Main Drive Dismantling	6	12-Apr-26	17-Apr-26		 Main Drive Dismantling	
TA1801	Concrete Slab + HAG System Demo	7	18-Apr-26	24-Apr-26		 Concrete S	
CKL Side		72	21-Feb-26	03-May-26			
CKL side - breakdown		72	21-Feb-26	03-May-26			
Cutterhead		40	21-Feb-26	01-Apr-26			
TA1811	CKL Civil Works #1 (Leveling Grout & Sliding Plate, Sliding Rails, l	21	21-Feb-26	13-Mar-26		CKL Civil Works #1 (Leveling Grout & Sliding Plate, Sliding Rails, Levelling Concrete & TBM Feet)	
TA1821	Cutterhead dismantling Part 1 & Rotation	9	14-Mar-26	22-Mar-26		 Cutterhead dismantling Part 1 & Rotation	
TA1831	Cutterhead dismantling Part 2	10	23-Mar-26	01-Apr-26		 Cutterhead dismantling Part 2	
Spherical Bearing		13	02-Apr-26	14-Apr-26			
TA1841	CKL Civil Works #2 (Stage 1 Perm/Temp Massfill, Install Concrete	9	02-Apr-26	10-Apr-26		 CKL Civil Works #2 (Stage 1 Perm/Temp Mass	
TA1851	Spherical Bearing	3	12-Apr-26	14-Apr-26		 Spherical Bearing	
Shield		19	15-Apr-26	03-May-26			
TA1891	CKL Civil Works #3 (Remove Dismantling Setup/Devices)	4	15-Apr-26	18-Apr-26		 CKL Civil Works #3 (Remo	
TA1871	Inner Shield Dismantling	15	19-Apr-26	03-May-26			
TSS - Tunnel Civil Works		526	17-Feb-25 A	27-Jul-26			
Westbound (WB)		301	02-Jul-25 A	29-Apr-26			
WB TSS Remaining Civil Works Summary		93	03-Jan-26 A	06-Apr-26			
TA105	WB TBM dismantling - TSS Remaining Civil Works	93	03-Jan-26 A	06-Apr-26		WB TBM dismantling - TSS Remaining Civil Works	
WB TSS - Service Gallery		10	26-Jan-26 A	04-Feb-26			
ISIG Dismantling & Last Galleries		10	26-Jan-26 A	04-Feb-26			
TC3070	WB TSS - 17 SG by Overhead rail & 4 by Sliding (R1115 to R1135	10	26-Jan-26 A	04-Feb-26		WB TSS - 17 SG by Overhead rail & 4 by Sliding (R1115 to R1135) + Concreting	
WB TSS - Corbel		84	01-Dec-25 A	23-Feb-26			
Corbel Construction After TBM1 Dismantling		84	01-Dec-25 A	23-Feb-26			
TC1960	WB TSS Final - Corbel Structure from R1032 to R1108	67	01-Dec-25 A	06-Feb-26		WB TSS Final - Corbel Structure from R1032 to R1108	
TC1970	WB TSS - Corbel Structure from R1109 to R1135 (up to end wall)	10	06-Feb-26	16-Feb-26		WB TSS - Corbel Structure from R1109 to R1135 (up to end wall)	
Concrete curing		17	06-Feb-26	23-Feb-26			
TC1350	WB TSS Final - Corbel Structure from R1032 to R1108 (concrete c	7	06-Feb-26	13-Feb-26		WB TSS Final - Corbel Structure from R1032 to R1108 (concrete curing)	
TC1660	WB TSS - Corbel Structure from R1109 to R1135 (up to end wall)	7	16-Feb-26	23-Feb-26		WB TSS - Corbel Structure from R1109 to R1135 (up to end wall) (concrete curing)	
Monorail Removal		7	04-Feb-26	11-Feb-26			
TC1090	WB TSS - Monorail Removal for final dismantling	7	04-Feb-26	11-Feb-26		WB TSS - Monorail Removal for final dismantling	
ISCG Dismantling		7	16-Feb-26	23-Feb-26			
TC1980	WB TSS - Corbel Gantry & Formwork dismantling	7	16-Feb-26	23-Feb-26		WB TSS - Corbel Gantry & Formwork dismantling	
WB TSS - OHVD		61	06-Feb-26	08-Apr-26			
OHVD installation After TBM1 Dismantling		34	06-Feb-26	12-Mar-26			
TC1190	WB TSS Final - OHVD from R1020 to R1096 (CP30.5)	26	06-Feb-26	04-Mar-26		WB TSS Final - OHVD from R1020 to R1096 (CP30.5)	
TC1200	WB TSS Final - OHVD from R1097 to R1119 (CP31)	8	04-Mar-26	12-Mar-26		WB TSS Final - OHVD from R1097 to R1119 (CP31)	
ISSG Dismantling & Final OHVDs		27	12-Mar-26	08-Apr-26			
TC970	WB - ISSG Dismantling	7	12-Mar-26	19-Mar-26		WB - ISSG Dismantling	
TC1230	WB TSS - OHVD Lifting Batch 1-3	14	19-Mar-26	02-Apr-26		WB TSS - OHVD Lifting Batch 1-3	
TC11530	WB TSS - Final Lifting & Cast in-situ OHVD	6	02-Apr-26	08-Apr-26		WB TSS - Final Lifting & Cast in-situ OHVD	
WB TSS - Fire Board - Road level with deletion up Ch8924		61	31-Jan-26	02-Apr-26			
After TBM1 Dismantling		61	31-Jan-26	02-Apr-26			

- ◆ ◆ Milestones
-  Planned Bar
-  Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Feb26-Apr26)



Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish	2026		
					Feb	Mar	Apr
TC11440	WB TSS - Fire Board - Walls & OHVD soffit - from CP26 to CP27	14	31-Jan-26	13-Feb-26	WB TSS - Fire Board - Walls & OHVD soffit - from CP26 to CP27		
TC11450	WB TSS - Fire Board - Walls & OHVD soffit - from CP27 to CP28	14	14-Feb-26	27-Feb-26	WB TSS - Fire Board - Walls & OHVD soffit - from CP27 to CP28		
TC1000	WB TSS - Fire Board - Walls & OHVD soffit - from CP28 to CP29	14	04-Mar-26	18-Mar-26	WB TSS - Fire Board - Walls & OHVD soffit - from CP28 to CP29		
TC1020	WB TSS - Fire Board - Walls & OHVD soffit - up to CH8924	7	18-Mar-26	25-Mar-26	WB TSS - Fire Board - Walls & OHVD soffit - up to CH8924		
TC1030	WB TSS - Fire Board Gantries dismantling	8	25-Mar-26	02-Apr-26	WB TSS - Fire Board Gantries dismantling		
Defect		46	14-Feb-26	01-Apr-26			
TC11610	WB TSS - inspection before black paint & E&M bracket CP26 to C	7	14-Feb-26	20-Feb-26	WB TSS - inspection before black paint & E&M bracket CP26 to CP27		
TC11620	WB TSS - inspection before black paint & E&M bracket CP27 to C	7	28-Feb-26	06-Mar-26	WB TSS - inspection before black paint & E&M bracket CP27 to CP28		
TC11630	WB TSS - inspection before black paint & E&M bracket CP28 to C	7	18-Mar-26	25-Mar-26	WB TSS - inspection before black paint & E&M bracket CP28 to CP29		
TC11640	WB TSS - inspection before black paint & E&M bracket CP29 to C	7	25-Mar-26	01-Apr-26	WB TSS - inspection before black paint & E&M bracket CP29 to CP29.		
WB TSS - Road Barrier		25	04-Mar-26	29-Mar-26			
Road Barriers After TBM1 Dismantling		25	04-Mar-26	29-Mar-26			
A229450740	WB TSS - Road Barrier up to CP29	7	04-Mar-26	11-Mar-26	WB TSS - Road Barrier up to CP29		
TC11220	WB TSS - Road Barrier up to CP30	4	12-Mar-26	16-Mar-26	WB TSS - Road Barrier up to CP30		
TC11230	WB TSS - Road Barrier up to CP30.5	4	16-Mar-26	20-Mar-26	WB TSS - Road Barrier up to CP30.5		
TC11670	WB TSS - Road Barrier from CP30.5 to CP31	4	20-Mar-26	24-Mar-26	WB TSS - Road Barrier from CP30.5 to CP31		
TC1285	WB TSS - Road Barrier from CP31 to endwall	5	24-Mar-26	29-Mar-26	WB TSS - Road Barrier from CP31 to endwall		
WB TSS - E&M Brackets		278	02-Jul-25 A	06-Apr-26			
E&M Brackets Installation Before TBM1 Dismantling		216	02-Jul-25 A	02-Feb-26			
CPS		216	02-Jul-25 A	02-Feb-26			
TC11030	WB TSS - E&M Brackets up to CP26	216	02-Jul-25 A	02-Feb-26	WB TSS - E&M Brackets up to CP26		
E&M Brackets Installation After TBM1 Dismantling		51	14-Feb-26	06-Apr-26			
CPS		48	14-Feb-26	03-Apr-26			
TC11040	WB TSS Final - E&M Brackets from CP26 to CP27 (CPS)	10	14-Feb-26	23-Feb-26	WB TSS Final - E&M Brackets from CP26 to CP27 (CPS)		
TC11050	WB TSS Final - E&M Brackets from CP27 to CP28 (CPS)	10	28-Feb-26	09-Mar-26	WB TSS Final - E&M Brackets from CP27 to CP28 (CPS)		
TC1380	WB TSS Final - E&M Brackets from CP28 to CP29 (CPS)	3	18-Mar-26	21-Mar-26	WB TSS Final - E&M Brackets from CP28 to CP29 (CPS)		
TC1400	WB TSS Final - E&M Brackets from CP29 to CP30 (CPS)	3	25-Mar-26	28-Mar-26	WB TSS Final - E&M Brackets from CP29 to CP30 (CPS)		
TC1410	WB TSS Final - E&M Brackets from CP30 to CP31 (CPS)	3	28-Mar-26	31-Mar-26	WB TSS Final - E&M Brackets from CP30 to CP31 (CPS)		
TC11550	WB TSS - E&M Bracket (last few rings) (CPS)	3	31-Mar-26	03-Apr-26	WB TSS - E&M Bracket (last few rings) (CPS)		
NCPS		41	24-Feb-26	06-Apr-26			
TC11760	WB TSS Final - E&M Brackets from CP26 to CP27 (NCPS)	10	24-Feb-26	05-Mar-26	WB TSS Final - E&M Brackets from CP26 to CP27 (NCPS)		
TC11770	WB TSS Final - E&M Brackets from CP27 to CP28 (NCPS)	10	10-Mar-26	19-Mar-26	WB TSS Final - E&M Brackets from CP27 to CP28 (NCPS)		
TC11780	WB TSS Final - E&M Brackets from CP28 to CP29 (NCPS)	3	21-Mar-26	24-Mar-26	WB TSS Final - E&M Brackets from CP28 to CP29 (NCPS)		
TC11790	WB TSS Final - E&M Brackets from CP29 to CP30 (NCPS)	3	28-Mar-26	31-Mar-26	WB TSS Final - E&M Brackets from CP29 to CP30 (NCPS)		
TC11800	WB TSS Final - E&M Brackets from CP30 to CP31 (NCPS)	3	31-Mar-26	03-Apr-26	WB TSS Final - E&M Brackets from CP30 to CP31 (NCPS)		
TC11810	WB TSS - E&M Bracket (last few rings) (NCPS)	3	03-Apr-26	06-Apr-26	WB TSS - E&M Bracket (last few rings) (NCPS)		
WB TSS - Black paint		8	01-Apr-26	09-Apr-26			
After TBM1 Dismantling		8	01-Apr-26	09-Apr-26			
TC1490	WB TSS - Black paint from CP26 to CP30	4	01-Apr-26	05-Apr-26	WB TSS - Black paint from CP26 to CP30		
TC11590	WB TSS - Black paint from CP30 to CP31	4	05-Apr-26	09-Apr-26	WB TSS - Black paint from CP30 to CP31		
WB TSS - Below Road Level Installation		88	31-Jan-26	29-Apr-26			
Service Gallery Civil Provision		48	31-Jan-26	19-Mar-26			
TC1100	WB TSS - Service Gallery Civil Provision from CP27.9 (R974) to R	30	31-Jan-26	01-Mar-26	WB TSS - Service Gallery Civil Provision from CP27.9 (R974) to R1081 (CP30.1)		
TC1140	WB TSS - Service Gallery Civil Provision from R1087 to R1135	18	04-Feb-26	22-Feb-26	WB TSS - Service Gallery Civil Provision from R1087 to R1135		
TC1130	WB TSS - Service Gallery Civil Provision from R1082 to R1086	18	02-Mar-26	19-Mar-26	WB TSS - Service Gallery Civil Provision from R1082 to R1086		
MiMEP		36	31-Jan-26	07-Mar-26			
TC11310	WB TSS - Service Gallery MiMEP from R974 (CP27.9) to CP29	18	31-Jan-26	17-Feb-26	WB TSS - Service Gallery MiMEP from R974 (CP27.9) to CP29		
TC1160	WB TSS - Service Gallery MiMEP from CP29 (R1026) to R1081 (C	6	18-Feb-26	23-Feb-26	WB TSS - Service Gallery MiMEP from CP29 (R1026) to R1081 (CP30.1)		
TC1170	WB TSS - Service Gallery MiMEP from R1082 to R1086	6	24-Feb-26	01-Mar-26	WB TSS - Service Gallery MiMEP from R1082 to R1086		
TC1180	WB TSS - Service Gallery MiMEP from R1087 to R1135	6	02-Mar-26	07-Mar-26	WB TSS - Service Gallery MiMEP from R1087 to R1135		
FS Control Room		21	04-Feb-26	25-Feb-26			

- ◆ Milestones
- Planned Bar
- Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Feb26-Apr26)



Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish	2026		
					Feb	Mar	Apr
TC920	WB TSS - FS Control Room Construction	21	04-Feb-26	25-Feb-26	WB TSS - FS Control Room Construction		
Low Point @ CP27		45	15-Mar-26	29-Apr-26			
TC910	WB TBM Tunnel - Cast In-situ Low Point Sump Pit construction (at	27	15-Mar-26	11-Apr-26	WB TBM Tunnel - Cast In-situ Low Point Sump Pit construction		
TC1450	WB TBM Tunnel - Low Point Sump Pit waterproofing & testing	18	11-Apr-26	29-Apr-26	WB TBM Tunnel - Low Point Sump Pit waterproofing & testing		
WB TSS - TCSS Civil provision at OHVD soffit		56	24-Feb-26	21-Apr-26			
After TBM1 Dismantling		56	24-Feb-26	21-Apr-26			
TC11650	WB TSS Final - TCSS Civil provision from CP26 to CP27	7	24-Feb-26	02-Mar-26	WB TSS Final - TCSS Civil provision from CP26 to CP27		
TC1570	WB TSS Final - TCSS Civil provision from CP27 to CP28	7	10-Mar-26	16-Mar-26	WB TSS Final - TCSS Civil provision from CP27 to CP28		
TC11660	WB TSS Final - TCSS Civil provision from CP28 to CP29	7	25-Mar-26	01-Apr-26	WB TSS Final - TCSS Civil provision from CP28 to CP29		
TC1590	WB TSS Final - TCSS Civil provision from CP29 to CP30	7	01-Apr-26	08-Apr-26	WB TSS Final - TCSS Civil provision from CP29 to CP30		
TC1560	WB TSS Final - TCSS Civil provision from CP30 to CP31	7	08-Apr-26	15-Apr-26	WB TSS Final - TCSS Civil provision from CP30 to CP31		
TC11570	WB TSS - TCSS Civil provision at OHVD soffit up to endwall (last 1	6	15-Apr-26	21-Apr-26	WB TSS - TCSS Civil provision at OHVD soffit up to endwall (last 1		
Eastbound (EB)		526	17-Feb-25 A	27-Jul-26			
EB TSS - TBM Slurry Pipes & Temporary Services		75	21-Feb-26	06-May-26			
Pipe dismantling & relocation after TBM2 Breakthrough		75	21-Feb-26	06-May-26			
CP22 to Back of TBM		21	21-Feb-26	13-Mar-26			
A229447750	TSS - EB NCPS Wall Pipe Dismantling from CP22 to CP27 (back of	21	21-Feb-26	13-Mar-26	TSS - EB NCPS Wall Pipe Dismantling from CP22 to CP27 (back of TBM dismantling area)		
CP7 to CP22		54	14-Mar-26	06-May-26			
A229447730	TSS - EB NCPS Wall Pipe Dismantling from FT to CP22	54	14-Mar-26	06-May-26	TSS - EB NCPS Wall Pipe Dismantling from FT to CP22		
EB TSS - Civil Works Before TBM2 Dismantled		93	31-Jan-26	03-May-26			
Gallery Installation Before TBM2 Dismantled		18	14-Apr-26	01-May-26			
TC0010	EB TSS - Service Gallery R948 to R978 (Up to pulling chair)	5	14-Apr-26	18-Apr-26	EB TSS - Service Gallery R948 to R978 (Up to pulling chair)		
TC0020	EB TSS - Service Gallery R979 to R1020 (Up to sliding rail)	12	20-Apr-26	01-May-26	EB TSS - Service Gallery R979 to R1020 (Up to sliding rail)		
Corbel Construction Before TBM2 Dismantled		93	31-Jan-26	03-May-26			
A229415962	EB TSS - Corbel Structure up to CP25	15	31-Jan-26	14-Feb-26	EB TSS - Corbel Structure up to CP25		
A229415972	EB TSS - Corbel Structure up to CP26	15	15-Feb-26	01-Mar-26	EB TSS - Corbel Structure up to CP26		
TC210	EB TSS Final - Corbel Structure from CP26 to CP27	15	15-Mar-26	30-Mar-26	EB TSS Final - Corbel Structure from CP26 to CP27		
TC220	EB TSS Final - Corbel Structure from CP27 (R930) to R954	15	19-Apr-26	03-May-26	EB TSS Final - Corbel Structure from CP27 (R930) to R954		
OHVD installation Before TBM2 Dismantled		47	14-Mar-26	29-Apr-26			
TC350	EB TSS - OHVD up to CP27 (R930)	15	15-Apr-26	29-Apr-26	EB TSS - OHVD up to CP27 (R930)		
CP21-26		20	14-Mar-26	03-Apr-26			
TC320	EB TSS - OHVD up to CP24	4	14-Mar-26	17-Mar-26	EB TSS - OHVD up to CP24		
TC330	EB TSS - OHVD up to CP25	4	18-Mar-26	21-Mar-26	EB TSS - OHVD up to CP25		
TC340	EB TSS - OHVD up to CP26	4	30-Mar-26	03-Apr-26	EB TSS - OHVD up to CP26		
Fire Board (Crown) Installation Before TBM2 Dismantled		32	14-Mar-26	14-Apr-26			
D12585	EB TSS - Fire board (Crown) up to CP24	8	14-Mar-26	21-Mar-26	EB TSS - Fire board (Crown) up to CP24		
D12595	EB TSS - Fire board (Crown) up to CP25	8	22-Mar-26	29-Mar-26	EB TSS - Fire board (Crown) up to CP25		
D12605	EB TSS - Fire board (Crown) up to CP26	8	30-Mar-26	06-Apr-26	EB TSS - Fire board (Crown) up to CP26		
D12615	EB TSS - Fire board (Crown) up to CP27 (R930)	8	07-Apr-26	14-Apr-26	EB TSS - Fire board (Crown) up to CP27 (R930)		
Fire Board (Road Level) Installation Before TBM2 Dismantled		51	14-Mar-26	03-May-26			
TC420	EB TSS - Fire Board - Walls & OHVD Soffit up to CP24	11	14-Mar-26	24-Mar-26	EB TSS - Fire Board - Walls & OHVD Soffit up to CP24		
TC430	EB TSS - Fire Board - Walls & OHVD Soffit up to CP25	11	25-Mar-26	04-Apr-26	EB TSS - Fire Board - Walls & OHVD Soffit up to CP25		
TC440	EB TSS - Fire Board - Walls & OHVD Soffit up to CP26	11	05-Apr-26	15-Apr-26	EB TSS - Fire Board - Walls & OHVD Soffit up to CP26		
TC450	EB TSS - Fire Board - Walls & OHVD Soffit up to CP27	11	16-Apr-26	26-Apr-26	EB TSS - Fire Board - Walls & OHVD Soffit up to CP27		
TC11740	EB TSS - inspection before black paint & E&M bracket CP25 to Cf	7	16-Apr-26	22-Apr-26	EB TSS - inspection before black paint & E&M bracket CP25 to Cf		
TC11710	EB TSS - inspection before black paint & E&M bracket CP26 to Cf	7	27-Apr-26	03-May-26	EB TSS - inspection before black paint & E&M bracket CP26 to Cf		
Road Barriers Before TBM2 Dismantled		21	14-Mar-26	04-Apr-26			
TC10160	EB TSS - Road Barrier up to CP25	5	14-Mar-26	18-Mar-26	EB TSS - Road Barrier up to CP25		
TC10170	EB TSS - Road Barrier up to CP26	5	19-Mar-26	23-Mar-26	EB TSS - Road Barrier up to CP26		
TC10180	EB TSS - Road Barrier up to CP27 (R930)	5	30-Mar-26	04-Apr-26	EB TSS - Road Barrier up to CP27 (R930)		
E&M Brackets Installation Before TBM2 Dismantled		46	18-Mar-26	02-May-26			

- ◆ Milestones
- Planned Bar
- Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Feb26-Apr26)



Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish	2026		
					Feb	Mar	Apr
TC620	EB - TBM Tunnel - E&M Bracket from CP22 to CP23	6	18-Mar-26	23-Mar-26			EB - TBM Tunnel - E&M Bracket from CP22 to CP23
TC630	EB - TBM Tunnel - E&M Bracket up to CP24	6	25-Mar-26	30-Mar-26			EB - TBM Tunnel - E&M Bracket up to CP24
TC640	EB - TBM Tunnel - E&M Bracket up to CP25	6	05-Apr-26	10-Apr-26			EB - TBM Tunnel - E&M Bracket up to CP25
TC650	EB - TBM Tunnel - E&M Bracket up to CP26	6	16-Apr-26	21-Apr-26			EB - TBM Tunnel - E&M Bracket up to CP26
TC660	EB - TBM Tunnel - E&M Bracket up to CP27 (R930)	6	27-Apr-26	02-May-26			EB - TBM Tunnel - E&M Bracket up to CP27 (R930)
EB TSS - Civil Works After TBM2 Dismantled		94	25-Apr-26	27-Jul-26			
EB TSS - Remaining Civil Works Summary		94	25-Apr-26	27-Jul-26			
TA1361	Summary - EB TSS Remaining Civil Works (TC0040-TC11690)	94	25-Apr-26	27-Jul-26			
EB TSS - Service Gallery		5	25-Apr-26	29-Apr-26			
Gallery Installation After TBM2 Dismantling		5	25-Apr-26	29-Apr-26			
TC0040	Sliding Rail demobilisation	5	25-Apr-26	29-Apr-26			
EB TSS - Below Road Level Installation		453	17-Feb-25 A	15-May-26			
CP26-30 MiMEP		12	31-Jan-26	11-Feb-26			
TC11080	EB TSS - Service Gallery MiMEP up to CP26 R885	6	31-Jan-26	05-Feb-26			EB TSS - Service Gallery MiMEP up to CP26 R885
TC11100	EB TSS - Service Gallery MiMEP up to CP27 R930	6	06-Feb-26	11-Feb-26			EB TSS - Service Gallery MiMEP up to CP27 R930
Low Point Sump Pit		453	17-Feb-25 A	15-May-26			
Low Point@CP12		376	17-Feb-25 A	27-Feb-26			
TC11330	EB TSS - Low Point Sump Pit waterproofing & testing (after TBM c	376	17-Feb-25 A	27-Feb-26			EB TSS - Low Point Sump Pit waterproofing & testing (after TBM dismantling)
CP27		27	19-Apr-26	15-May-26			
TC060	EB TSS - Cast In-situ Low Point Sump Pit construction	27	19-Apr-26	15-May-26			
FSIRoom		21	06-Feb-26	26-Feb-26			
TC070	EB TSS - FSI Room 9 - civil works	21	06-Feb-26	26-Feb-26			EB TSS - FSI Room 9 - civil works
EB TSS - TCSS Civil provision at OHVD soffit		40	25-Mar-26	03-May-26			
TC800	EB - TBM Tunnel - TCSS Civil provision at OHVD soffit up to CP23	7	25-Mar-26	31-Mar-26			EB - TBM Tunnel - TCSS Civil provision at OHVD soffit up to CP23
TC810	EB - TBM Tunnel - TCSS Civil provision at OHVD soffit up to CP24	7	01-Apr-26	07-Apr-26			EB - TBM Tunnel - TCSS Civil provision at OHVD soffit up to CP24
TC820	EB - TBM Tunnel - TCSS Civil provision at OHVD soffit up to CP25	7	05-Apr-26	11-Apr-26			EB - TBM Tunnel - TCSS Civil provision at OHVD soffit up to CP25
TC830	EB - TBM Tunnel - TCSS Civil provision at OHVD soffit up to CP26	7	16-Apr-26	22-Apr-26			EB - TBM Tunnel - TCSS Civil provision at OHVD soffit up to CP26
TC840	EB - TBM Tunnel - TCSS Civil provision at OHVD soffit up to CP27	7	27-Apr-26	03-May-26			EB - TBM Tunnel - TCSS Civil provision at OHVD soffit up to CP27
08 CKL Tunnel		72	20-Jan-26 A	01-Apr-26			
Westbound (WB)		72	20-Jan-26 A	01-Apr-26			
WB CKL - After TBM breakthrough		72	20-Jan-26 A	01-Apr-26			
WB CKL Remaining Civil Works Summary		72	20-Jan-26 A	01-Apr-26			
TA335	Summary - WB CKL Remaining Civil Works (TB1090-TC1380)	72	20-Jan-26 A	01-Apr-26			Summary - WB CKL Remaining Civil Works (TB1090-TC1380)
Westbound (WB) Final Civil Works		62	28-Jan-26 A	30-Mar-26			
Service Gallery		16	28-Jan-26 A	12-Feb-26			
TB1120	WB - In-situ SG at End Wall (4m)	12	28-Jan-26 A	08-Feb-26			WB - In-situ SG at End Wall (4m)
TB1180	WB - Drainage & Road Slab	4	09-Feb-26	12-Feb-26			WB - Drainage & Road Slab
OHVD		24	13-Feb-26	08-Mar-26			
TB1200	WB - OHVD Formwork Erection	6	13-Feb-26	18-Feb-26			WB - OHVD Formwork Erection
TB1230	WB - Type A2 OHVD (1 bays, 4d.bay)	4	19-Feb-26	22-Feb-26			WB - Type A2 OHVD (1 bays, 4d.bay)
TB1260	WB - Type A2 OHVD (2 bays, 4d.bay)	8	23-Feb-26	02-Mar-26			WB - Type A2 OHVD (2 bays, 4d.bay)
TB1290	WB - Type A2 OHVD Formwork Dismantling	6	03-Mar-26	08-Mar-26			WB - Type A2 OHVD Formwork Dismantling
Barrier		3	09-Mar-26	11-Mar-26			
TB1320	WB - Type A Dr&Br - Remaining Parapet	3	09-Mar-26	11-Mar-26			WB - Type A Dr&Br - Remaining Parapet
E&M Brackets & Black paint		7	24-Mar-26	30-Mar-26			
TB1310	WB - Type A Dr&Br - Remaining Bracket	3	24-Mar-26	26-Mar-26			WB - Type A Dr&Br - Remaining Bracket
TB1340	WB - Defect Rectification and HyD inspection, Black paint	2	29-Mar-26	30-Mar-26			WB - Defect Rectification and HyD inspection, Black paint
WB End Wall Civil & Structure Works		48	13-Feb-26	01-Apr-26			
TB1150	WB - End Wall Kicker & Wall	25	13-Feb-26	09-Mar-26			WB - End Wall Kicker & Wall
TB1220	WB - End Wall Corbel Construction	5	10-Mar-26	14-Mar-26			WB - End Wall Corbel Construction
TB1240	WB - End Wall Parapet (2 nos)	3	15-Mar-26	17-Mar-26			WB - End Wall Parapet (2 nos)

- ◆ Milestones
- Planned Bar
- Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Feb26-Apr26)



Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish	2026		
					Feb	Mar	Apr
TB1270	WB - End Wall Temporary L-frame Construction	1	18-Mar-26	18-Mar-26			WB - End Wall Temporary L-frame Construction
TB1250	WB - End Wall Crown Falsework Erection	5	19-Mar-26	23-Mar-26			WB - End Wall Crown Falsework Erection
TB1280	WB - End Wall E&M Bracket	3	24-Mar-26	26-Mar-26			WB - End Wall E&M Bracket
TB1300	WB - End Wall Crown Concreting & Falsework Removal	5	24-Mar-26	28-Mar-26			WB - End Wall Crown Concreting & Falsework Removal
TB1380	WB - End Wall Transition OHVD	4	29-Mar-26	01-Apr-26			WB - End Wall Transition OHVD
WB TCSS Civil Provision		3	27-Mar-26	29-Mar-26			
TB1350	WB - Type A Dr&Br - Remaining TCSS Civil Provision	3	27-Mar-26	29-Mar-26			WB - Type A Dr&Br - Remaining TCSS Civil Provision
09 Cross Passages		187	06-Nov-25 A	12-May-26			
Cross Passages @ TSS & CKL Tunnel (CP7 to CP33)		187	06-Nov-25 A	12-May-26			
CP25 by Mini TBM		112	06-Nov-25 A	25-Feb-26			
A8260	CP25 - Internal & Collar Structure & ABWF	98	06-Nov-25 A	11-Feb-26	CP25 - Internal & Collar Structure & ABWF		
A8280	CP25 - E&M Installation	14	12-Feb-26	25-Feb-26	CP25 - E&M Installation		
A8340	CP25 - EB Tym Remaining Civil Works (Fireboard, Black Paint & E	9	12-Feb-26	20-Feb-26	CP25 - EB Tym Remaining Civil Works (Fireboard, Black Paint & E&M Brackets)		
CP26 by Mini TBM		112	24-Dec-25 A	14-Apr-26			
A8270	CP26 - Internal & Collar Structure & ABWF	98	24-Dec-25 A	31-Mar-26			CP26 - Internal & Collar Structure & ABWF
A8300	CP26 - E&M Installation	14	01-Apr-26	14-Apr-26			CP26 - E&M Installation
A8370	CP26 - EB Tym Remaining Civil Works (Fireboard, Black Paint & E	9	01-Apr-26	09-Apr-26			CP26 - EB Tym Remaining Civil Works (Fireboard
CP27 by Mini TBM		119	07-Jan-26 A	05-May-26			
TD0300	CP27 - EB - Tympanum Civil works R0935E	32	07-Jan-26 A	08-Feb-26	CP27 - EB - Tympanum Civil works R0935E		
A7972	CP27 - Mobilisation	12	08-Feb-26	20-Feb-26	CP27 - Mobilisation		
TD1450	CP27 - EB - Tympanum Strength Gain	14	08-Feb-26	22-Feb-26	CP27 - EB - Tympanum Strength Gain		
A229450670	CP27 - CP TBM mining	6	22-Feb-26	28-Feb-26	CP27 - CP TBM mining		
A7982	Mini TBM Demo after last CP is mined	15	28-Feb-26	15-Mar-26	Mini TBM Demo after last CP is mined		
A229450680	CP27 - Lining Grouting	6	28-Feb-26	06-Mar-26	CP27 - Lining Grouting		
A8290	CP27 - Internal & Collar Structure & ABWF	60	06-Mar-26	05-May-26			
A8360	CP27 - EB Tympanum Remaining Civil Work (Fireboard, Black Pai	9	27-Apr-26	05-May-26			
CP28 by D&Br		112	13-Jan-26 A	04-May-26			
TD1290	CP28 - Remaining Lining/Collar structure	98	13-Jan-26 A	20-Apr-26			CP28 - Remaining Lin
TD1300	CP28 - E&M Installation	14	21-Apr-26	04-May-26			
TD1320	CP28 - WB Tympanum Remaining Civil Work (Fireboard, Black Pa	9	21-Apr-26	29-Apr-26			
CP29 by D&Br		115	15-Jan-26 A	09-May-26			
TD1490	CP29 - Excavation from WB (Part 2 subject to EB TBM progress)	28	15-Jan-26 A	11-Feb-26	CP29 - Excavation from WB (Part 2 subject to EB TBM progress)		
TD1351	CP29 - EB - Final Break-out	7	12-Feb-26	18-Feb-26	CP29 - EB - Final Break-out		
TD1380	CP29 - Remaining Lining/Collar structure	80	19-Feb-26	09-May-26			
CP30 Remaining Works		68	06-Feb-26	15-Apr-26			
CP30 remaining works		68	06-Feb-26	15-Apr-26			
TD1140	CP30 WB TSS - Sawcut & final breaking work CP30	18	06-Feb-26	24-Feb-26	CP30 WB TSS - Sawcut & final breaking work CP30		
TD1150	CP30 - Waterproofing	3	24-Feb-26	27-Feb-26	CP30 - Waterproofing		
TD1160	CP30 - Collar structure at WB TSS	16	27-Feb-26	15-Mar-26	CP30 - Collar structure at WB TSS		
TD1200	CP30 - Remaining lining structure	19	15-Mar-26	03-Apr-26			CP30 - Remaining lining structure
TD1210	CP30 - E&M Installation	12	03-Apr-26	15-Apr-26			CP30 - E&M Installation
CP31 Remaining Works		54	19-Mar-26	12-May-26			
CP31 remaining works		54	19-Mar-26	12-May-26			
TD1170	CP31 WB TSS - Sawcut & final breaking work CP31	18	19-Mar-26	06-Apr-26			CP31 WB TSS - Sawcut & final breaking work CP31
TD1180	CP31 - Waterproofing	3	06-Apr-26	09-Apr-26			CP31 - Waterproofing
TD1220	CP31 - Collar structure at WB TSS	14	09-Apr-26	23-Apr-26			CP31 - Collar s
TD1230	CP31 - Remaining lining structure	19	23-Apr-26	12-May-26			
10 East Ventilation Building - EVB		111	26-Jan-26 A	16-May-26			
EVB Remaining Works (TBC)		92	31-Jan-26	02-May-26			
Landscape works		92	31-Jan-26	02-May-26			
EVB1650	EVB - Hard Landscape - Above G/F	92	31-Jan-26	02-May-26			

- ◆ Milestones
- Planned Bar
- Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Feb26-Apr26)



Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish	2026		
					Feb	Mar	Apr
VO - Recovery Vehicle Base (RVB) Construction							
EVB1810	RVB - Rock Excavation & Site Formation	50	26-Jan-26 A	16-Mar-26	RVB - Rock Excavation & Site Formation		
EVB1630	RVB - Road & Drainage works (subject to TBMs dismantled)	31	17-Mar-26	16-Apr-26	RVB - Road & Drainage works		
EVB1685	RVB - Canopy Footings & Structure works	30	17-Apr-26	16-May-26			
11 Tunnel E&M Installation							
WB - E&M Works							
WB - HV Cabling & HV Power On							
TE1180	WB Tunnel - Permanent HV Cable laying (Final Section)	18	29-Mar-26	16-Apr-26	WB Tunnel - Permanent HV Cab		
TE1220	WB Tunnel - Final HV Power On Change Over	12	16-Apr-26	28-Apr-26	W		
WB - LV Cabling & LV Power On							
E&MC1190	WB SUS CP1 to CP12 - E&M Installation (Final Stage)	30	31-Jan-26	01-Mar-26	WB SUS CP1 to CP12 - E&M Installation (Final Stage)		
E&MC1070	WB TSS - CP16-19 E&M installation (Final Stage subject to CP25-	30	03-Feb-26	04-Mar-26	WB TSS - CP16-19 E&M installation (Final Stage subject to CP25-26 available)		
WB - Below Road Level E&M Installation							
MiMEP							
TC1240	WB TSS - Service Gallery MiMEP Connection up to CP29	6	18-Feb-26	23-Feb-26	WB TSS - Service Gallery MiMEP Connection up to CP29		
TC1250	WB TSS - Service Gallery MiMEP Connection up to R1081 (CP30.1)	6	24-Feb-26	01-Mar-26	WB TSS - Service Gallery MiMEP Connection up to R1081 (CP30.1)		
TC1260	WB TSS - Service Gallery MiMEP Connection up to R1086	6	02-Mar-26	07-Mar-26	WB TSS - Service Gallery MiMEP Connection up to R1086		
TC1290	WB TSS - Service Gallery MiMEP Connection up to R1135	6	08-Mar-26	13-Mar-26	WB TSS - Service Gallery MiMEP Connection up to R1135		
TF070	WB TSS - Service Gallery E&M Installation	18	14-Mar-26	31-Mar-26	WB TSS - Service Gallery E&M Installation		
FS Control Room							
TC950	WB TSS - FS Control Room E&M Installation	28	25-Feb-26	25-Mar-26	WB TSS - FS Control Room E&M Installation		
EB - E&M Works							
EB - LV Cabling & LV Power On							
E&MC1150	EB SUS to CP12 - E&M Installation (Final Stage)	30	31-Jan-26	01-Mar-26	EB SUS to CP12 - E&M Installation (Final Stage)		
E&MC1100	EB TSS - CP16-19 E&M installation (Final Stage subject to CP25-;	30	22-Apr-26	21-May-26			
EB - Below Road Level E&M Installation							
FS Room							
TC150	EB TBM Tunnel - FS Control Room E&M Installation	28	27-Feb-26	26-Mar-26	EB TBM Tunnel - FS Control Room E&M Installation		
12 Projectwide TCSS Installation							
WB - TCSS Installation							
TE1170	WB - TCSS Installation concurrent with E&M installation	705	12-Aug-24 A	17-Jul-26			
TF030	WB - TBM Tunnel - TCSS fibre cabling	418	20-Jan-25 A	13-Mar-26	WB - TBM Tunnel - TCSS fibre cabling		
TF040	WB - TBM Tunnel - TCSS Signage Installation	412	20-Jan-25 A	07-Mar-26	WB - TBM Tunnel - TCSS Signage Installation		
EB - TCSS Installation							
TE130	EB - TBM Tunnel - TSSC Fibre Cabling	563	20-Jan-25 A	06-Aug-26			
TE170	EB - TBM Tunnel - TSSC Sign Installation	538	20-Jan-25 A	11-Jul-26			
13 Projectwide Testing and Commissioning							
E&M T&C							
WB E&M T&C							
TF080	WB - TSS - Service Gallery MiMEP T&C	21	01-Apr-26	21-Apr-26	WB - TSS - Service		
VAC T&C							
WB VAC T&C							
TF050	WB - TBM Tunnel - VAC T&C	56	28-Apr-26	23-Jun-26			
14 Projectwide Final Works							
Cladding							
Eastbound							
Typical Subframe & Cladding							
EB CPS							
VE10220	VE Panel - EB SUS (CPS) 400m	67	19-Dec-25 A	23-Feb-26	VE Panel - EB SUS (CPS) 400m		
VE10280	VE Panel - EB TSS CP7-12 (CPS) 500m	24	26-Mar-26	18-Apr-26	VE Panel - EB TSS CP7-1		
EB NCPS							

- ◆ Milestones
- Planned Bar
- Actual Bar

ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Feb26-Apr26)



Date	Revision	Checked	Approved

Activity ID	Activity Name	Dur	Start	Finish	2026		
					Feb	Mar	Apr
VE10571	VE Panel - EB SUS (NCPS) 400m	24	24-Feb-26	19-Mar-26	VE Panel - EB SUS (NCPS) 400m		
Westbound		99	10-Jan-26 A	18-Apr-26			
Typical Subframe & Cladding		99	10-Jan-26 A	18-Apr-26			
WB CPS		89	10-Jan-26 A	08-Apr-26			
VE10021	VE Panel - WB SUS (CPS) 400m	75	10-Jan-26 A	25-Mar-26	VE Panel - WB SUS (CPS) 400m		
VE10060	VE Panel - WB TSS CP7-12 (CPS) 500m	24	02-Mar-26	25-Mar-26	VE Panel - WB TSS CP7-12 (CPS) 500m		
VE10080	VE Panel - WB TSS CP16-25 (CPS) 900m	35	05-Mar-26	08-Apr-26	VE Panel - WB TSS CP16-25 (CPS) 900m		
WB NCPS		45	05-Mar-26	18-Apr-26			
VE10731	VE Panel - WB TSS CP19-24 (NCPS) 500m	24	05-Mar-26*	28-Mar-26	VE Panel - WB TSS CP19-24 (NCPS) 500m		
VE10651	VE Panel - WB SUS (NCPS) 400m	24	26-Mar-26*	18-Apr-26	VE Panel - WB SUS (NCPS) 400m		
Pavement		111	04-Feb-26	26-May-26			
Westbound (SUS to CKL)		104	04-Feb-26	19-May-26			
PAV10010	Pavement - WB Initial Layers TSS LSCC/CP7 to CP16	21	04-Feb-26	25-Feb-26	Pavement - WB Initial Layers TSS LSCC/CP7 to CP16		
PAV10020	Pavement - WB Initial Layers TSS CP16 to CKL (include EVB RL)	21	28-Apr-26	19-May-26			
TKOLTT Interchange (Top Layer Only)		42	15-Apr-26	26-May-26			
PAV30000	Pavement - TKOLTT Interchange Top Layer	42	15-Apr-26*	26-May-26			
Infrastructure Works		404	01-Mar-25 A	08-Apr-26			
06 Road S20		12	31-Jan-26	13-Feb-26			
VO - Modification of Irrigation System at Charging Station Run-in		12	31-Jan-26	13-Feb-26			
A1070	S20 - Shrubs Reinstatement (Non Critical)	12	31-Jan-26	13-Feb-26	S20 - Shrubs Reinstatement (Non Critical)		
07 Road L10(N)		404	01-Mar-25 A	08-Apr-26			
L10(N) Landscape (KD-26)		26	05-Mar-26	08-Apr-26			
LN10110	L10(N) - Landscape softwork (TBC)	26	05-Mar-26	08-Apr-26	L10(N) - Landscape softwork (TBC)		
LN10120	KD-26 - Section 9D - Road L10 (N) Landscape Softworks	0		08-Apr-26	◆ KD-26 - Section 9D - Road L10 (N) Landscape Softworks		
L10 (N) Remaining Road Works (Subject to Manpower)		283	01-Mar-25 A	04-Mar-26			
A229450270	L10 (N) - Remaining Road Signage	283	01-Mar-25 A	04-Mar-26	L10 (N) - Remaining Road Signage		
08 Road L10(S) & L18		25	31-Jan-26	04-Mar-26			
L10(S) & L18 Landscape (KD-24)		25	31-Jan-26	04-Mar-26			
A229445710	L10 (S) & L18 - Landscape softwork (TBC)	25	31-Jan-26*	04-Mar-26	L10 (S) & L18 - Landscape softwork (TBC)		
A229445711	KD-24 - Completion of Section 9B - Remaining Stage 5 Infrastructure Landscape	0		04-Mar-26	◆ KD-24 - Completion of Section 9B - Remaining Stage 5 Infrastructure Landscape		

- ◆ Milestones
- Planned Bar
- Actual Bar


ED/2018/04 Trunk Road T2 and Infrastructure Works
for Developments at South Apron
Three Months Rolling Programme (Feb26-Apr26)



Date	Revision	Checked	Approved

CONTRACT NO. ED/2020/03
TRUNK ROAD T2
TRAFFIC CONTROL SURVEILLANCE SYSTEM AND ASSOCIATED WORKS
OVERALL PROJECT TIMELINE

Appendix III A - Overall Project Timeline

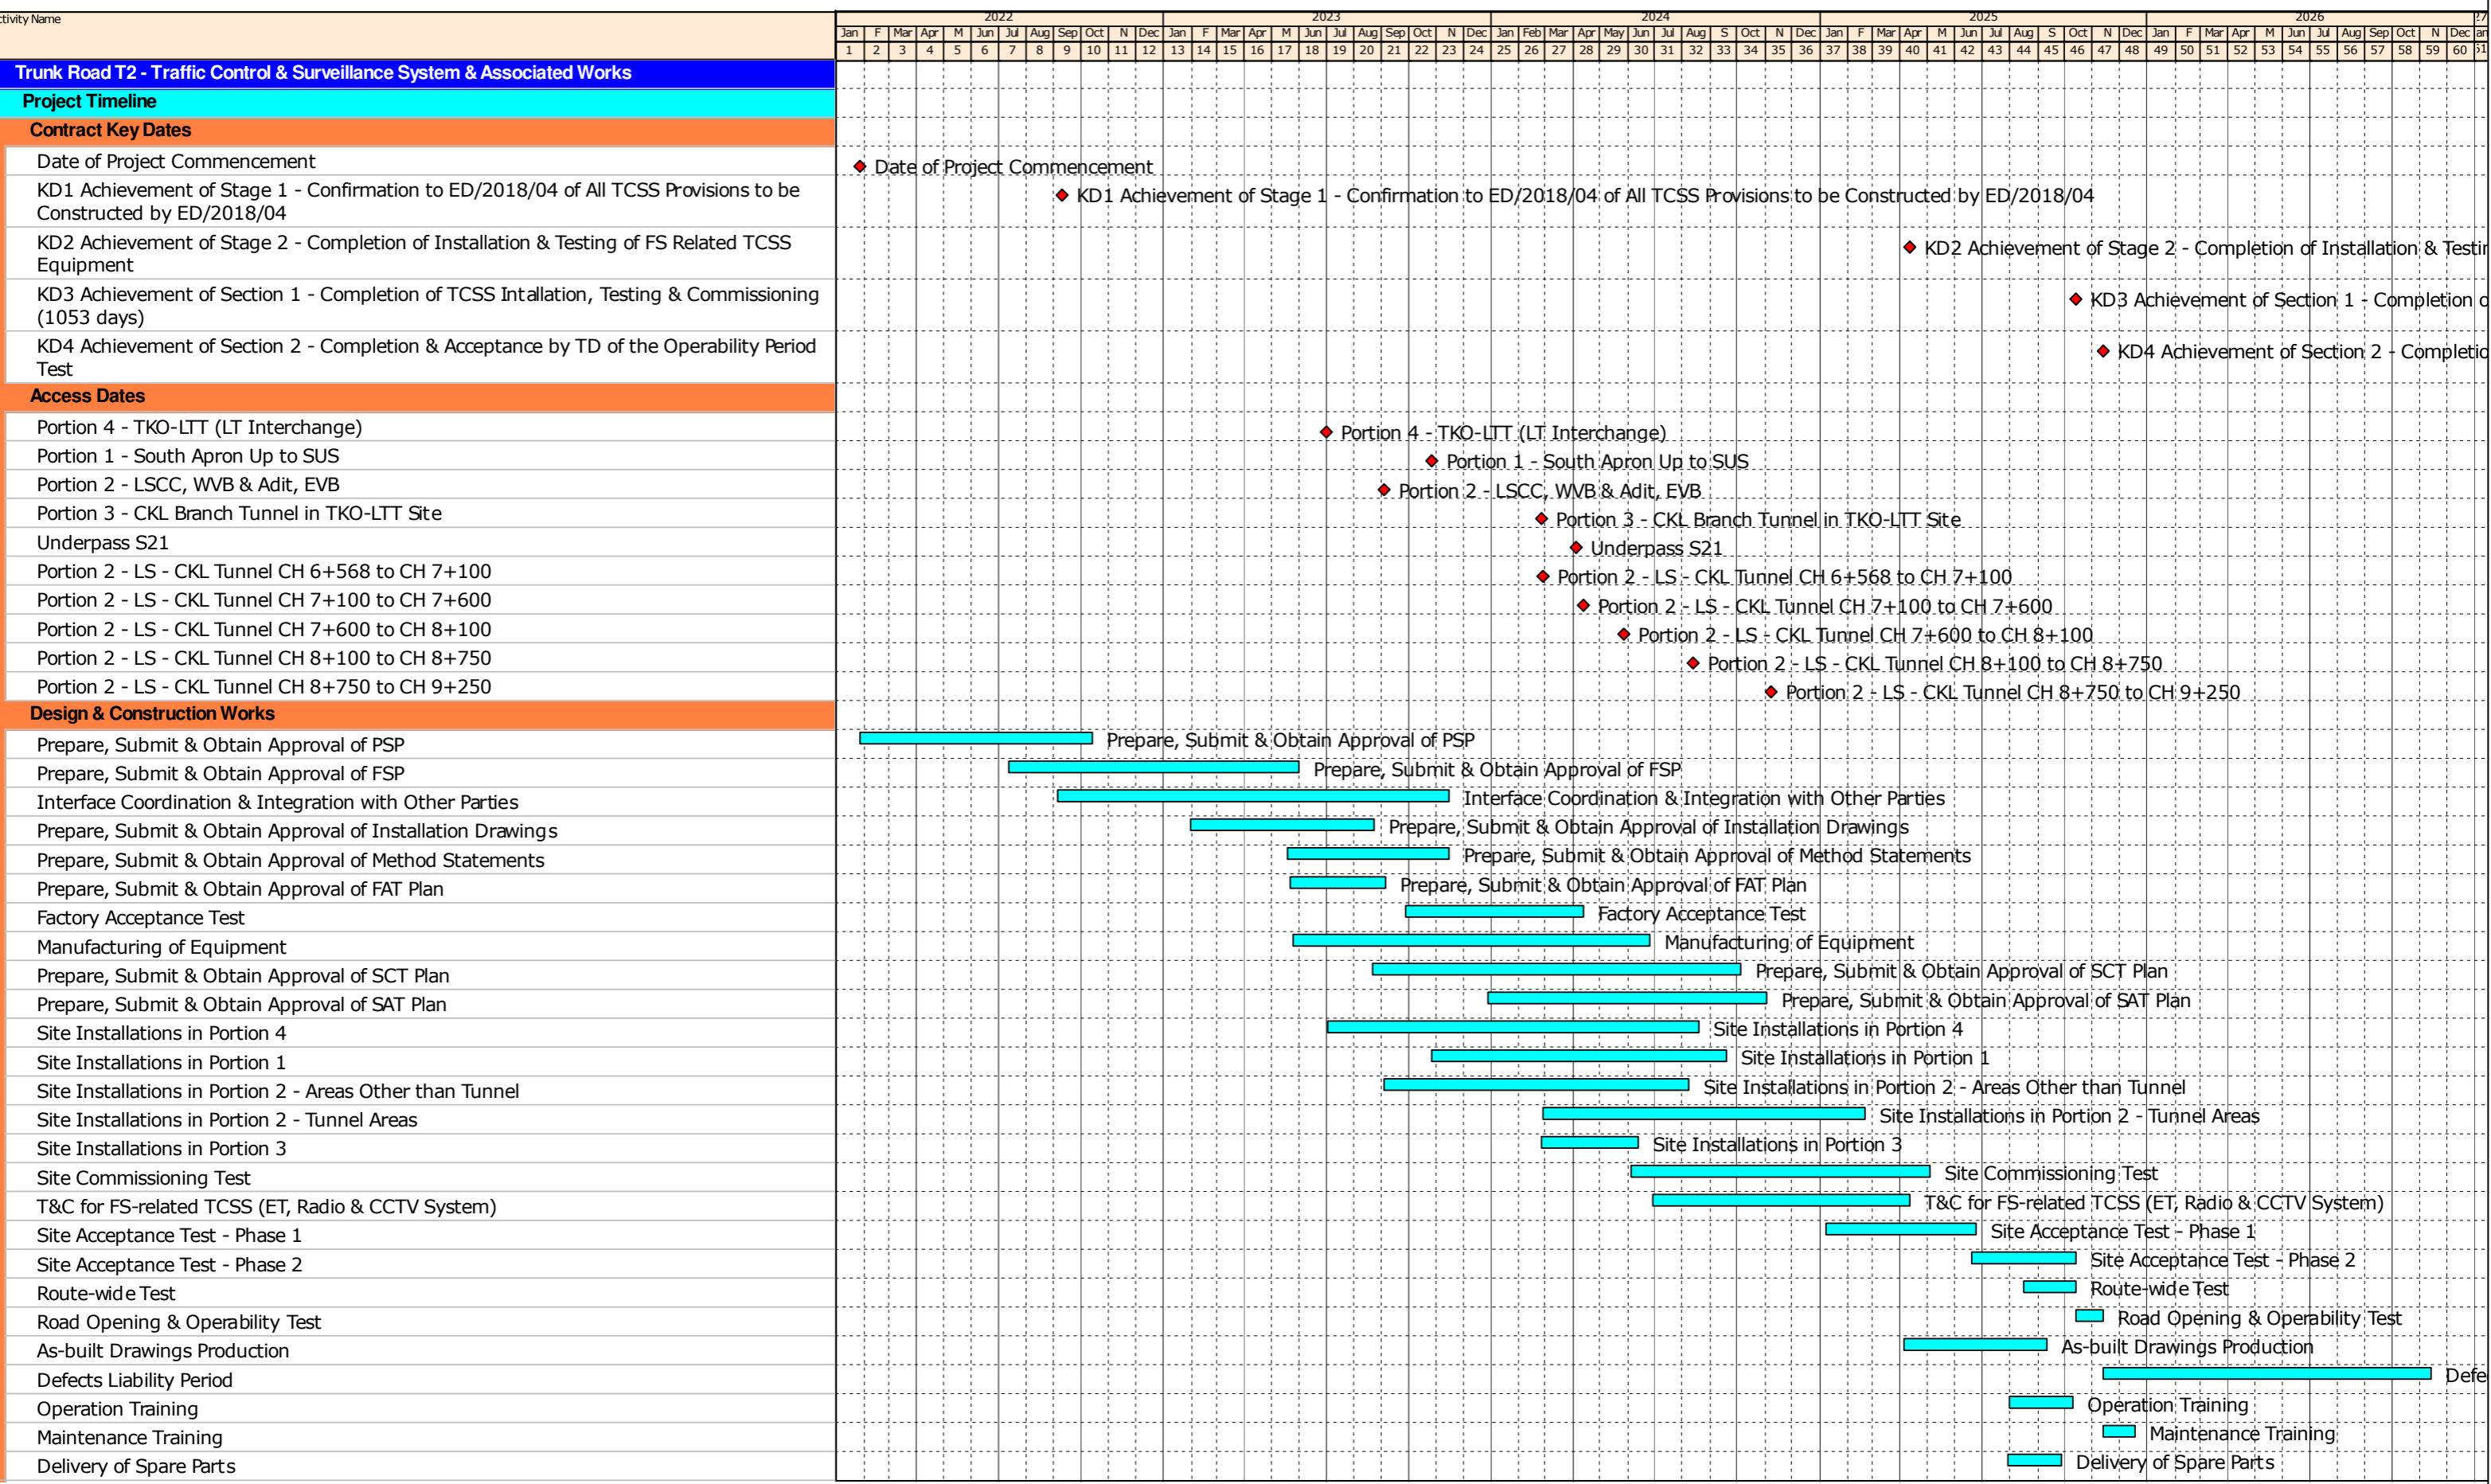

Date	Revision	Checked	Approved
14-Oct-22	Rev. B	FC	
05-Dec-22	Rev. C	FC	
18-Apr-23	Rev. D	FC	
