

Appendix H - Noise Monitoring Results

(0700-1900 hrs on Normal Weekdays)

Location CKL1 - Flat 121 Cha Kwo Ling Village							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
5-Jun-25	9:35	Fine	72.4	75.6	61.7	72.4	72.4 Measured \leq Baseline
11-Jun-25	15:38	Fine	72.0	74.8	59.4	72.4	72 Measured \leq Baseline
17-Jun-25	11:05	Fine	72.5	76.5	62.1	72.4	56
23-Jun-25	13:00	Sunny	71.9	76.2	57.1	72.4	71.9 Measured \leq Baseline



Location CKL2 - Flat 103 Cha Kwo Ling Village							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
5-Jun-25	10:10	Fine	72.1	74.8	61.4	71.4	64
11-Jun-25	10:20	Fine	73.3	76.9	62.8	71.4	69
17-Jun-25	11:35	Fine	75.8	79.9	62.9	71.4	74
23-Jun-25	13:35	Sunny	73.2	76.5	58.0	71.4	69

Location KTD1 - Centre of Excellence in Paediatrics (Rooftop of Children's Hospital)							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
5-Jun-25	12:40	Fine	64.1	65.0	63.3	78.0	64.1 Measured \leq Baseline
11-Jun-25	13:58	Fine	67.6	71.1	64.4	78.0	67.6 Measured \leq Baseline
17-Jun-25	14:26	Fine	69.8	71.1	66.0	78.0	69.8 Measured \leq Baseline
23-Jun-25	11:10	Sunny	66.8	68.5	64.6	78.0	66.8 Measured \leq Baseline

Location KER1 - Future Residential Development at Kerry Godown							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
5-Jun-25	11:50	Fine	73.0	75.2	68.2	65.0	72
11-Jun-25	9:00	Fine	73.5	75.7	67.6	65.0	73
17-Jun-25	13:29	Fine	71.0	73.7	65.6	65.0	70
23-Jun-25	11:55	Sunny	65.6	68.4	59.5	65.0	57


Location KTD2d - Next to the SOR Office of Trunk Road T2 in Kai Tak Area							
Date	Time	Weather	Unit: dB (A) (30-min)				
			Measured Noise Level			Baseline Level	Construction Noise Level
			L _{eq}	L ₁₀	L ₉₀	L _{eq}	L _{eq}
5-Jun-25	13:25	Fine	59.5	60.6	57.5	64.0	60 Measured \leq Baseline
11-Jun-25	16:12	Fine	63.1	64.8	60.2	64.0	63 Measured \leq Baseline
17-Jun-25	15:38	Fine	62.6	63.7	59.3	64.0	63 Measured \leq Baseline
23-Jun-25	10:20	Sunny	62.9	65.7	54.9	64.0	63 Measured \leq Baseline


Noise Levels

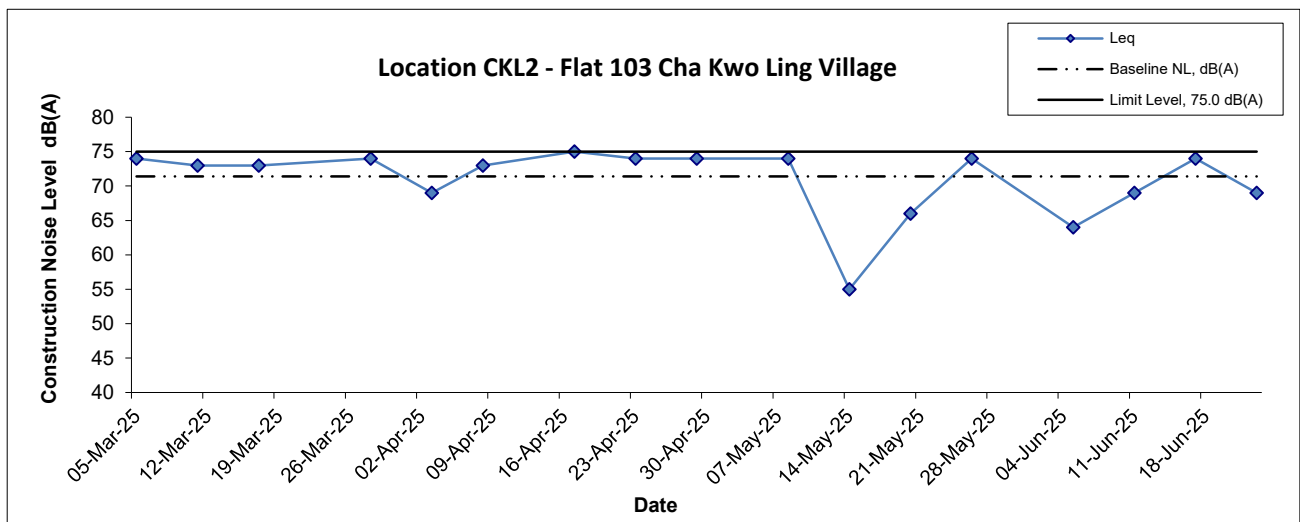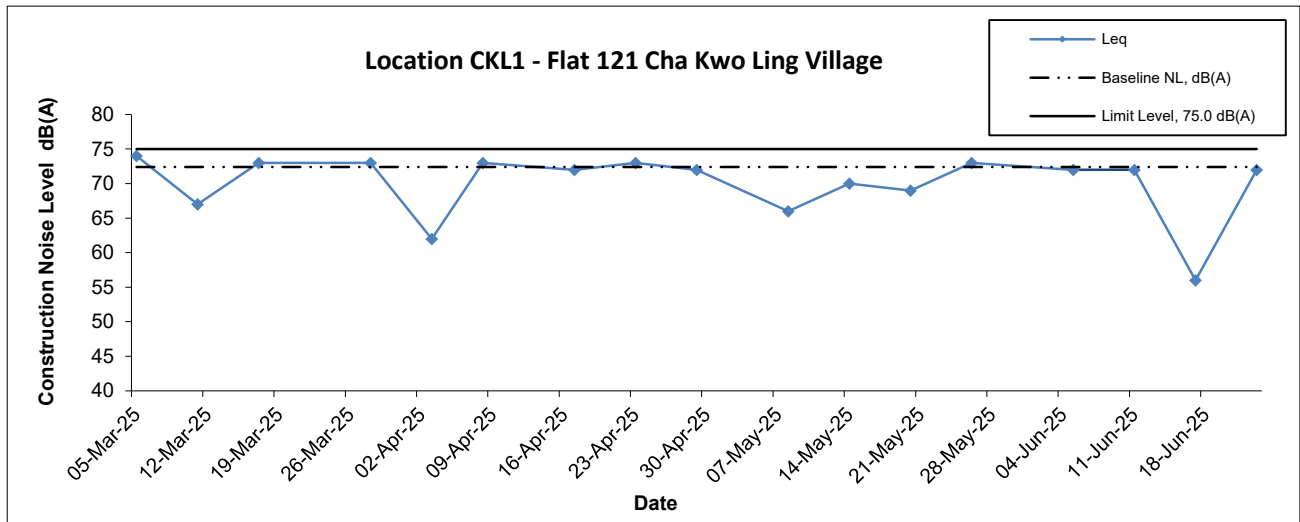

Title Kai Tak Development – Trunk Road T2 and Infrastructure Works at the Former South Apron Graphical Presentation of Construction Noise Monitoring Results	Date Jun 25	Project No. MA20003	
		Appendix H	

Noise Levels

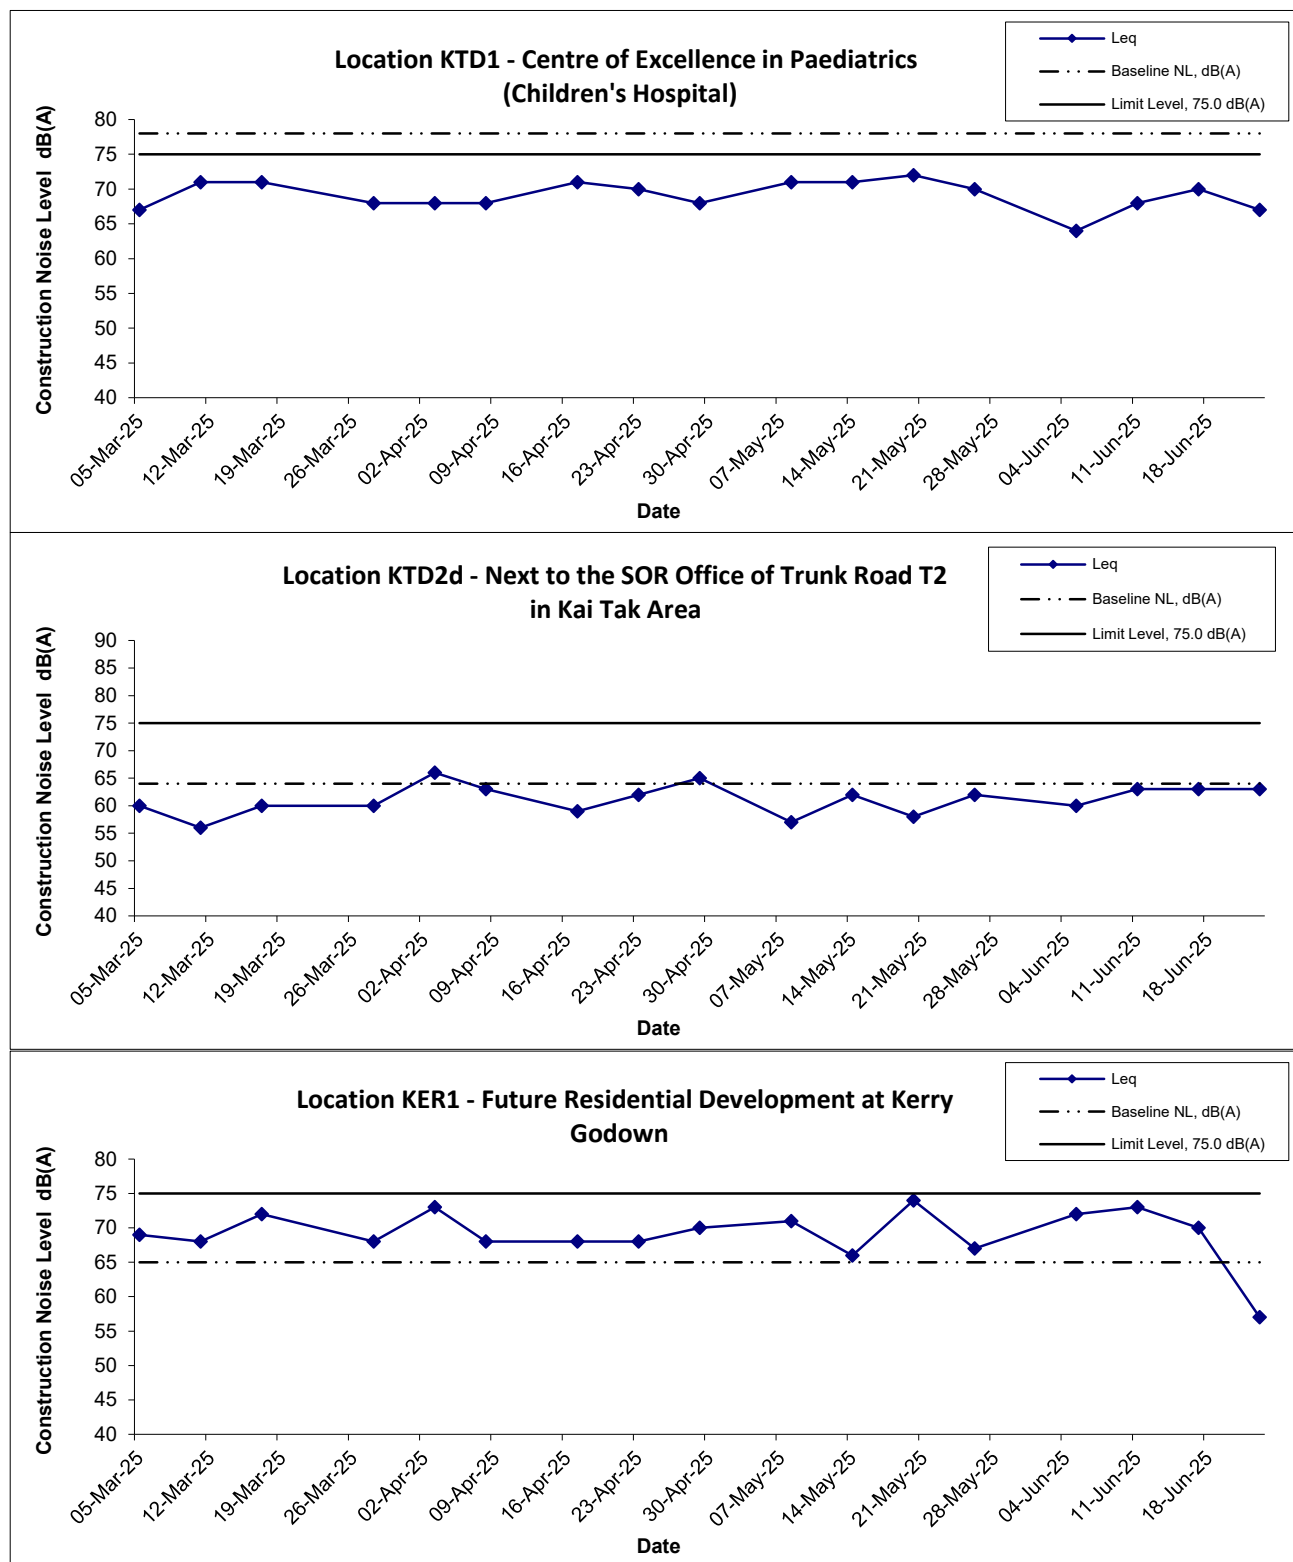

Title Kai Tak Development – Trunk Road T2 and Infrastructure Works at the Former South Apron Graphical Presentation of Construction Noise Monitoring Results	Date	Project	
	Jun 25	No. MA20003	
		Appendix H	
